

September 2026



Document details and history

Document details

Document title REHABILITATION MANAGEMENT PLAN ENV-RHB-PLN-001

File name 2608 Rehabilitation Management Plan

Document status and review

Edition	Comments	Author	Authorised by	Date
0	Required under the <i>Mining Regulation 2016</i>	James Bailey & Associates	A Williams	Jul 2022
1	Amendment	James Bailey & Associates	A Williams	Dec 2022
2	Amendment	James Bailey & Associates	A Williams	Mar 2023
3	Amendment	James Bailey & Associates	A Williams	Jul 2023
4	Amendment	James Bailey & Associates	L Tolson T McDermott	Jan 2024
5	Amendment	James Bailey & Associates	L Tolson T McDermott	Feb 2024
6	Amendment – Mod 8	James Bailey & Associates	L Tolson T McDermott	Jul 2024
7	Amendments to refer to grant of ML1883	Xenith	L Tolson	March 2025
8	Annual Review – align with updated Form and way	M Wright	S Torrance	September 2026

Disclaimer Document uncontrolled when printed

Table of contents

1	INTRODUCTION TO MINING PROJECT	8
1.1	History of Operations	8
1.2	Current Development Consents, Leases and Licences	10
1.3	Land Ownership and Land Use	12
1.3.1	Land Ownership and Land Use Figures	20
2	FINAL LAND USE	27
2.1	Regulatory Requirements for Rehabilitation	27
2.2	Final Land Use Options Assessment	38
2.3	Final Land Use Statement	38
2.4	Final Land Use and Mining Domains	39
2.4.1	Final Land Use Domains	39
2.4.2	Mining Domains	40
3	REHABILITATION RISK ASSESSMENT	41
4	REHABILITATION OBJECTIVES AND REHABILITATION COMPLETION CRITERIA	54
4.1	Rehabilitation Objectives and Rehabilitation Completion Criteria	54
4.2	Rehabilitation objectives and rehabilitation completion criteria – Stakeholder Consultation	75
5	FINAL LANDFORM AND REHABILITATION PLAN	79
6	REHABILITATION IMPLEMENTATION	81
6.1	Life of Mine Rehabilitation Schedule	81
6.2	Phases of Rehabilitation and General Methodologies	87
6.2.1	Active Mining Phase	88
6.2.2	Decommissioning	102
6.2.3	Landform Establishment	103
6.2.4	Growth Medium Development	107
6.2.5	Ecosystem and Land Use Establishment	110
6.2.6	Ecosystem and Land Use Development	112
6.3	Rehabilitation of Areas Affected by Subsidence	114
7	REHABILITATION QUALITY ASSURANCE PROCESS	115
8	REHABILITATION MONITORING PROGRAM	117
8.1	Analogue Site Baseline Monitoring	117
8.2	Rehabilitation Establishment Monitoring	121

8.3	Measuring Performance Against Rehabilitation Objectives and Rehabilitation Completion Criteria	122
9	REHABILITATION RESEARCH, MODELLING AND TRIALS	123
9.1	Current Rehabilitation Research, Modelling and Trials	123
9.2	Future Rehabilitation Research, Modelling and Trials	124
10	INTERVENTION AND ADAPTIVE MANAGEMENT	126
11	REVIEW, REVISION AND IMPLEMENTATION	138

List of figures

Figure 1-1:	Regional Locality	21
Figure 1-2:	Landownership	22
Figure 1-3:	Mining Leases and Exploration Licences	23
Figure 1-4:	Vegetation Communities.....	24
Figure 1-5:	Environmentally and Culturally Sensitive Areas	25
Figure 1-6:	Water Management System – 2021	26
Figure 5-1:	Final Landform and Rehabilitation Plan.....	80
Figure 6-1:	Mine Plan and Rehabilitation (December 2024).....	82
Figure 6-2:	Conceptual Staged Mine Plan Year 10 (Boggabri EA).....	83
Figure 6-3:	Conceptual Staged Mine Plan Year 21	84
Figure 6-4:	Conceptual Staged Mine Plan 2023 (MOD 8 Amendment).....	85
Figure 6-5:	Conceptual Staged Mine Plan 2027 (MOD 8 Amendment).....	86
Figure 6-6:	2020 – 2024 Exploration Program	101

List of tables

Table 1-1:	Summary of modifications to MP 09_0182.....	8
Table 1-2:	Summary of current consents, authorisations and licences	10
Table 1-3:	Schedule of Land Ownership.....	12
Table 1-4:	Land Occupancy	18
Table 2-1:	Relevant Approval Conditions	28
Table 2-2:	Final Land Use Domains	39
Table 2-3:	Mining Domains	40
Table 3-1:	Summary of Rehabilitation Risks and Controls	42
Table 4-1:	Rehabilitation Objectives and Proposed Completion Criteria.....	55
Table 4-2:	Summary of agency consultation undertaken over the life of the project.....	75
Table 4-3:	Stakeholder Expectations	76
Table 6-1:	Rehabilitation Phases	87
Table 6-2:	Unsuitable Subsoil and Spoil Parameters	89
Table 7-1:	Roles and Responsibilities for Implementation of the RMP	115
Table 8-1:	Vegetation Community Structures.....	119
Table 10-1:	Rehabilitation Trigger Action Response Plan	128

Appendices

Appendix A.1	Approved Rehabilitation Objectives Statement	142
--------------	--	-----

Summary table

Name of Mine	Boggabri Coal Mine
Rehabilitation Management Plan: Commencement Date	2 July 2022
Rehabilitation Management Plan: Revision Dates and Version Numbers	Version 8 revised August 2026
	Revision triggered by submission of Annual Review in March 2026.
Mining Leases / Exploration Licences (Authorisations)	ML 1755 – Expires 30 June 2038 ML 1883 – Expires 24 September 2045 CL 368 – Expires 14 November 2032 A355 – Expires 11 April 2028 A339 - Expired 11 April 2025 (Not being Renewed)
Name of Lease Holders	Boggabri Coal Pty Limited; NS Boggabri Pty Limited; and Chugoku Electric Power Australia Resources Pty Ltd

Document control

Distribution Control

Controlled copies will be distributed to and retained by relevant personnel including key Boggabri Coal Operations Pty Limited (BCOPL) agency and contractor representatives.

Company	Position
BCOPL	Environment Superintendent
BCOPL	Environment and Community Manager
BCOPL	General Manager
Resources Regulator	Inspector Environment

Uncontrolled Copies

Uncontrolled copies may be issued on the authority of the BCOPL Environment Superintendent. Such copies will neither be numbered nor kept up to date.

Author:	M. Wright – Environment Advisor
Reviewer:	Tim McDermott – Senior Environment Advisor
Approved by:	Sarah Torrance – Environmental Operations Superintendent
Signed:	Sarah Torrance
Date:	23/09/2026
Distribution:	BCOPL Website

1 INTRODUCTION TO MINING PROJECT

This Rehabilitation Management Plan (RMP) has been prepared for Boggabri Coal Mine (BCM) in accordance with the Mining Amendment (Standard Conditions of Mining Leases – Rehabilitation) Regulation 2021, the prescribed Form and Way: Rehabilitation Management Plan for Large Mines (NSW Resources Regulator, 2021), and Clause 9 of Schedule 8A of the Mining Regulation 2016. The RMP outlines the rehabilitation strategy, objectives, outcomes and completion criteria for the mine and supports the progressive rehabilitation of disturbed land.

1.1 History of Operations

BCM is an open cut coal mine located within the Gunnedah Basin, New South Wales (**Figure 1-1**). Mining development was approved in 1989, with Coal Lease 368 granted in 1990. Site construction commenced in 2006 and coal production began later that year.

Mining initially progressed through the Merriown and Jeralong pits before consolidating into the Bollol Creek pit. Progressive rehabilitation has been undertaken throughout the life of the operation, including rehabilitation of overburden emplacement areas and other disturbed land.

In 2012, development consent (MP 09_0182) was granted to extend mining operations, increase production capacity and construct additional mining and transport infrastructure, including rail loading facilities and a coal handling and preparation plant. The upgraded infrastructure was commissioned in 2014–2015, enabling product coal to be transported directly from the mine by rail.

BCM has modified the MP 09_0182 on nine occasions since it was issued in 2012. These are summarised in **Table 1-1** below. BCM currently operates under the relevant mining leases and development consents, with rehabilitation undertaken progressively in accordance with regulatory requirements and approved management plans.

BCM is proposed to re-establish a minimum of 1,508 ha of native vegetation communities consistent with the pre-mining environment. Progressive rehabilitation has been undertaken throughout the life of the mine. As at the end of 2024, approximately 362 ha of rehabilitation had been completed.

Table 1-1: Summary of modifications to MP 09_0182

Modification	Approval Date	Activities
MOD1	Application Withdrawn	Emergency trucking operations.
MOD 2	17 February 2015	- Processing of up to 3.5 Mtpa of ROM coal in the CHPP in any calendar year. - Infrastructure, processing, and associated transport of up to 3 Mtpa of ROM coal from Tarrawonga Coal Mine.
MOD 3	17 March 2014	- Construction of permanent mine access roads from the Kamilaroi Highway. - Temporary storage of processed mine overburden material at the existing Rock Quarry and the reuse of this material during the construction of the rail spur embankments. - The reuse of the existing Daisymede laydown compound. - The use of temporary in-pit fuel storage facilities.

Modification	Approval Date	Activities
MOD 4	23 March 2015	- Project boundary adjustments to include infrastructure and borrow pits built prior to the MP 09_0182. - Alterations to existing infrastructure within the BCM, including the extension of two dirty water dams (SD12 & SD3). - Realignment of a haul road, extension of the ROM coal stockpile and construction of new hardstand areas within the Mine Infrastructure Area. - Construction of a security fence and firebreak along the approved disturbance boundary. - Use of additional portable fuel storages within operational areas.
MOD 5	30 August 2016	Construction of additional groundwater production bores and supporting infrastructure including pumps, access roads, water tanks and power lines.
MOD 6	7 July 2017	Approval to transport a maximum of 10 Mtpa of product coal from site via the Boggabri Rail Spur, of which up to 8.6 million tonnes may be from the BCM and up to 3 million tonnes may be from the neighbouring Tarrawonga Coal Mine.
MOD 7	27 May 2019	- Amend the available security mechanisms and timing to secure biodiversity offsets. - Use of an approved stockpile area for BCM's product coal. - Undertake exploration and associated activities within the approved disturbance area. - Transport small tonnages of coal by road for testing and marketing purposes. - Realign a small section of the project boundary.
MOD 8	22 January 2024	- Increase the depth of approved mining operations to recover an additional coal resource. - Extend mine life by three years until the end of 2036
MOD 9	2 March 2023	- Operation of a mobile rock crushing plant within the existing BCM Disturbance Boundary. - Relocation of the Pre-shift Start-up Infrastructure closer to active mining operations. - Minor administrative changes relating to the management of rehabilitation activities to align with changes to the <i>Mining Regulation 2016</i>.
MOD 10	In Approval Process	- Continued mining operations beyond the approved Mine Disturbance Boundary, but within existing Project Boundary to recover an additional 30 Mt of ROM Coal. - Extend mine life by four years until the end of 2040.
MOD 11	19 July 2024	Extension to the Workshop and stores facilities.

1.2 Current Development Consents, Leases and Licences

BCM is considered a “Large Mine” in accordance with the definition under Schedule 8A of the *Mining Regulation 2016* as it has more than one mining lease and operates in accordance with an EPL which was issued in accordance with the *Protection of the Environment Operations Act 1997* (POEO Act).

Table 1-2 summarises the current consents, authorisations and licences that have been granted for BCM.

Table 1-2: Summary of current consents, authorisations and licences

Lease / Licence / Approval	Date Granted	Expiry / Duration
Exploration Licences / Authorisations		
Authorisation A355	19 July 1984	19 July 2028
Coal Leases / Mining Lease		
CL 368	15 November 1990	14 November 2032
ML 1755	30 June 2017	30 June 2038
ML 1883	24 September 2024	24 September 2045
Project Approvals / Development Consents		
Development Consent DA36-88	22 August 1989	15 November 2011
MOD 1	22 July 2009	15 November 2011
MOD 2	19 October 2011	31 December 2013
MP 09_0182	18 July 2012	31 December 2033
MOD1	Withdrawn	N/A
MOD2	17 February 2015	31 December 2033
MOD3	17 March 2014	31 December 2033
MOD4	23 March 2015	31 December 2033
MOD5	30 August 2016	31 December 2033
MOD6	7 July 2017	31 December 2033
MOD7	27 May 2019	31 December 2033
MOD8	22 January 2024	31 December 2036
MOD9	2 March 2023	31 December 2033
MOD 10	In Approval Process	
MOD 11	18 July 2024	31 December 2036
Other licences & Approvals		
EPBC Act Approval 2009/5256	11 February 2013	31 December 2053
EPBC Act Approval 2021/8875	19 December 2024	31 December 2053
EPL 12407 (as currently modified)	11 January 2006	-
Approval of Controlled Works Part 8 of the Water Act 1912 – Floodplain construction works for rail loop	01 October 2013	-

Lease / Licence / Approval	Date Granted	Expiry / Duration
Approval of Controlled Works Part 8 of the Water Act 1912 – Floodplain construction works for Kamilaroi Highway access road	5 June 2014	-
Water Licences		
Water Access Licence (WAL) 12691	31 May 2017	In perpetuity
WAL 12767	8 April 2014	In perpetuity
WAL 15037	12 December 2013	In perpetuity
WAL 24103	1 September 2011	In perpetuity
WAL 37519	14 June 2016	In perpetuity
WAL 37067	18 February 2015	In perpetuity
WAL 29473	26 July 2012	In perpetuity
WAL 29562	26 July 2012	In perpetuity
WAL 2571	12 December 2013	In perpetuity
WAL 2572	25 September 2013	In perpetuity
WAL 2595	12 December 2013	In perpetuity
WAL 2596	25 September 2013	In perpetuity
WAL 36547	6 February 2014	In perpetuity
WAL 44134	21 April 2022	In perpetuity
Rehabilitation Reforms		
Forward Works Program & Rehabilitation Cost Estimate	1 January	3 years
Rehabilitation Objectives	13 October 2023	-
Rehabilitation Completion Criteria	Proposed only	Not yet submitted for approval
Final Landform Rehabilitation Plan	March 2025	Not yet endorsed
Radiation Licences		
Licence No. 5083602	14 June 2017	Renewed Annually
Council Approvals		
CC 04-04-2012 Mod1	22 October 2012	In perpetuity
CC 02-03-2012	6 June 2012	In perpetuity
CC 10-01-2012 Mod1	1 June 2012	In perpetuity
OC 09-10-2013	19 November 2013	In perpetuity

Lease / Licence / Approval	Date Granted	Expiry / Duration
OC 02-04-2013	9 April 2013	In perpetuity
OC 01-03-2013	28 March 2013	In perpetuity
Part 5 Determination – Goonbri Road Upgrade	28 March 2014	In perpetuity
Forestry Corporation Permits		
Forestry Compensation Agreement	23 January 2006	14 November 2032
Land Access and Compensation Arrangement	5 June 2009	14 November 2032
Crown Lands Licences		
RI 507102	12 November 2012	14 November 2032
RI 533986	5 June 2014	14 November 2032

1.3 Land Ownership and Land Use

The BCM lies wholly within the Narrabri Shire Council (NSC) local government area (**Figure 1-1**). **Table 1-3** provides the land tenure of the lots within and adjacent to the mining leases at BCM. **Table 1-4** provides a schedule of occupancy over the mining lease areas for the BCM. Properties shown as 'bold' are owned or leased by BCOPL. Landownership details are illustrated on **Figure 1-2**.

Table 1-3: Schedule of Land Ownership

Landownership	Lot//DP	Landownership	Lot//DP
Boggabri Coal	156//DP455004	Boggabri Coal	9//DP1096302
Boggabri Coal	264//DP755475	Boggabri Coal	1//DP748046
Boggabri Coal	1//DP622375	Boggabri Coal	7//DP754940
Boggabri Coal	3//DP566122	Boggabri Coal	157//DP755475
Boggabri Coal	14//DP754940	Boggabri Coal	142//DP754926
Boggabri Coal	2//DP748046	Boggabri Coal	202//DP755475
Boggabri Coal	A//DP362061	Boggabri Coal	44//DP754926
Boggabri Coal	3//DP748046	Boggabri Coal	27//DP754940
Boggabri Coal	12//DP754927	Boggabri Coal	28//DP754940
Boggabri Coal	56//DP754924	Boggabri Coal	13//DP754927
Boggabri Coal	1//DP754926	Boggabri Coal	37//DP754933
Boggabri Coal	59//DP754948	Boggabri Coal	161//DP755475
Boggabri Coal	3//DP754927	Boggabri Coal	12//DP625789
Boggabri Coal	43//DP754926	Boggabri Coal	19//DP754940

Landownership	Lot//DP	Landownership	Lot//DP
Boggabri Coal	3//DP1175679	Boggabri Coal	262//DP755475
Boggabri Coal	2//DP1175856	Boggabri Coal	37//DP754940
Boggabri Coal	161//DP754926	Boggabri Coal	28//DP754927
Boggabri Coal	2//DP754927	Boggabri Coal	23//DP754940
Boggabri Coal	250//DP755475	Boggabri Coal	44//DP754940
Boggabri Coal	132//DP754926	Boggabri Coal	24//DP754940
Boggabri Coal	165//DP754926	Boggabri Coal	41//DP754926
Boggabri Coal	203//DP755475	Boggabri Coal	40//DP754926
Boggabri Coal	127//DP754926	Boggabri Coal	5//DP754940
Boggabri Coal	154//DP755475	Boggabri Coal	18//DP754940
Boggabri Coal	21//DP754940	Boggabri Coal	225//DP755475
Boggabri Coal	125//DP755475	Boggabri Coal	39//DP754926
Boggabri Coal	85//DP755475	Boggabri Coal	13//DP754940
Boggabri Coal	153//DP755475	Boggabri Coal	107//DP755470
Boggabri Coal	22//DP754940	Boggabri Coal	158//DP755475
Boggabri Coal	29//DP754927	Boggabri Coal	1//DP716002
Boggabri Coal	15//DP754927	Boggabri Coal	A//DP379148
Boggabri Coal	12//DP754926	Boggabri Coal	191//DP755470
Boggabri Coal	A//DP379147	Boggabri Coal	12//DP754940
Boggabri Coal	125//DP754926	Boggabri Coal	26//DP754927
Boggabri Coal	124//DP754926	Boggabri Coal	105//DP755470
Boggabri Coal	1//DP566122	Boggabri Coal	2//DP716002
Boggabri Coal	8//DP754940	Boggabri Coal	17//DP754940
Crown	7020//DP1051979	Crown	7006//DP1028729
Crown	7300//DP1143939	Crown	7001//DP94069
Crown	7015//DP1051978	Crown	145//DP755475
Crown	7008//DP1116201	Crown	7003//DP1028512
Crown	171//DP755475	Crown	87//DP755475
Crown	7001//DP1028744	Crown	102344090
Crown	164//DP754926	Crown	160//DP755475

Landownership	Lot//DP	Landownership	Lot//DP
Crown	7003//DP1114719	Crown	89//DP755475
Crown	207//DP754926	Crown Special Lease	7001//DP1052587
Crown	7002//DP1051146	Crown Special Lease	263//DP755475
Crown	7005//DP1028732	Crown Special Lease	7002//DP1052587
Crown	7003//DP1050545	Leard State Conservation Area	310//DP1191559
Mining Joint Ownership	186//DP754926	Mining Joint Ownership	5//DP1131282
Mining Joint Ownership	60//DP754948	Mining Joint Ownership	248//DP755475
Mining Joint Ownership	159//DP755475	Mining Joint Ownership	2//DP868635
Mining Joint Ownership	149//DP754926	Mining Joint Ownership	145//DP754926
Mining Joint Ownership	4//DP1131282	Mining Joint Ownership	206//DP754926
Mining Joint Ownership	1//DP868635	Mining Joint Ownership	121//DP754926
Narrabri Shire Council	1//DP1068048	Private	73//DP754953
Private	1//DP1175679	Private	15//DP754953
Private	80//DP755475	Private	85//DP821271
Private	35//DP754953	Private	1//DP114747
Private	55//DP754953	Private	10//DP755525
Private	52//DP754953	Private	168//DP754926
Private	22//DP618032	Private	1//DP1103922
Private	17//DP754953	Private	110//DP755470
Private	47//DP754953	Private	1//DP1092877
Private	49//DP754953	Private	151//DP755475
Private	81//DP754948	Private	4//DP114747
Private	2//DP1175679	Private	74//DP754953
Private	192//DP754926	Private	13//DP754953
Private	36//DP754948	Private	12//DP754953
Private	44//DP754953	Private	3//DP114747
Private	16//DP754953	Private	108//DP755470
Private	41//DP754953	Private	188//DP755470
Private	5//DP754927	Private	11//DP775513

Landownership	Lot//DP	Landownership	Lot//DP
Private	189//DP755470	Private	104//DP755470
Private	53//DP754953	Private	C//DP100330
Private	4//DP754927	Private	B//DP100330
Private	216//DP657938	Private	1//DP509031
Private	12//DP775513	Private	106//DP755470
Private	21//DP618032	Private	71//DP754953
Private	62//DP754948	Private	51//DP754953
Private	A//DP100330	Private	249//DP755475
Private	111//DP755470	Private	109//DP755470
Private	1//DP791323	Private	821//DP1074515
Private	190//DP755470	Private	48//DP754948
Private	2//DP114747	Private	B//DP190503
Private	143//DP754926	Private	H//DP100330
Private	48//DP754953	Private	102//DP755470
Private	168//DP755475	Private	E//DP100330
Private	72//DP754953	Private	14//DP754953
Private	2//DP1103922	Private	A//DP100332
Private	50//DP754953	Private	104//DP754953
Private	101//DP755470	State Forest	30//DP754940
State Forest	38//DP1211027	State Forest	87//DP754953
State Forest	56//DP754940	State Forest	38//DP754940
Whitehaven Coal Mining	204//DP754926	Whitehaven Coal Mining	60//DP754953
Whitehaven Coal Mining	205//DP754926	Whitehaven Coal Mining	7//DP754951
Whitehaven Coal Mining	200//DP754926	Whitehaven Coal Mining	11//DP754951
Whitehaven Coal Mining	37//DP754953	Whitehaven Coal Mining	25//DP754953
Whitehaven Coal Mining	6//DP754951	Whitehaven Coal Mining	40//DP754940
Whitehaven Coal Mining	2//DP830730	Whitehaven Coal Mining	23//DP754927
Whitehaven Coal Mining	122//DP834141	Whitehaven Coal Mining	81//DP754953
Whitehaven Coal Mining	121//DP834141	Whitehaven Coal Mining	2//DP1131282
Whitehaven Coal Mining	24//DP754953	Whitehaven Coal Mining	33//DP754953

Landownership	Lot//DP	Landownership	Lot//DP
Whitehaven Coal Mining	57//DP754953	Whitehaven Coal Mining	93//DP755475
Whitehaven Coal Mining	10//DP754951	Whitehaven Coal Mining	2//DP509312
Whitehaven Coal Mining	26//DP754953	Whitehaven Coal Mining	2//DP1015921
Whitehaven Coal Mining	75//DP754953	Whitehaven Coal Mining	67//DP754924
Whitehaven Coal Mining	43//DP754953	Whitehaven Coal Mining	2//DP622375
Whitehaven Coal Mining	31//DP754953	Whitehaven Coal Mining	86//DP754953
Whitehaven Coal Mining	27//DP754953	Whitehaven Coal Mining	1//DP1092050
Whitehaven Coal Mining	23//DP754953	Whitehaven Coal Mining	71//DP754948
Whitehaven Coal Mining	1//DP1145592	Whitehaven Coal Mining	70//DP754948
Whitehaven Coal Mining	193//DP754926	Whitehaven Coal Mining	2//DP1013660
Whitehaven Coal Mining	147//DP754926	Whitehaven Coal Mining	11//DP611290
Whitehaven Coal Mining	822//DP1074515	Whitehaven Coal Mining	83//DP754948
Whitehaven Coal Mining	11//DP754940	Whitehaven Coal Mining	65//DP754924
Whitehaven Coal Mining	39//DP754940	Whitehaven Coal Mining	57//DP754940
Whitehaven Coal Mining	32//DP754953	Whitehaven Coal Mining	25//DP754940
Whitehaven Coal Mining	17//DP754927	Whitehaven Coal Mining	66//DP754948
Whitehaven Coal Mining	53//DP654577	Whitehaven Coal Mining	602//DP854685
Whitehaven Coal Mining	12//DP754924	Whitehaven Coal Mining	84//DP754924
Whitehaven Coal Mining	77//DP754948	Whitehaven Coal Mining	12//DP611290
Whitehaven Coal Mining	54//DP754924	Whitehaven Coal Mining	5//DP223209
Whitehaven Coal Mining	1//DP1099042	Whitehaven Coal Mining	73//DP754948
Whitehaven Coal Mining	74//DP754948	Whitehaven Coal Mining	68//DP754953
Whitehaven Coal Mining	69//DP754953	Whitehaven Coal Mining	75//DP754948
Whitehaven Coal Mining	54//DP754948	Whitehaven Coal Mining	87//DP754924
Whitehaven Coal Mining	26//DP754940	Whitehaven Coal Mining	3//DP754924
Whitehaven Coal Mining	61//DP754924	Whitehaven Coal Mining	35//DP754940
Whitehaven Coal Mining	21//DP754927	Whitehaven Coal Mining	61//DP754948
Whitehaven Coal Mining	2//DP1068048	Whitehaven Coal Mining	67//DP754953
Whitehaven Coal Mining	88//DP754953	Whitehaven Coal Mining	22//DP754927
Whitehaven Coal Mining	1//DP614506	Whitehaven Coal Mining	1//DP754924

Landownership	Lot//DP	Landownership	Lot//DP
Whitehaven Coal Mining	81//DP754924	Whitehaven Coal Mining	34//DP754940
Whitehaven Coal Mining	68//DP754948	Whitehaven Coal Mining	99//DP754924
Whitehaven Coal Mining	41//DP754940	Whitehaven Coal Mining	36//DP754924
Whitehaven Coal Mining	34//DP754924	Whitehaven Coal Mining	45//DP754953
Whitehaven Coal Mining	3//DP1068048	Whitehaven Coal Mining	16//DP754924
Whitehaven Coal Mining	17//DP754924	Whitehaven Coal Mining	27//DP754927
Whitehaven Coal Mining	64//DP754948	Whitehaven Coal Mining	76//DP754948
Whitehaven Coal Mining	39//DP754953	Whitehaven Coal Mining	46//DP754948
Whitehaven Coal Mining	1//DP120611	Whitehaven Coal Mining	113//DP754953
Whitehaven Coal Mining	121//DP808273	Whitehaven Coal Mining	83//DP754924
Whitehaven Coal Mining	37//DP754924	Whitehaven Coal Mining	2//DP614506
Whitehaven Coal Mining	51//DP754924	Whitehaven Coal Mining	11//DP754924
Whitehaven Coal Mining	69//DP754948	Whitehaven Coal Mining	80//DP754924
Whitehaven Coal Mining	8//DP754924	Whitehaven Coal Mining	43//DP754940
Whitehaven Coal Mining	32//DP754940	Whitehaven Coal Mining	55//DP754924
Whitehaven Coal Mining	A//DP367991	Whitehaven Coal Mining	80//DP754953
Whitehaven Coal Mining	58//DP754940	Whitehaven Coal Mining	65//DP754948
Whitehaven Coal Mining	10//DP754924	Whitehaven Coal Mining	45//DP754948
Whitehaven Coal Mining	61//DP754940	Whitehaven Coal Mining	10//DP754940
Whitehaven Coal Mining	59//DP754940	Whitehaven Coal Mining	A//DP100331
Whitehaven Coal Mining	42//DP754940	Whitehaven Coal Mining	106//DP754953
Whitehaven Coal Mining	B//DP190502	Whitehaven Coal Mining	61//DP754953
Whitehaven Coal Mining	46//DP754953	Whitehaven Coal Mining	83//DP754953
Whitehaven Coal Mining	65//DP754953	Whitehaven Coal Mining	3//DP114590
Whitehaven Coal Mining	2//DP510801	Whitehaven Coal Mining	74//DP754924
Whitehaven Coal Mining	16//DP754940	Whitehaven Coal Mining	2//DP754924
Whitehaven Coal Mining	33//DP754940	Whitehaven Coal Mining	120//DP754926
Whitehaven Coal Mining	38//DP754924	Whitehaven Coal Mining	1//DP970060
Whitehaven Coal Mining	58//DP754924	Whitehaven Coal Mining	62//DP754953
Whitehaven Coal Mining	72//DP754948	Whitehaven Coal Mining	84//DP754953

Landownership	Lot//DP	Landownership	Lot//DP
Whitehaven Coal Mining	1//DP1015921	Whitehaven Coal Mining	60//DP754940
Whitehaven Coal Mining	1//DP510801	Whitehaven Coal Mining	45//DP754926
Whitehaven Coal Mining	15//DP754940	Whitehaven Coal Mining	6//DP754940
Whitehaven Coal Mining	29//DP754940	Whitehaven Coal Mining	1//DP509312
Whitehaven Coal Mining	110//DP754924	Whitehaven Coal Mining	31//DP754940
Whitehaven Coal Mining	166//DP754926	Whitehaven Coal Mining	120//DP808273
Whitehaven Coal Mining	18//DP754953	Whitehaven Coal Mining	55//DP754940
Whitehaven Coal Mining	35//DP754924	Whitehaven Coal Mining	9//DP754924
Whitehaven Coal Mining	67//DP754948	Whitehaven Coal Mining	27//DP754948
Whitehaven Coal Mining	16//DP754927	Whitehaven Coal Mining	18//DP754927
Whitehaven Coal Mining	6//DP223209	Whitehaven Coal Mining	64//DP754924
Whitehaven Coal Mining	196//DP754926	Whitehaven Coal Mining	1//DP1013660
Whitehaven Coal Mining	40//DP754924	Whitehaven Coal Mining	11//DP754927


Table 1-4: Land Occupancy

Property	Occupancy	Parish	County	Description
Authorisation Area 355	Unoccupied	Leard	Nandewar	Non designated crown land to the north and east of Lots 30 and 38 DP 754940
Coal Lease 368	Unoccupied	Leard	Nandewar	Lots 30, 38 and 56 DP 754940
Mining Lease 1883	Unoccupied	Leard	Nandewar	Non designated crown land to the north and east of Lots 30 and 38 DP 754940 Lot 60 DP 754940
Closed road	Unoccupied	Baan Baa	Pottinger	Between Parish 191 and PT 156
Leard State Forest	Unoccupied			State Forest – Leard 420
“Merriown” – Farm and Cottage	Unoccupied	Leard	Nandewar	Lots 5, 12, 17, and 37 DP 754940
“Nagero” – Farm and Cottage	Occupied	Leard	Nandewar	Lots 24, 25, and Lot 44 DP 754940. Lot 279 DP 1196626
Crown controlled public roads	Unoccupied	Leard	Nandewar	Road that runs East West through the Southern portion of A 355. Road in the South East corner of A 339
“Greenhills”	Occupied	Leard	Nandewar	Lots 86, 87 and 88 DP 754953
Local Government controlled public roads	Unoccupied	Leard	Nandewar	Leard Forest Road path through the Leard State Forest and Road in the South East corner of A 339

Property	Occupancy	Parish	County	Description
"Forest View" Farm only	Unoccupied	Wean	Nandewar	Lot 83 DP 754953
Whitehaven Coal owned freehold	Unoccupied	Leard	Nandewar	Lot 60 DP 754940
Mining Lease 1755	Unoccupied	Leard	Nandewar	Lots 241, 242, 243 DP 1219864 Lot 279 DP 1196626 Lot 161 DP 1255904 Lot 10 DP 754940 Lot 12 DP 1182291 Lot 1 DP 970060

1.3.1 Land Ownership and Land Use Figures

The Land Ownership and Land Use figures as required by the *Form and Way: Rehabilitation Management Plan for Large Mines* (NSW Resources Regulator, 2021) are provided in **Figure 1-2** to **Figure 1-6** below.

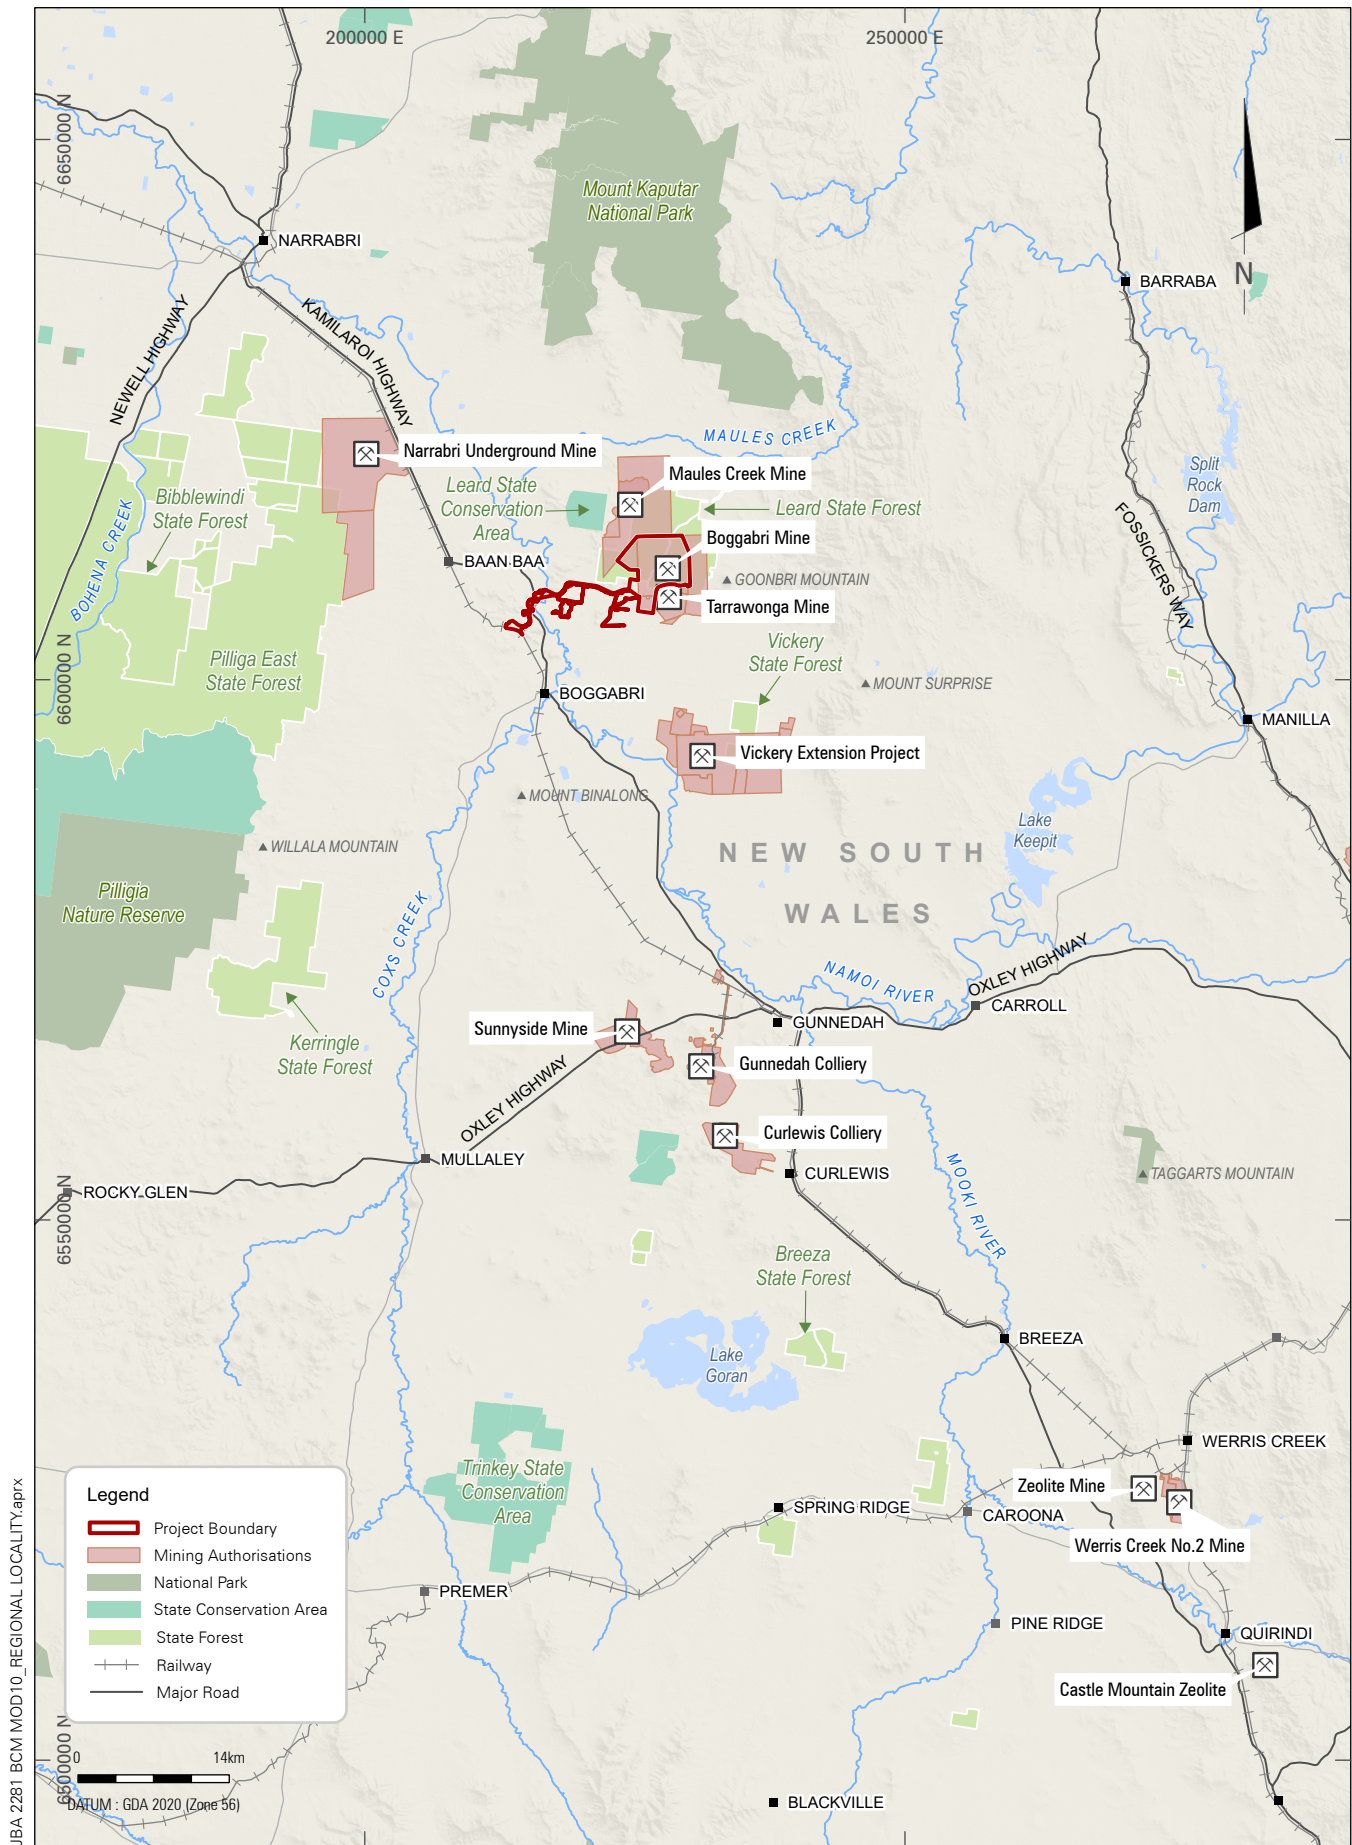


BOGGABRI COAL MINE

Regional Locality

FIGURE 1-1



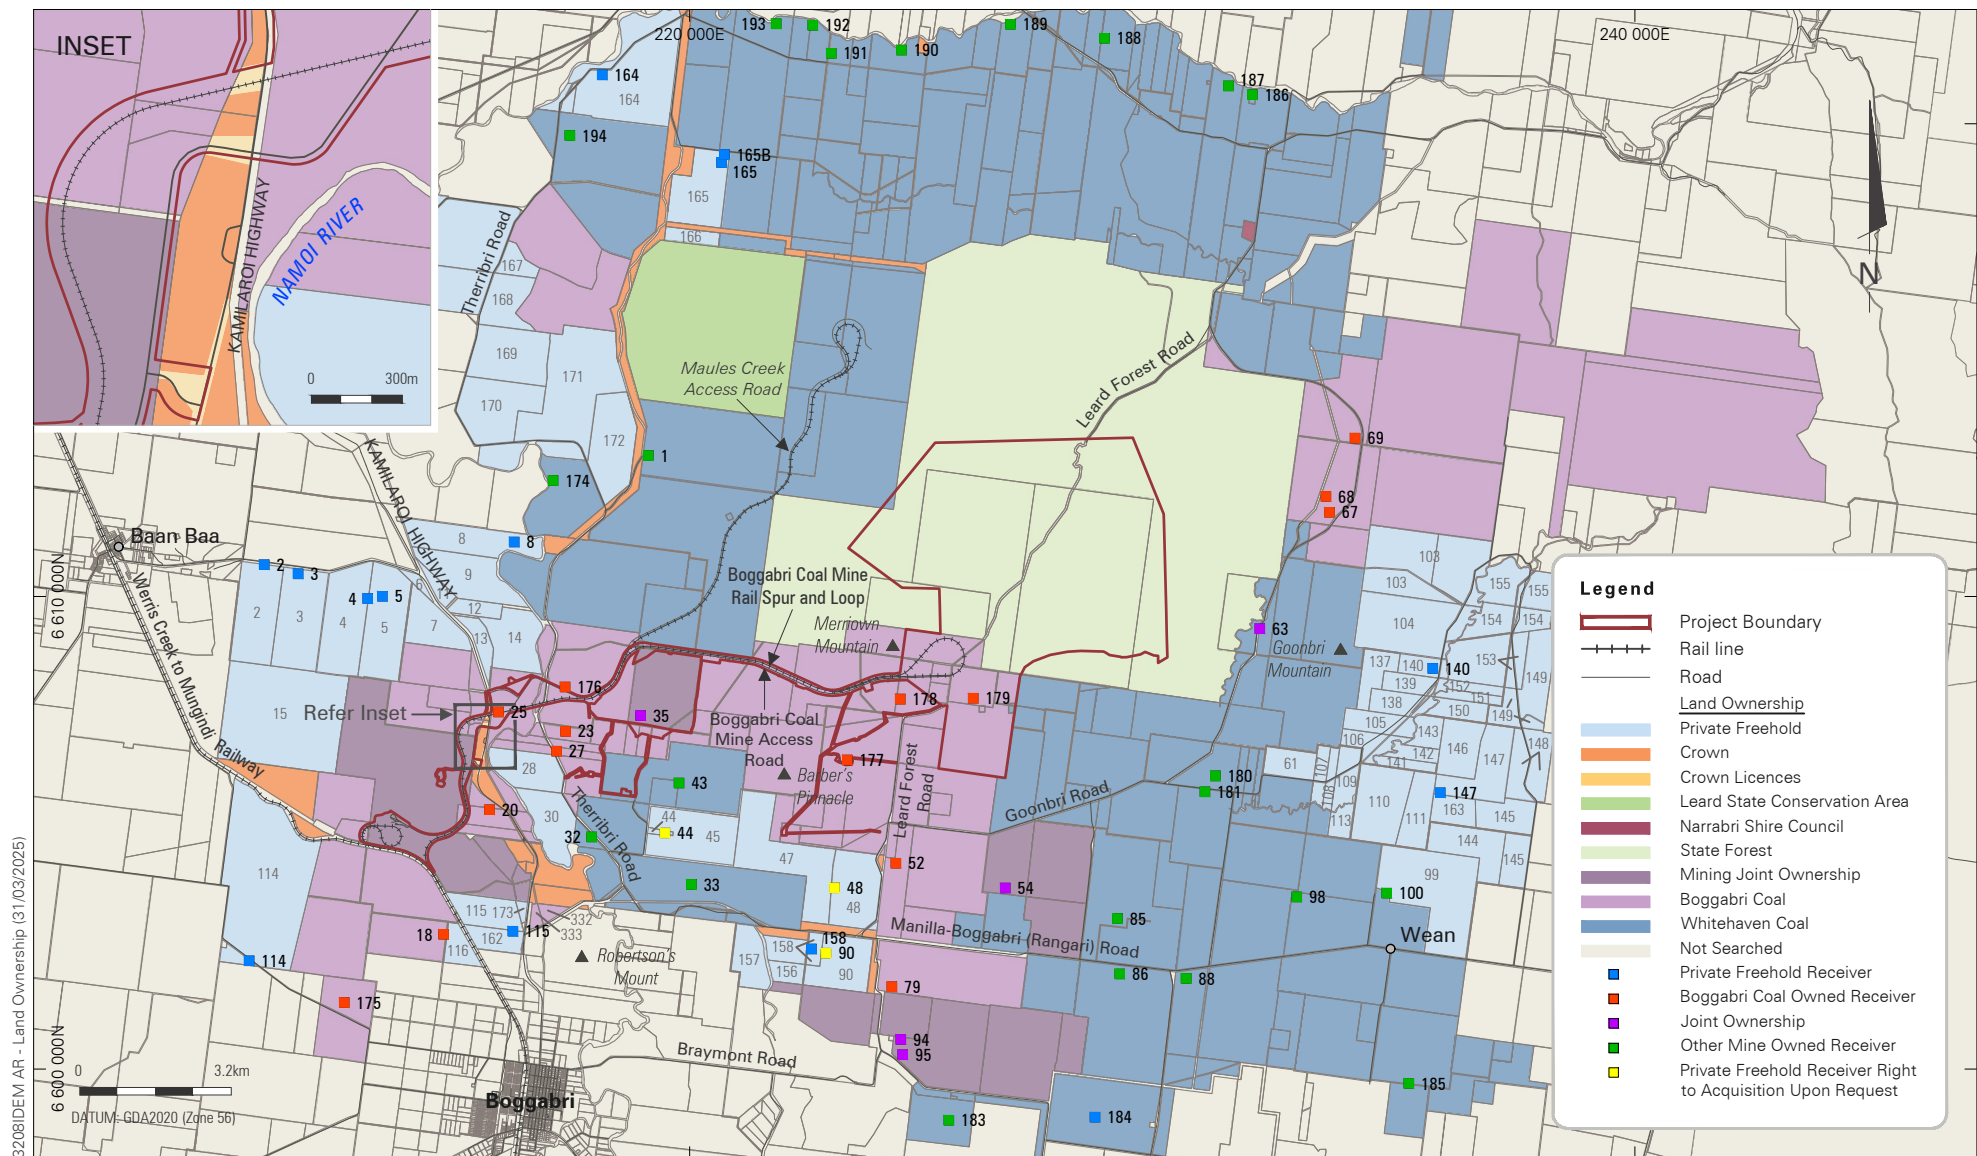

BOGGABRI COAL MINE

Land Ownership

FIGURE 1-2



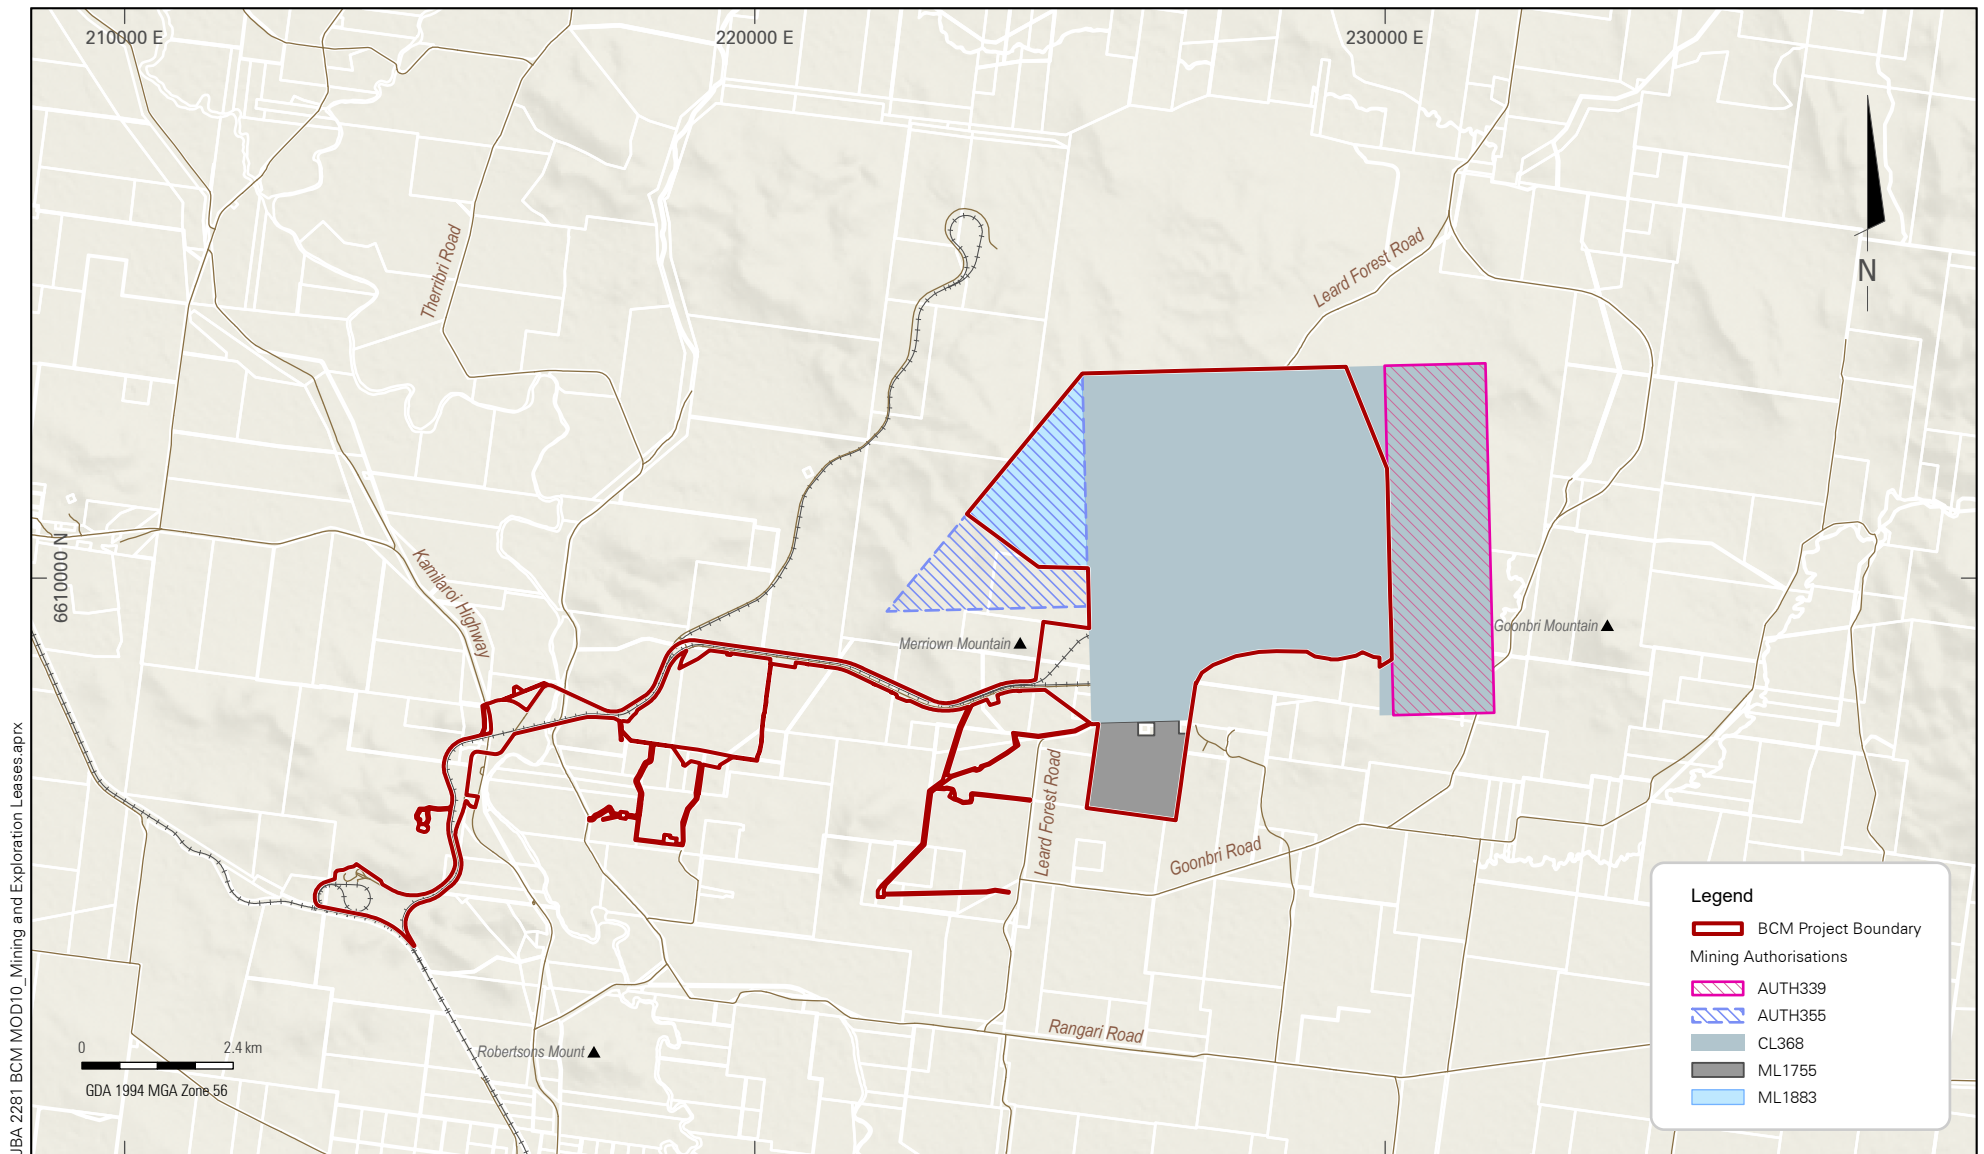


FIGURE 1-3


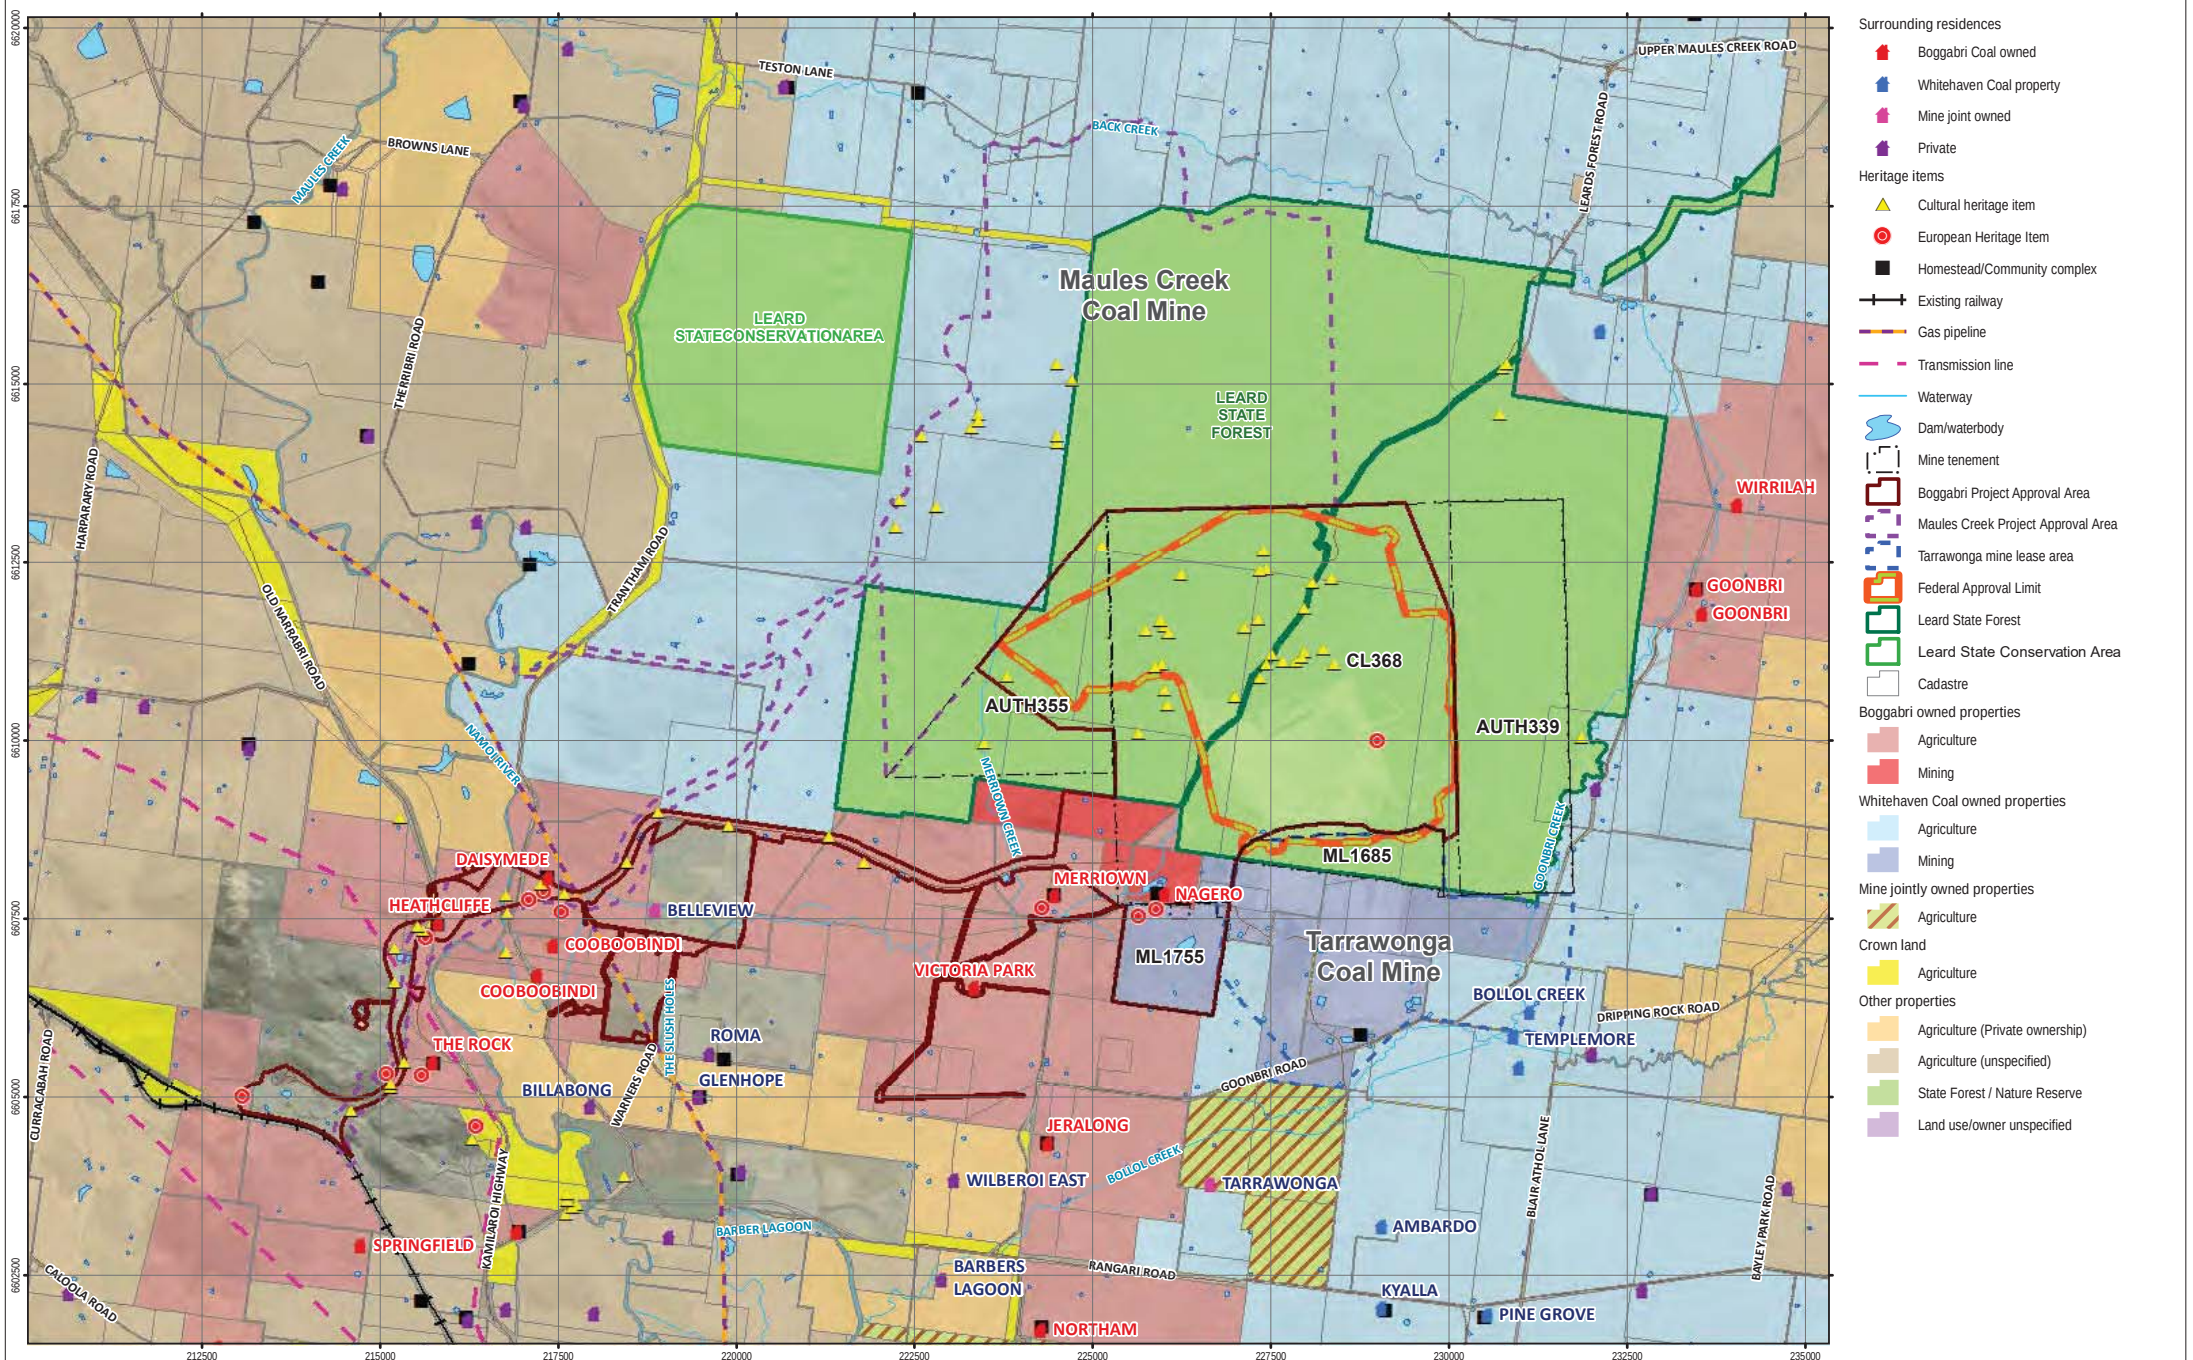


FIGURE 1-5

ENVIRONMENTALLY & CULTURALLY SENSITIVE AREAS

 00.511.52 Scale 1:75,000 Projection: Transverse Mercator Coordinate System: GDA 1994 MGA Zone 56 Scale correct when printed at A3 Landscape Data source: LPI2014 DTDB and DCDB Imagery source: BCPL (2014,2015,2016,2017), © Persons Brecknell Australia Pty Ltd ("PBA") Copyright in the drawings, information and data recorded ("the information") is the property of PBA. This document and the information are solely for the use of the addressee and this document may not be used, copied or reproduced in whole or part for any purpose other than that which it was supplied by PBA. PBA makes no representation, undertaking or warranty as to the accuracy, completeness or reliability of any information or data supplied by PBA or any third party who may rely upon this document or the information. NCS Certified Quality System to ISO 9001. © APPROVED FOR AND ON BEHALF OF Persons Brecknell Australia Pty Ltd <tr><td> MINE NAME: BOGGABRI COAL MINE </td><td> NAME: </td><td> NAME: </td></tr> <tr><td> MINE TITLE: CL0368 </td><td> TITLE: </td><td> TITLE: </td></tr> <tr><td> LEASE HOLDER: BOGGABRI COAL OPERATIONS PTY. LTD. </td><td> SIGNATURE: </td><td> SIGNATURE: </td></tr> <tr><td></td><td> DATE: </td><td> DATE: </td></tr>	MINE NAME: BOGGABRI COAL MINE	NAME:	NAME:	MINE TITLE: CL0368	TITLE:	TITLE:	LEASE HOLDER: BOGGABRI COAL OPERATIONS PTY. LTD.	SIGNATURE:	SIGNATURE:		DATE:	DATE:
MINE NAME: BOGGABRI COAL MINE	NAME:	NAME:										
MINE TITLE: CL0368	TITLE:	TITLE:										
LEASE HOLDER: BOGGABRI COAL OPERATIONS PTY. LTD.	SIGNATURE:	SIGNATURE:										
	DATE:	DATE:										

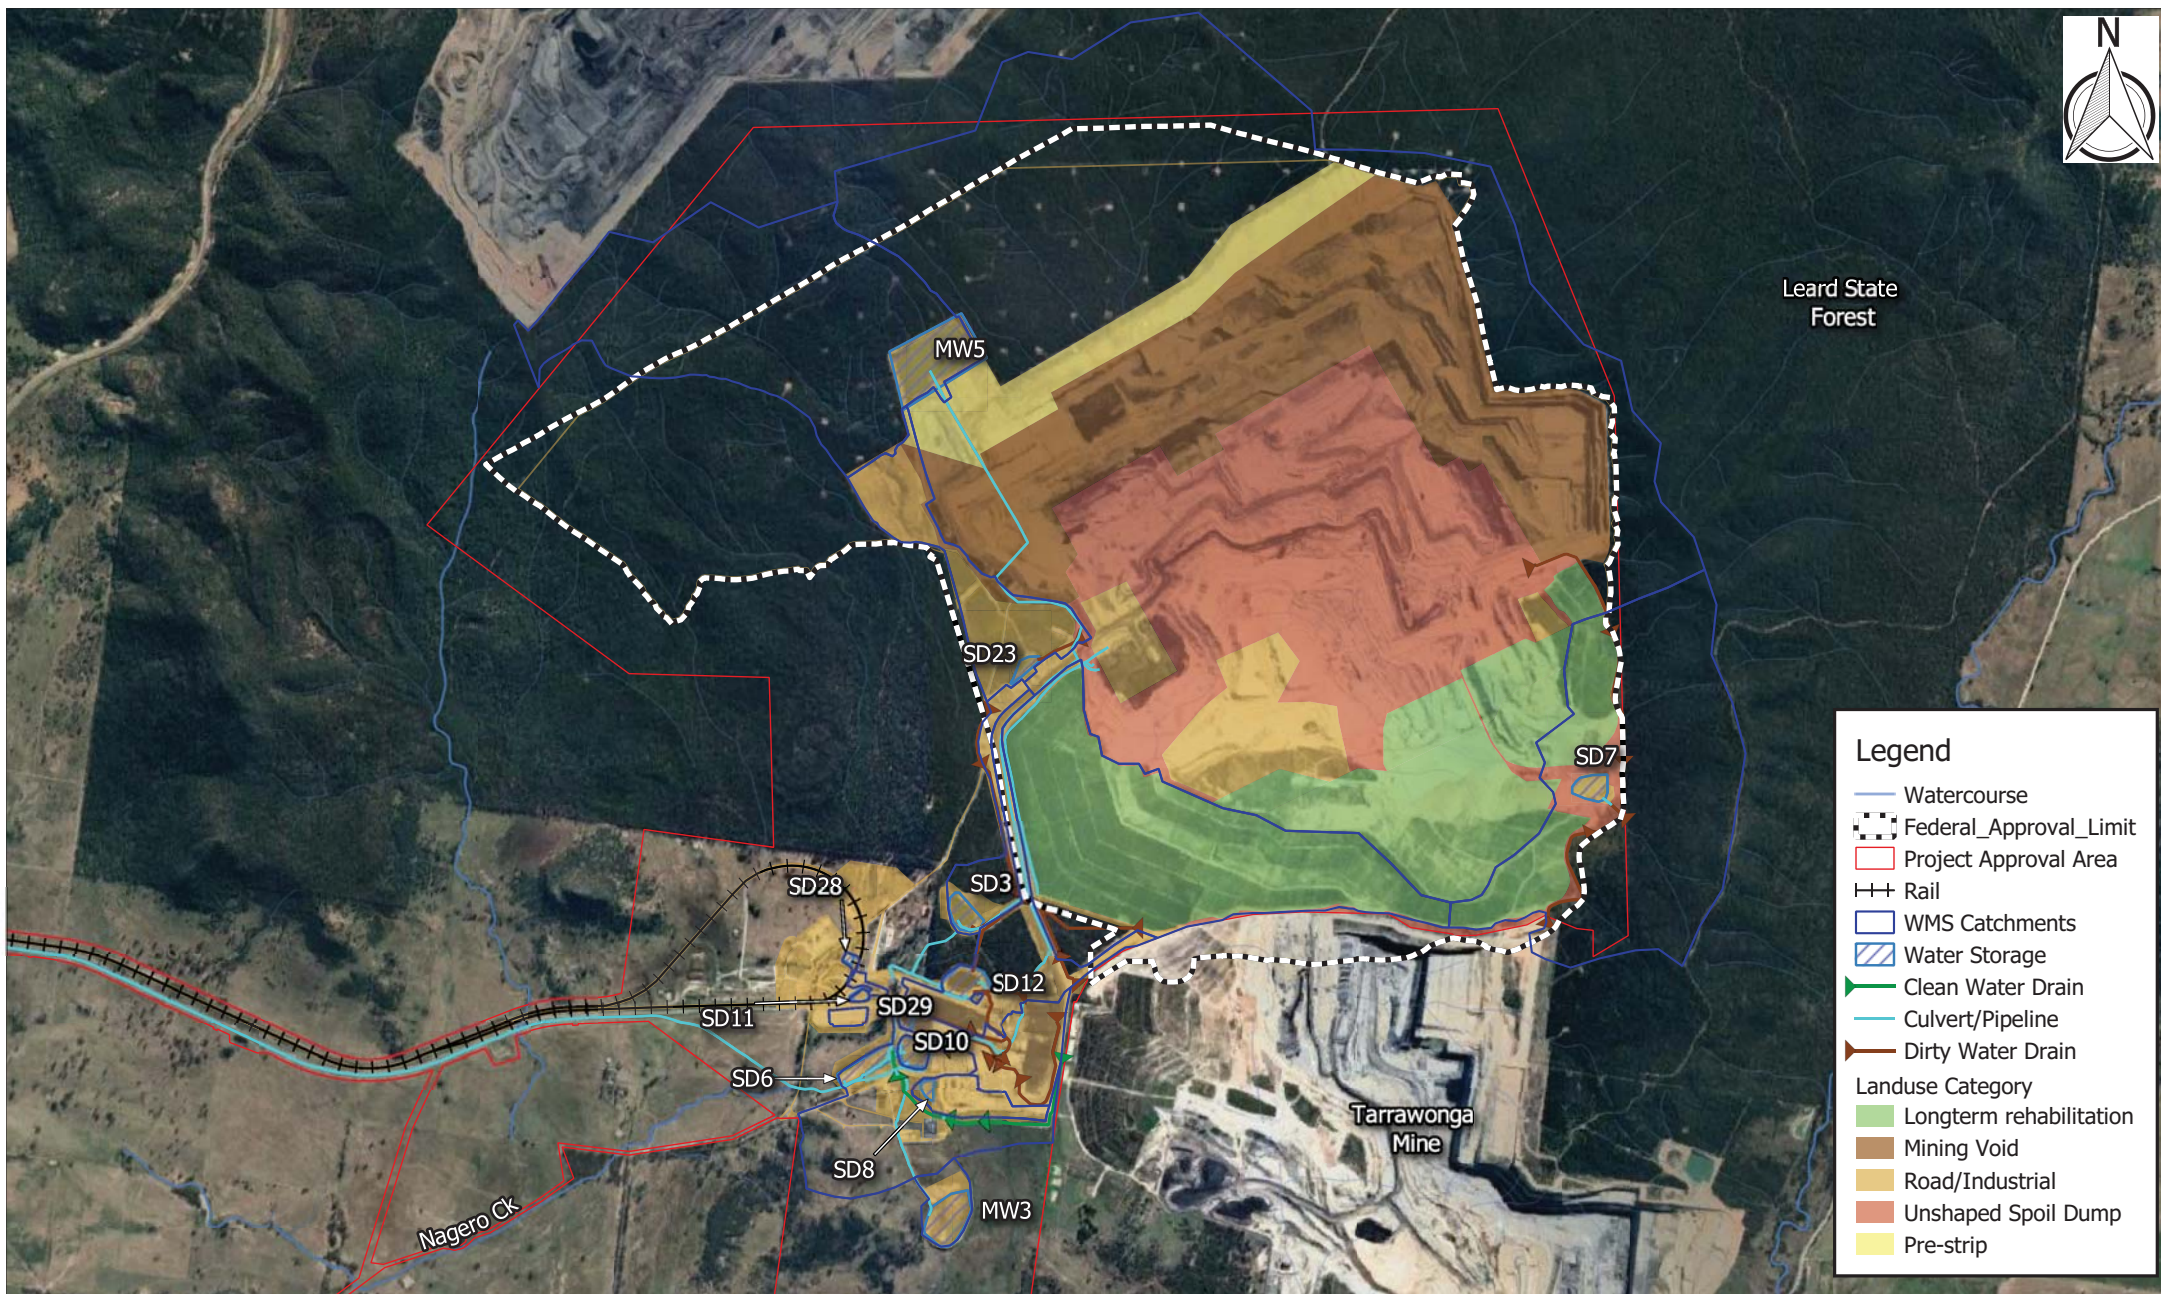

2 FINAL LAND USE

2.1 Regulatory Requirements for Rehabilitation

BCM operates under a range of Commonwealth and State legislation, development consents, mining lease conditions, licences and other statutory approvals relevant to rehabilitation, mine closure and environmental management. This includes, but is not limited to, the Environmental Protection and Biodiversity Conservation Act 1999, Mining Act 1992, Mining Regulation 2016, Protection of the Environment Operations Act 1997, Biodiversity Conservation Act 2016, Biosecurity Act 2015, Local Land Services Act 2013, Brigalow and Nandewar Community Conservation Area Act 2005, and Environment Protection Licence (EPL) 12407. Requirements arising under these instruments are addressed through the environmental management framework for BCM, including relevant management plans, procedures and approval conditions.

Table 2-1: Relevant Approval Conditions **Table 2-1** summarises the regulatory requirements that directly relate to rehabilitation, mine closure and achievement of the approved final land uses at BCM. The table identifies the applicable rehabilitation requirement, the timing for implementation, the land use domain or area to which the requirement applies, and the relevant section of this RMP where the requirement is addressed.

Table 2-1: Relevant Approval Conditions

Applicable condition	Requirement	Timing	Domain	RMP Reference
EPBC Conditions				
2009/5256 Condition 21	To mitigate the impacts to the White Box-Yellow Box-Blakely's Red Gum Grassy Woodland and derived Native Grassland and the habitat of the regent honeyeater, swift parrot and greater long-eared bat, the person taking the action must, within 12 months of commencement of the new mining activities, submit to the Minister for approval a Mine site rehabilitation plan for the progressive rehabilitation and revegetation of no less than 650ha (less the portion included in the biodiversity corridor identified in condition 2) in the Boggabri extension mine site using species consistent with a White Box-Yellow Box-Blakely's red Gum Grassy Woodland and Derived Native Grassland Ecological Community. This approved Mine site rehabilitation plan must be implemented.	Progressive rehabilitation and Closure	Native Ecosystem Domains (A)	Section 4.0 and Section 6.2.1.2
2009/5256 Condition 22	The person taking the action must: a. Rehabilitate the site to be consistent with the proposed rehabilitation strategy as provided in the Environment Assessment and, as required under the NSW state government Project Approval dated 18 July 2012 (application number 09_0182); and	Progressive rehabilitation	Native Ecosystem Domains (A), Agricultural (B)	Section 4.0, Section 6.0 and Section 7.0
	b. Not replace top soil and sub soil layers at a depth less than the minimum depths determined through pre-stripping soil surveys as described in condition 23c. Note: the NSW state government Project Approval dated 18 July 2012 (application number 09_0182) conditions require pre-stripping soil surveys and inventories to inform the availability, rehandling, stockpiling and management of soils, and maximising the salvaging of soil to be used, in the rehabilitation of the site.			Section 6.2.1.1
2009/5256 Condition 23	The Mine site rehabilitation plan must include, at a minimum, the following information: a. Targets and performance indicators to achieve effective restoration of native forest and woodlands. b. Details of the vegetation communities to be rehabilitated and the timing of progressive rehabilitation (commencing as soon as practicable following disturbance).	Ongoing	Entire Site	Section 4.0
				Section 6.2.5

Applicable condition	Requirement	Timing	Domain	RMP Reference
	c. Detailed soil depth surveys and analysis to inform the effective placement and restoration of soils underlying the proposed rehabilitation sites; including mapping of soils across the disturbance sites and soil sampling at no less than one sample point per 20ha of each soil types identified. Sampling must identify; type, depth, water holding capacity, structure and physio-chemical properties of each of the soil and subsoil layers.			Section 6.2.1.1
	d. Processes and methodologies for the removal, storage and re-layering of the top soil and sub soil layers underlying the disturbed sites being prepared for rehabilitation. These processes and methodologies must ensure the replacement of top soil and sub soil layers:			Section 6.2.1.1
	i Meet the minimum depth requirements determined from sampling outcomes as identified in condition 23c; and			Section 6.2.1.10
	ii Replicates the other existing soil parameters including, but not limited to, soil type, water holding capacity, structure and physio-chemical properties.			Section 6.2.4
	e. Criteria to determine success of rehabilitation of native vegetation.			Section 4.0
	f. A process to progressively report to the department the rehabilitation management actions undertaken and the outcomes of those actions, and the mechanisms to be used to identify the need for improved management			Section 8.0 and Section 11.0
	g. A description of the potential risks to successful management and rehabilitation on the project site, and a description of the contingency measures that would be implemented to mitigate these risks			Section 3.0
	h. Details of long-term management and protection of the mine site.			Section 8.0 and Section 11.0
	Note: for consistency, the person taking the action may develop a single mine rehabilitation plan to align with the requirements including timing of reports of the NSW state government Project Approval dated 18 July 2012 (application number 09_0182) requirements and this approval. The Offset management plan and the Mine site rehabilitation plan need to be substantially integrated for achieving biodiversity objectives for the rehabilitated mine-site.			
2009/5256 Condition 24	The person taking the action must rehabilitate the site consistent with the proposed Rehabilitation Strategy as required under conditions 69, 70, 71 and 72 of the NSW state government Project Approval dated 18 July 2012 (application 09_0182) such that the final landform provides the optimum opportunity for the successful restoration of native forest and woodland including the critically	Closure	Native Ecosystem Domains (A)	Section 4.0 and Section 6.2.5

Applicable condition	Requirement	Timing	Domain	RMP Reference
	endangered White Box-Yellow Box-Blakely's Red gum Grassy Woodland and Derived Native Grassland Ecological Community.			
2009/5256 Condition 25	The person taking the action must undertake rehabilitation to ensure the final landform minimises the extent of any resulting pit lake, avoids salt scalding and ensures that drained waters do not adversely affect the downstream environment and avoids any impacts on matters of national environmental significance. Note: the NSW state government Project Approval dated 18 July 2012 (application 09_0182) approval conditions require the preparation and implementation of an updated Final Void and Mine Closure Plan that considers interactions with the adjoining mines, including interaction between final voids, opportunities for integrated mine planning with adjoining mines to minimise environmental impacts, all reasonable and feasible landform options for the final void (including filling) and predicted hydrochemistry and hydrogeology (including long-term groundwater recovery and void groundwater quality).	Closure	Final Void (J), Water Domains (G)	Section 6.2.3.4 and Section 9.2
MP 09_0182				
Schedule 3, Condition 36	The Proponent must: a. Develop a detailed soil management protocol that identifies procedures for · Comprehensive soil surveys prior to soil stripping; · Assessment of top-soil and sub-soil suitability for mine rehabilitation; and · Annual soil balances to manage soil handling including direct resspreading and stockpiling;	Progressive rehabilitation	Entire Site	ENV-RHB-PRO-001 Soil Management Protocol (SMP)
	b. Maximise the salvage of suitable top-soils and sub-soils and biodiversity habitat components such a bush rocks, tree hollows and fallen timber for rehabilitation of disturbed areas within the site and for enhancement of biodiversity offset areas;			Section 6.2.1
	c. Ensure that coal reject or any potentially acid forming Interburden materials must not be emplaced at elevations within the Boggabri pit shell where they may promote acid or sulphate species generation and migration beyond the pit shell;			Section 6.2.1

Applicable condition	Requirement	Timing	Domain	RMP Reference
	d. Ensure that any coal barrier between the final void and any future surrounding mining operations must remain intact in order to impede exchange of any contaminated groundwaters in the Boggabri pit shell.			Section 6.2.3 and Section 9.0
Schedule 3 Condition 44	For the White Box - Yellow Box - Blakeley's Red Gum Grassy Woodland Endangered Ecological Community the Proponent must:	Progressive rehabilitation and Closure	Native Ecosystem Domains (A)	
	a. Ensure that the Biodiversity Offset Strategy and Rehabilitation Strategy are focused on protection, rehabilitation, re-establishment and long-term maintenance of viable stands of this community			Section 4.0 and Section 6.2.1.2
	b. Investigate in consultation with BCS and the North West LLS, all factors likely to enhance or impede the effective long-term restoration of degraded remnants of this EEC in offset areas or regeneration of this EEC on disturbed areas (both offset areas and the site)			Section 9.0
	c. Within 24 months of the date of this approval (and if possible in conjunction with Stage 2 of the Leard Forest Mining Precinct regional Biodiversity Strategy), submit a report of this investigation and provide an implementation plan to maximise the prospects for rehabilitation and regeneration of this EEC on the offset areas and the site, for approval by the Secretary, and			Section 9.0
	d. Incorporate the approved implementation plan into the revised Biodiversity Management Plan, required under condition 50.			Biodiversity Management Plan (BMP)
Schedule 3, Condition 45	For all threatened species on site, the proponent must ensure that the Biodiversity Offset Strategy and Rehabilitation Strategy are focussed on protection, rehabilitation and long-term maintenance of viable stands of suitable habitat for these species.	Progressive rehabilitation and Closure	Native Ecosystem Domains (A)	Section 4.0

Applicable condition	Requirement	Timing	Domain	RMP Reference
Schedule 3, Condition 46	The Proponent must:	Ongoing	Native Ecosystem Domains (A)	Section 9.0 and Section 6.2.6
	a. Investigate, in consultation with BCS and the North West LLS, all factors likely to enhance or impede the effective long-term provision of suitable habitat(s) for the following species: Brown Treecreeper, Hooded Robin, Black-chinned Honeyeater, Painted Honeyeater, Pied Honeyeater, Grey-crowned Babbler, Speckled Warbler, Diamond Firetail, Varied Sittella, Regent Honeyeater, Eastern False Pipistrelle, Greater Long-eared Bat, Yellow-bellied Sheath Tail Bat			BMP
	b. Within 24 months of the date of this approval (and if possible, in conjunction with Stage 2 of the Leard Forest Mining Precinct Regional Biodiversity Strategy), submit a report of this investigation and provide an implementation plan to ensure delivery of suitable areas of viable habitat for the species included in (a) above, for approval by the Secretary, and			BMP
	c. Incorporate the approved implementation plan into the revised Biodiversity Management Plan, required under condition 50.			
Schedule 3, Condition 69	The Proponent must rehabilitate the site in accordance with the conditions imposed on the mining lease(s) associated with the development under the Mining Act 1992. This rehabilitation must be generally consistent with the proposed Rehabilitation Strategy described in the EA (and depicted conceptually in Appendix 9) and comply with the objectives in Table 16.	Ongoing and Closure	Entire Site	This RMP Section 4.0 and Section 7.0
Schedule 3, Condition 70	The Proponent must rehabilitate the site progressively, that is, as soon is reasonably practical following disturbance. All reasonable and feasible measures must be taken to minimise the total area exposed for dust generation at any time. Interim rehabilitation strategies shall be employed when areas prone to dust generation cannot yet be permanently rehabilitated.	Ongoing	Entire Site	Section 6.0
Schedule 3, Condition 71	The Proponent must prepare a Rehabilitation Strategy for all land disturbed by the development to the satisfaction of the Secretary. This plan must: a. Be prepared by a suitably qualified and experienced person/s; b. Be prepared in consultation with the Resources Regulator, FCNSW, BCS, DPE Water, North West Local Land Services, Council and the CCC; c. Be submitted to the Secretary for approval within one year of the date of the approval of MOD 9, unless otherwise agreed by the Secretary;	Ongoing	Entire Site	ENV-RHB-STR-001 Rehabilitation Strategy dated 7 June 2024

Applicable condition	Requirement	Timing	Domain	RMP Reference
	d. Build upon the Rehabilitation Objectives in Table 16, describe the overall rehabilitation outcomes for the site, and address all aspects of rehabilitation including mine closure, final landform, final void outcomes, post-mining land use/s and water management; e. Align with strategic rehabilitation and mine closure objectives and address the principles of the Strategic Framework for Mine Closure (ANZMEC and MCA, 2000); f. Describe how rehabilitation will be integrated with the mine planning process, including a plan to address premature or temporary mine closure; g. Describe how the rehabilitation measures would be integrated with the measures in the Biodiversity Management Plan required under condition 49; h. Investigate opportunities to refine and improve the final landform over time, including the configuration of the waste rock emplacement areas; i. Include a stakeholder engagement plan to guide rehabilitation and mine closure planning processes and outcomes; j. Detail on how rehabilitation will be integrated with the adjoining Tarrawonga Coal; and k. Include a program to periodically review and update this strategy at least every three years.			
Schedule 3, Condition 71A	The Proponent must implement the Rehabilitation Strategy approved by the Planning Secretary. Note: The Proponent must prepare and implement a Rehabilitation Management Plan in accordance with the conditions imposed on the mining lease(s) associated with the development under the Mining Act 1992.	Ongoing	Entire Site	BCM implements the actions outlined within the Rehabilitation Strategy ENV-RHB-STR-001
Schedule 3, Condition 72	The Proponent must prepare and implement an updated Final Void and Mine Closure Plan as part of the Rehabilitation Strategy required under Schedule 3 Condition 71. This plan must: a. Be submitted to the Resources Regulator and the Department by the end of December 2025; b. Address future stability of the proposed landforms, long term groundwater recovery and void groundwater quality characteristics;	Closure Planning and Closure	Final Void (J), Water Storage (G), Native Ecosystem	Sections 6.2.3 and 9.2.3

Applicable condition	Requirement	Timing	Domain	RMP Reference
	c. Include a detailed assessment of the hydrochemistry, hydrogeology and hydrology components of the final void and landform design that has been subject to independent review and verification by suitably qualified, experienced and independent person/s whose appointment has been approved by the Secretary. d. Demonstrate that: · The long term landform will not generate a pit lake; · Emplaced spoil has the capacity to drain to the natural environment; · Drained waters do not adversely affect the downstream environment; and e. Identify opportunities for integrated mine planning with adjoining mines to minimise environmental impacts of the final landform.		(A), Agricultural (B)	
EA Commitments (Hansen Bailey, 2010)				
Section 8.16.3 (p.164)	It is proposed that the final land use of the rehabilitated site will include those similar to pre-mining land uses including biodiversity, pastoral, forestry and recreational opportunities.	Closure	Entire Site	Section 2.3, Section 2.4 and Section 4.0
Section 8.16.3, (p.165)	The Mine Disturbance Area: The final land use of this area will comprise a mixture of the native vegetation communities including, grassy woodland (70%), shrubby woodland / open forest (25%) and riparian forest (5%) for conservation and forestry.	Closure	Native Ecosystem Domains (A)	Section 2.3, Section 2.4 Section 4.0 and Section 5.0
Section 8.16.3 (p.165)	The Mine Infrastructure Area and Haul Route / Rail Spur: final land use will incorporate a mixture of land capability classes III, IV and V for agricultural lands. The rehabilitation strategy will, where practical, revegetate the haul route and rail spur corridor to maximise its ecological contribution to the east-west wildlife corridor.	Closure	Agricultural Domain (B)	Section 2.3, Section 2.4 Section 4.0 and Section 5.0

Applicable condition	Requirement	Timing	Domain	RMP Reference
Section 8.16.3 (p.167)	The final void will be reshaped to ensure the land form is safe, stable, non-erosive and revegetated as is practical.	Closure	Final Void (J)	Section 6.2.3 and Section 9.2.3
Mining Regulation 2016 Schedule 8A Part 2				
5	Rehabilitation to occur as soon as reasonably practicable after disturbance The holder of a mining lease must rehabilitate land and water in the mining area that is disturbed by activities under the mining lease as soon as reasonably practicable after the disturbance occurs.	Entire Site	Ongoing	Section 6.1
6	Rehabilitation must achieve final land use (1) The holder of a mining lease must ensure that rehabilitation of the mining area achieves the final land use for the mining area. (2) The holder of the mining lease must ensure any planning approval has been obtained that is necessary to enable the holder to comply with subclause (1). (3) The holder of the mining lease must identify and record any reasonably foreseeable hazard that presents a risk to the holder's ability to comply with subclause (1). Note— Clause 7 requires a rehabilitation risk assessment to be conducted whenever a hazard is identified under this subclause. (4) In this clause— final land use for the mining area means the final landform and land uses to be achieved for the mining area— (a) as set out in the rehabilitation objectives statement and rehabilitation completion criteria statement, and (b) for a large mine—as spatially depicted in the final landform and rehabilitation plan, and (c) if the final land use for the mining area is required by a condition of development consent for activities under the mining lease—as stated in the condition. planning approval means— (a) a development consent within the meaning of the <i>Environmental Planning and Assessment Act 1979</i> , or (b) an approval under that Act, Division 5.1.	Entire Site, and all final land use domains	Closure	Section 4.0 Section 1.2 Section 3.0

Applicable condition	Requirement	Timing	Domain	RMP Reference
7	Rehabilitation risk assessment (1) The holder of a mining lease must conduct a risk assessment (a rehabilitation risk assessment) that— (a) identifies, assesses and evaluates the risks that need to be addressed to achieve the following in relation to the mining lease— (i) the rehabilitation objectives, (ii) the rehabilitation completion criteria, (iii) for large mines—the final land use as spatially depicted in the final landform and rehabilitation plan, and (b) identifies the measures that need to be implemented to eliminate, minimise or mitigate the risks. (2) The holder of the mining lease must implement the measures identified. (3) The holder of a mining lease must conduct a rehabilitation risk assessment— (a) for a large mine—before preparing a rehabilitation management plan, and (b) for a small mine—before preparing the rehabilitation outcome documents for the mine, and (c) whenever a hazard is identified under clause 6(3)—as soon as reasonably practicable after it is identified, and (d) whenever given a written direction to do so by the Secretary.	Entire Site	Prior to and throughout Rehabilitation	Section 3.0
10	Rehabilitation management plans for large mines (1) The holder of a mining lease relating to a large mine must prepare a plan (a rehabilitation management plan) for the mining lease that includes the following— (a) a description of how the holder proposes to manage all aspects of the rehabilitation of the mining area, (b) a description of the steps and actions the holder proposes to take to comply with the conditions of the mining lease that relate to rehabilitation, (c) a summary of rehabilitation risk assessments conducted by the holder, (d) the risk control measures identified in the rehabilitation risk assessments, (e) the rehabilitation outcome documents for the mining lease,	Entire Site	Ongoing	This Document

Applicable condition	Requirement	Timing	Domain	RMP Reference
	(f) a statement of the performance outcomes for the matters addressed by the rehabilitation outcome documents and the ways in which those outcomes are to be measured and monitored. (2) If a rehabilitation outcome document has not been approved by the Secretary, the holder of the mining lease must include a proposed version of the document. (3) A rehabilitation management plan is not required to be given to the Secretary for approval. (4) The holder of the mining lease— (a) must implement the matters set out in the rehabilitation management plan, and (b) if the forward program specifies timeframes for the implementation of the matters—must implement the matters within those timeframes.			
12	Rehabilitation outcome documents (1) The holder of a mining lease must prepare the following documents (the rehabilitation outcome documents) for the mining lease and give them to the Secretary for approval— (a) the rehabilitation objectives statement, which sets out the rehabilitation objectives required to achieve the final land use for the mining area, (b) the rehabilitation completion criteria statement, which sets out criteria, the completion of which will demonstrate the achievement of the rehabilitation objectives, (c) for a large mine, the final landform and rehabilitation plan, showing a spatial depiction of the final land use. (2) If the final land use for the mining area is required by a condition of development consent for activities under the mining lease, the holder of the mining lease must ensure the rehabilitation outcome documents are consistent with that condition.	Entire Site	Ongoing	Section 4.1.1
				Section 4.1.2
				Section 5.0
				Section 2.1

2.2 Final Land Use Options Assessment

Throughout the preparation of the Boggabri EA, the then Department of Planning established a Boggabri Coal Biodiversity Offsets Strategy Working Group. The Working Group involved representatives of the then Department of Sustainability, Environment, Water, Population and Communities, Industry and Investment NSW Mineral Resources, Forestry NSW, Department of Environment Climate Change and Water and BCOP. In contemplation over the Biodiversity Offset Strategy for the BCM, the Working Group identified that the preferred approach for the rehabilitation of the mining disturbance areas for the Project would be to focus on the reestablishment of biodiversity values and the establishment of habitat for Threatened species. This was a move from the previous strategy which had focussed on the establishment of commercial timbers for future forestry activities.

The intended biodiversity land use and establishment as part of the regional east to west wildlife corridor was described within the EA which was placed on public exhibition for comment by all stakeholders. The strategy described within the EA culminated in the Rehabilitation Objectives identified within Table 16 of Schedule 3, Condition 69 of MP 09_0182.

Given that MP 09_0182 identifies the intended final land use for the BCM, no further final land use options assessment is required as part of this RMP.

2.3 Final Land Use Statement

The final land uses and rehabilitation strategy for the BCM will be undertaken to ensure consistency with the National Recovery Plan for White Box-Yellow Box-Blakely's Red Gum Grassy Woodland and Derived Native Grassland (Box-Gum Grassy Woodland) (DECCW, 2010).

The rehabilitation strategy broadly includes:

- Rehabilitation of disturbed areas to form part of a regional east-west wildlife corridor created as part of the Biodiversity Offset Strategy. This will create a linkage to remnant vegetation between the Namoi River to the west through the Leard State Forest to the Nandewar Range to the east;
- Revegetation of the post mine landscape with native vegetation, comprising a mixture of native grassy woodland, shrubby woodland/ open forest, riparian forest vegetation types and Box-Gum Woodland with fauna habitat for Threatened species to encourage the re- establishment of pre-mining biodiversity values; and
- Ensuring the sustainability of the post mining ecological values of the landscape.

The long-term security and management of Leard State Forest will be subject to review and recommendations in the development of the Boggabri, Tarrawonga, Maules Creek Complex (BTM Complex) Regional Biodiversity Strategy. Biodiversity is the focus of the final land uses within the BCM mining disturbance boundary.

The final land uses at the BCM will include the following:

- Native Ecosystem Areas, including three vegetation communities:
 - Grassy Woodland on fertile soils (Box Gum Woodland);
 - Riverine Woodland;
 - Shrubby Woodland/Open Forest on skeletal soils;
- Agricultural – grazing areas which will comprise grassland / pasture on land which has been rehabilitated to land capability classes III, IV and V;
- Water Management Areas – including water drainage lines from the rehabilitated landform;
- Water Storage Areas – including dams to be retained within the final landform; and

- Final Void – referring to the treated highwall areas.

The Final Landform and Rehabilitation Plan for the BCM is provided in **Section 5** and presents the spatial layout of the above final land uses.

2.4 Final Land Use and Mining Domains

2.4.1 Final Land Use Domains

The final land use domains for the BCM as illustrated in the Final Landform and Rehabilitation Plan (**Section 5**) are described in **Table 2-2** below.

BCOPL is considering the establishment of a further Native Ecosystem land use domain to reflect the area which was rehabilitated prior to the grant of MP 08_0182 and in accordance with varied rehabilitation objectives to those currently in place. This RMP will be revised and updated in the event that BCOPL considers that this additional final land use domain is required.

Table 2-2: Final Land Use Domains

Reference	Final Land Use Domain
A	Native Ecosystem: <i>Grassy Box Gum Woodland Vegetation Community</i>
A	Native Ecosystem: <i>Riverine Woodland Vegetation Community</i>
A	Native Ecosystem: <i>Shrubby Woodland Vegetation Community</i>
B	Agricultural – grazing: <i>Native pasture for low intensity grazing purposes</i>
G	Water Storage
J	Final Void ¹

A final void is demarcated by the extent of an area that does not free drain to the surrounding surface environment. In other words, the void's planar extent is defined by the lowest point of the voids crest, often referred to as the spill point level (or spill level). The spill level is the elevation in the void, which if filled with water, water would spill into the surrounding landscape. A final void typically comprises the following:

- an area whereby material was extracted as a result of mining and a void remains after mining is complete; and or
- highwalls; and or
- low walls; and or
- ramps.

Definition from:

"GUIDELINE - Rehabilitation objectives and rehabilitation completion criteria, NSW Resources Regulator (2021)"

2.4.2 Mining Domains

The mining domains are summarised in **Table 2-3**.

Table 2-3: Mining Domains

Reference	Final Land Use Domain
1	Infrastructure Area
3	Water Management Area
4	Overburden Emplacement Area
5	Active Mining Area
7	Beneficiation Facility
8	Other

3 REHABILITATION RISK ASSESSMENT

BCOPL completed a rehabilitation risk assessment workshop on 12 February 2025 to revise and update the previous Rehabilitation Risk Assessment completed for BCM. The purpose of this revised risk assessment was to address the inclusion of ML1883 and identify any modified or new key risks to rehabilitation activities for achieving the rehabilitation objectives and final land uses for BCM and to outline the effectiveness of current mitigation and management measures in place to manage these risks. Attendees of the rehabilitation risk assessment included the BCOPL Operations Manager, Technical Services Superintendent, Environment Superintendents, Senior Environmental Advisor, technical specialists from WSP (biodiversity and final land use), Landloch (rehabilitation), site rehabilitation contractor and Xenith (who facilitated the risk assessment workshop).

The Rehabilitation Risk Assessment Workshop was undertaken in accordance with the Resources Regulator's Guideline: Rehabilitation Risk Assessment (NSW Resources Regulator, 2021) which follows the general principles outlined in *Australian Standard AS/NZ ISO 31000:2009 Risk Management – Principles & Guidelines*. The Bowtie Risk Assessment method was used, with the outputs presented in table form rather than as a Bowtie diagram. This method adopts a systematic approach to identify and qualitatively assess risks and identifies potential causes of an unwanted event occurring (i.e. rehabilitation failure), the nominated proactive barriers (preventative controls) to prevent the event from occurring, and the reactive barriers (mitigating controls) to manage the consequences of the unwanted event occurring.

The Rehabilitation Risk Assessment was undertaken to:

- identify, assess and evaluate the potential risks to achieving the rehabilitation objectives, rehabilitation completion criteria and the final land use as spatially depicted in the final landform and rehabilitation plan;
- identify the specific risk control measures that need to be implemented to eliminate, minimise or mitigate the risks; and
- identify how the effectiveness of the risk control measures will be assessed.

The Bowtie Risk Assessment was separated into six key rehabilitation phases/aspects. This included: Rehabilitation Materials and Biological Resources; Landform Establishment; Growth Media, Ecosystem Establishment; Ecosystem Development; Integration of Rehabilitation into Life of Mine (LOM) Planning.

Measures used at the site to manage risks associated with rehabilitation activities are discussed in **Section 6**.

A Trigger Action Response Plan has been developed (and recently updated) to continually monitor and track progress towards the rehabilitation completion criteria with consideration of the identified risks (**Section 10**).

Table 3-1 includes a summary of the key risks to rehabilitation identified during the Bowtie risk assessment and the controls to be implemented, which the key controls are described within this RMP.

The rehabilitation risk assessment will be reviewed annually and revised at least every three years to ensure it remains contemporary with mining operations at BCM. Any changes to the rehabilitation risks will be reflected within future iterations of this RMP.

Table 3-1: Summary of Rehabilitation Risks and Controls

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Rehabilitation Materials and Biological Resources		
Lack of Storage Space for Topsoil and other salvaged materials	• LOM and 3 Year Plan (3YP) planning systems identifies required topsoil stockpile locations for inclusion into ENV-RHB-STR-001-ATT-003 Forward Works Program. • ENV-RHB-PRO-001 Soil Management Protocol describes current knowledge of soil material properties to assist in LOM planning. • Methods for soil stripping activities are reviewed annually. • Register of stripped topsoil/subsoils is maintained by mine planning team (as per SMP).	Section a
Stripping and stockpiling methods results in contamination or loss of resources	• ENV-RHB-PRO-001 Soil Management Protocol describes soil stripping, stockpiling and amelioration application methodology. • ENV-RHB-PRO-001 Soil Management Protocol requires soil testing during stripping to ensure stripping depths consider the depth of the seedbank. • Appropriate stockpiling of materials with specific qualities to avoid contamination. • Methods and protocols are revised frequently as per the topsoil recovery procedure. • Operators are appropriately experienced and trained at conducting stripping activities in accordance with BCOPL requirements. • Appropriate equipment is utilised for stripping and stockpiling activities. • Register of stripped topsoil/subsoils is maintained by mine planning team (as per SMP).	Section a

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Topsoil weed contamination	• ENV-RHB-PRO-001 Soil Management Protocol describes measures to control and manage weeds. • Pre-clearing inspections identify the requirement for weed control prior to stripping activities being completed. • Weeds are scalped from surface of topsoil or from stockpile prior to salvaging for rehabilitation activities. • Topsoil stockpiles are seeded with a prolific low maintenance species that does not contaminate or remove nutrients from the soil, where temporarily stored. Species used similarly needs to be easily neutralised before using topsoil on rehabilitation. • Weed monitoring, maintenance and control of topsoil stockpiles. • Growth media for long term stockpiles are appropriately managed to ensure stockpiles remain fertile for PCT establishment.	Section a
Inadequate or insufficient topsoil/subsoil is available to create/enhance the desired ecological communities.	• ENV-RHB-PRO-001 Soil Management Protocol incorporates an estimate of salvageable soils within the approved Mine Disturbance Boundary and the required soil resources required for effective rehabilitation of the final landform. These estimates are reviewed and updated on an annual basis, with the review of alternative growth mediums in the event that available resources are insufficient. • LOM and 3YP planning systems consider storage locations for final closure activities. • Mine Closure and Final Void Management Plan to be prepared. • Rehabilitation Trigger Action Response Plan (TARP).	Section a
Failure to characterise soils (and identify if ameliorants are required).	• ENV-RHB-PRO-001 Soil Management Protocol requires soil testing to identify qualities of soil materials being stripped. • Appropriate stockpiling of separate soil types. • Revision of methods and protocols frequently. • Survey of stockpile locations, volumes and qualities, including whether ameliorants may be required prior to use.	Section a

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Failure to recover suitable habitat features (i.e. hollow bearing trees, bush rock, logs, etc) to support final land use	• Pre-clearing inspection process to identify suitable habitat features to recover and reuse on rehabilitation. • LOM and 3YP planning systems consider location for temporary storage of habitat features.	Section b and Section k
Lack of suitable rock and substrate available on site (grading, size and competency) to enable key structures to be built.	• Pre-clearing inspection process requires suitable rock materials to be identified for recovery and reuse on rehabilitation areas; • Existing external supplier for suitable rock materials for use in drainage structures. • LOM and 3YP planning systems consider requirement for rock and substrate for water management structures. • Rock testing undertaken to ensure rock/substrate materials are suitable for use in water management structures. • Rock and substrate materials balance and stockpile inventory to be developed and maintained. • Implement tailored rock management practices – rock testing, storage and mixed sizes.	Section d and Section k
Poor quality seed (i.e. poor germination/success of revegetation).	• Rehabilitation Management Plan and Biodiversity Management Plan identifies the requirement to collect seed from the region for propagation. • Pre-clearing inspections identify potential seed resources for collection prior to clearing. • Storage of seed collected onsite and surrounding areas. • Seed purchased from reputable supplier. • Visual inspection of seed prior to use on rehabilitation. • Utilise qualified and experienced personnel to collect and store seed. • Certification from seed supplier. • Processes to amend seed mix to ensure rehabilitation is sufficiently achieved.	Section k

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Insufficient quantity of seed/tubestock available to achieve effective rehabilitation.	• Rehabilitation Management Plan and Biodiversity Management Plan identifies the requirement to collect seed from the region for propagation. • Pre-clearing inspections identify potential seed resources for collection prior to clearing. • Suitably qualified personnel employed to appropriately collect seed onsite and surrounds. • Appropriate storage of seed (utilise external specialists for storage). • Seed purchased from reputable supplier. • Notify seed supplier of requirements well in advance to ensure suitable supply. • Tubestock purchased from reputable supplier. • Notify tubestock suppliers of requirements well in advance to ensure suitable supply.	Section k
Equipment and skills not available to appropriately salvage rehabilitation materials.	• Access to experienced contractors and suitable equipment.	Section k
Problematic materials (PAF, carbonaceous materials, sodic materials, etc) are used on outer slopes of rehabilitation areas.	• Approved final landform design is incorporated into mine planning to ensure problematic materials are not emplaced near the final surface. • Mine Planning Standard No. 38 provides detailed procedures for the management and placement of problematic materials. • Regular land survey to identify locations where problematic materials cannot be dumped. • Regular testing of soil qualities for final rehabilitation activities and any requirement for amelioration. • Ground and Strata Management Plan. • MIN-PRO-008 Dumping Operations and MIN-PRO-009 Rejects Management and Operations identifies appropriate measures to be implemented during disposal of reject materials.	Sections e, f, g, h, i and k
Insufficient knowledge of available biological resources within the disturbance area.	• Biodiversity Management Plan and Rehabilitation Management Plan identifies pre-existing biological resources for salvage and use within rehabilitation activities. • Pre-Clearing Inspections are undertaken by suitably qualified persons to identify available biological resources.	Section b
Adequacy of Final Landform		

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Inadequate consideration of achieving a safe, stable and non-polluting final landform.	• Landform design criteria and landform design process has been identified. • Conceptual Final Landform Study (Landloch, 2012) provides an indicative erosional assessment. Other geotechnical reference reports provide information / recommendation regarding OEA construction. • Refinements to Conceptual Final Landform design are subject to geotechnical/erosional modelling to determine areas of erosion potential and requirement for landform treatments (e.g. rock armouring, blankets, etc). • Geotechnical and engineering design for drainage drop structures, etc • Post construction landform survey to verify landform is constructed to design. • Post construction erosion and landform stability monitoring.	Sections d, j and 0
Inadequate landform design and sustainable construction.	• Rehabilitation Reforms Conceptual Final Landform design. • Mine plan design software utilised to build Conceptual Final Landform Design • GPS on key equipment • As built landform surveys	Section b
Not meeting the approved Conceptual Final Landform Design profiles (i.e. max OEA heights, water catchments, surface water drainage, free draining landform)	• Mine Planning utilises Conceptual Final Landform Design. • Availability/Surplus of materials to develop Conceptual Final Landform design • Post construction landform survey to verify landform is constructed to design.	Section b
Premature closure of mine means that the approved final landform cannot be achieved.	• Seek modification to SSD Approval to adjust Conceptual Final Landform design • Mine closure planning adjusted to accommodate required changes from premature closure.	Section b
Infrastructure not decommissioned and/or contamination not remediated in accordance with the SSD Approval OR Mining Lease requirements	• Rehabilitation Management Plan describes the decommissioning process required to achieve closure. • Development of Final Void and Mine Closure Plan by end 2025 as required by SSD Approval. • Approval to utilise infrastructure for future uses.	Section 6.2.2

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Saline leachates expressing from the final landform.	• Mine Planning for emplacement of hostile materials to be in accordance with the MIN-PRO-009 Rejects Management and Operations. • Water Monitoring Program includes sampling of water from the OEA landforms.	Sections f and h
Unplanned ponding and slumping in landforms.	• Independent rehabilitation specialist review of rehabilitation plans. • Temporary landform surface water drainage. • Final landform surface water management design • Landform design developed to be free draining. • Post construction survey to verify landform construction is to design.	Section 0 and Section 8
Large scale landform failure (geotechnical event).	• Landform design criteria and landform design process has been identified. • Conceptual Final Landform Study (Landloch, 2012) provides an indicative erosional assessment. Other geotechnical reference reports provide information / recommendations regarding OEA construction. • Refinements to Conceptual Final Landform design are subject to geotechnical/erosional modelling to determine areas of erosion potential and requirement for landform treatments (e.g. rock armouring, blankets, etc). • Geotechnical and engineering design for drainage drop structures, etc • Post construction survey to verify landform construction is to design. • Post construction erosion and landform stability monitoring.	Section 8
Groundwater recovery in the partially infilled final void results in void retaining surface water.	• Final landform designed to remain higher than the predicted steady state groundwater level. • Development of Final Void and Mine Closure Plan by end 2025 as required by SSD Approval. • BTM Complex Groundwater model every 3 years. • Surface water modelling for the final void to be undertaken for Mine Closure Plan.	Section d
Landform design has not adequately considered changing climate variations.	• Final landform drainage design to consider impacts of extreme events, • Consideration of landform evolution modelling.	Section 0

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Landform design has not considered the integration with Tarrawonga landform.	- Existing agreement in place since 2014 for the establishment of Integrated Landform. - Regular liaison with Tarrawonga / Whitehaven in relation to the establishment of integrated landform.	Section 0
Adequacy of Growth Media		
Topsoil depth is unsuitable to sustain final land use	- ENV-RHB-PRO-001 Soil Management Protocol describes the topsoil depth to be utilised in rehabilitation areas. - Post construction landform survey to verify landform constructed to design. - Topsoil balance provides the availability of topsoil resources. - Knowledge of optimal topsoil depth for final land use (i.e. vegetation types).	Section 0
Sub-soil depth is unsuitable (where it is required) to sustain final land use.	- Rehabilitation Management Plan describes the optimal sub-soil depths to be adopted. - Post construction landform survey to verify landform constructed to design. - Sub-soil balance provides the availability of topsoil resources. - Knowledge of optimal sub-soil depth for final land use (i.e. vegetation types).	Section 0
Inadequate amelioration of growth media resulting in sodicity, surface crusting and long-term erosion.	- ENV-RHB-PRO-001 Soil Management Protocol describes soil testing and amelioration required to growth media. - Selective handling and storage strategies implemented. - Timing of growth media application and seed bed preparation. - Application of ameliorants (as required) during placement of materials onto rehabilitation areas.	Section 0
Handling practices damage physical properties / soil structure.	- ENV-RHB-PRO-001 Soil Management Protocol describes soil stripping and stockpiling requirements to be implemented. - Minimise rehandling through adequate mine planning. - Proven handling methods and equipment and dedicated training systems for personnel. - Stockpile management (reduce compositional changes).	Section a

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Adverse geochemical properties of media (i.e. salinity, acidity, sodicity, etc).	• ENV-RHB-PRO-001 Soil Management Protocol describes growth media testing and amelioration required. • Identification of adverse materials which are not suitable for use in rehabilitation activities. • Implement selective handling and storage strategies.	Sections e, f, g, h and i
Biologically depleted growth media.	• ENV-RHB-PRO-001 Soil Management Protocol describes soil stripping and stockpiling methodologies to implement. • Reintroduction of organic materials and/or habitat features to encourage insect colonisation (as required). • Minimise rehandle of topsoil materials. • Maintain topsoil register to identify opportunities to utilise viable topsoil on rehabilitation.	Section 0
Inadequate consideration to erosion potential.	• Sediment controls implemented as required. • Overburden slope design. • Application of growth media in favourable weather conditions. • Frequent inspection of areas with higher potential for erosion.	Section 0
Physical and structural properties of substrate.	• ENV-RHB-PRO-001 Soil Management Protocol describes soil stripping and stockpiling methods to be implemented to minimise impacts to growth media. • Fit for purpose equipment fleet and experienced operators for optimal stripping and reapplication. • Implement erosion and sediment controls (where relevant).	Section 0
Ecosystem Establishment and Development		
Seed bed preparation is inadequate for native vegetation ecosystem land uses	• Adequate planning and review of seed bed plans to suit projected final land use. • Geochemical testing of soils to achieve optimal seed beds. • Growth media sourced from areas with similar pre-mining vegetation communities.	Sections 6.2.5 and 6.2.6

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Unseasonal adverse weather	• Schedule revegetation in optimal seasons. • Temporary soil stabilisation with temporary cover crop species when revegetation is delayed. • Installation of temporary sediment control structures.	Section 0
Tubestock planting methodology is suitable.	• Proven methods and equipment and dedicated training systems for personnel. • Tubestock installation timing is appropriate (May to July). • Watering of tubestock (when required).	Section 0
Native vegetation establishment from seed within growth media (topsoil, subsoil, mulch) is unsuitable.	• ENV-RHB-PRO-001 Soil Management Protocol describes soil stripping and stockpiling methods to be implemented to minimise impacts to seed resource within growth media. • Topsoil and mulch respreading. • Monitoring of seed germination (post application). • Apply native vegetation seeding for ground cover species. • Thinning of canopy species to facilitate establishment of ground cover.	Section 6.2.5
Tubestock quality and viability.	• Viability testing. • Germination testing. • Certification from suppliers.	Section 0
Predation of juvenile vegetation.	• Biodiversity Management Plan includes pest management controls. • Monitoring and control (as required) of feral animal populations. • Exclusion fencing installed (where required). • Vertebrate pest culling programs.	Section 0

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Damage to rehabilitation areas including bushfire damage.	• Demarcate and control access to rehabilitation areas. • Use appropriate plant and equipment to avoid damage. • Management of bushfire through Bushfire Management Plan. • Active encouragement of staff involvement with the Rural Fire Services • Access paths for fire fighting. • Fire breaks. • Tree guards.	Section 0
Rehabilitation areas are not on trajectory to meet the approved completion criteria for final land use.	• Rehabilitation Management Plan describes the required monitoring, management and Trigger Action Response Plan to implement. • Annual monitoring and reporting of rehabilitation performance against the completion criteria. • General rehabilitation inspections undertaken to identify areas for potential maintenance and repair. • Review of aerial photography.	Section 8
Competitive exclusion of native flora due to exotic weed species and noxious weed.	• Rehabilitation Management Plan includes details of weed management within the rehabilitation areas. • Routine ecology monitoring to detect changes in biodiversity and presence of weeds. • Weed spraying and maintenance.	Section 8
Competitive exclusion of native fauna due to feral animals.	• Rehabilitation monitoring includes monitoring of presence of feral animals and required control. • Feral animal control (as required).	Section 8
Inadequate habitat and resources for native fauna.	• Rehabilitation monitoring (including camera monitoring). • Installation of nest boxes on rehabilitation areas. • Installation of salvaged habitat features (i.e. tree stags, hollows and rocks). • Installation of tree troughs.	Section 8

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Adverse surface water and groundwater quantity and quality.	- Hydrogeological assessments completed to characterise surface water and groundwater resources. - Design and implement groundwater and surface water management strategy. - Water monitoring and reporting.	Section 8
Integration of Rehabilitation into LOM Planning		
Inadequate resources to complete the rehabilitation required.	- Budget – allocation of funds to execute required rehabilitation activities. - Annual review of the rehabilitation budget requirements. - Dedicated rehabilitation planning team available to conduct rehabilitation activities. - External suppliers and contractors available (as required).	Section 5.0
Misalignment of long-term conceptual and short term implementation (internal) – operational constraints mean long-term plans are not achieved.	- Review similarities between plans to recognise commonality. - Pause some works until any conflicts are resolved.	Section 5.0
Inadequate records to demonstrate rehabilitation success and that risks are being managed.	- Evidence of implementation and records of management to be maintained. - Development of quality assurance processes. - Ongoing rehabilitation inspections and post closure monitoring. - Independent rehabilitation audit. - Verification records, including 'as built' surveys in GIS. - Rehabilitation completion and maintenance records.	Section 7
Ineffective scheduling of rehabilitation inside mine planning systems.	- LOM planning and 3 YP provides scheduling for rehabilitation. - Three year plan and annual budgets allow for rehabilitation. - Review plans on a frequent basis to refine (as required).	Section 5.0

Risk/Cause/Consequence	Summary of Control Measures to be Implemented	Where Addressed within this RMP
Rehabilitation execution.	• Mine Design Standard No. 38. • Landform Establishment Quality Assurance Plan (QAP). • Annual Rehabilitation Budget. • Three Monthly Plan. • Monthly Plan. • Weekly Plan. • Annual Review Reporting.	Section 5.0
Lack of governance around mine closure and related financial obligations (i.e. corporate standards).	• SSD Approvals are in place that prescribes mine closure timing. • Boggabri EA (2010) provides figures illustrating progressive rehabilitation. • EPBC Approval requires progressive rehabilitation according to an approved Rehabilitation Plan. • Rehabilitation Management Plan and ENV-RHB-STR-001-ATT-003 Forward Works Program outlines the timing and amount of rehabilitation that is to be completed annually for the three year term. • Rehabilitation Bond is held with the NSW Government. • Final Void and Mine Closure Plan to be prepared in accordance with SSD approval. • Corporate Mine Planning Standard (Idemitsu). • Corporate Site Closure Standard (Idemitsu).	Section 5.0
Inadequate risk assessment (i.e. not all risks and controls are identified relevant to current status of operations).	• Frequent revision of Rehabilitation Risk Assessment. • Input from a suitably qualified team of appropriately skilled people representing a cross-section of the workforce and activities currently being conducted.	Section 3

4 REHABILITATION OBJECTIVES AND REHABILITATION COMPLETION CRITERIA

4.1 Rehabilitation Objectives and Rehabilitation Completion Criteria

Rehabilitation objectives, management goals and key actions have been developed with consideration of:

- Schedule 3, Condition 69 of MP 09_0182
- The Rehabilitation Strategy (as modified) and presented for the EA
- All conditions included within the Mining Leases associated with the development.

The Rehabilitation Outcomes Documents (including the Proposed Rehabilitation Objectives and Proposed Rehabilitation Completion Criteria) are to be submitted to the NSW Resources Regulator for approval (Clauses 9, 12 and 15(b) of Schedule 8A of the *Mining Regulation 2016*).

The Rehabilitation Objectives Statement was approved by the NSW Resources Regulator on 13 October 2023. A copy is included in **Appendix A**.

BCOPL has developed proposed rehabilitation completion criteria, however, has not yet submitted these to the Resources Regulator for review and approval. The Guideline for Rehabilitation Objectives and Rehabilitation Completion Criteria (Resources Regulator, 2021) states "*The intention is for lease holders to submit final rehabilitation completion criteria to us for approval no later than three years before rehabilitation of the whole (or an identified part) of the mining area is proposed to be completed*".

Approved Rehabilitation Objectives and Proposed Completion Criteria are listed in Error! Not a valid bookmark self-reference..

Table 4-1: Rehabilitation Objectives and Proposed Completion Criteria

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
Agricultural Revegetation	B1, B3, B7	Native pasture for low intensity grazing purposes	Revegetation is sustainable for the long-term and only requires maintenance that is consistent with the intended final land use.	Litter cover is within 10th-90th percentile variation range of the analogue communities	Indicators of nutrient cycling are suitable for sustaining the targeted vegetation communities (PCT78/NA193, PCT84/NA191 and/or PCT102/NA181)	Biodiversity Monitoring rehabilitation assessment reports
			Land capable of sustaining low intensity grazing land use.	Soils/spoils ameliorated to sustain low intensity grazing land use	Soil based criteria within 25% of analogue site values for the following criteria; - Water holding capacity mm - Permeability mm/day - pH – Water pH units - Total Nitrogen – Kjeldahl mg/kg -Phosphorus - Colwell extr mg/kg -Organic Carbon % -Emerson Class	Rehabilitation monitoring reports

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
			Final Landform is safe for future use	The final landform is safe for the intended future use and does not have an impact on public safety or the environment	No signs of land instability or active erosion. The final landform complies with the final landform construction in accordance with the Final Landform and Rehabilitation Management Plan	Rehabilitation monitoring reports
Bushfire	A1, A3, A4, A7, A8, B1, B3, B7, G3, J4	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community; Water storage (excluding final void)	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation	Bushfire controls implemented	Appropriate bushfire hazard controls have been implemented on the advice from the NSW Rural Fire Service	Statement provided and before/after photos
Ecological rehabilitation	A1, A3, A4, A7, A8, J4	Grassy Box Gum Woodland Vegetation Community; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest	Vegetation is in a condition comparable to that of the analogue communities	At least 75% of benchmark values for native plant species richness equal or greater proportion of overstorey species occurring as regeneration	Biodiversity Monitoring rehabilitation assessment reports
	A1	Shrubby Woodland Vegetation Community	Levels of ecosystem function have been established that demonstrate the	1. Litter cover is within 10th-90th percentile variation range of the analogue communities	Indicators of nutrient cycling are suitable for sustaining the targeted vegetation communities (PCT78/NA193,	Biodiversity Monitoring rehabilitation assessment reports demonstrate long-term function of rehabilitated landform (i.e.

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
			rehabilitation is self-sustainable		PCT84/NA191 and/or PCT102/NA181)	suitable trends demonstrated).
				2. Second generation individuals of trees are within the 10th-90th percentile variation range of reference sites/data and Number of native plant species flowering / fruiting	Evidence of plant regeneration from 0.04 hectare fixed monitoring plots or a walk over of the ecological rehabilitation area	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				3. Foliage cover of 'high threat exotic' (HTE) weeds (as defined by BAM Calculator) is within 10th-90th percentile variation range of reference sites/data or at a level that does not cause significant risk to rehabilitation.	Cover of exotic species within 0.04 hectare fixed monitoring plots is low	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required). Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				4. Total organic carbon is within 10th 90th percentile variation range of reference sites/data; and Total microbial biomass is within 10th-90th percentile variation range of reference	Soil health is suitable to sustain the target vegetation community(s) (e.g. PCT)	Rehabilitation monitoring reports, independent soil reports (where required) that demonstrate long-term function of rehabilitated landform. Depending on the nature, scale and risks

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				sites/data The ratio of fungus to bacteria (fungal:bacterial) biomass is within 10th-90th percentile variation range of reference sites/data		associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				5. Suitable levels of coarse woody debris have been installed to meet habitat requirements.	Coarse woody debris	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met.
				6. Vertebrate pest species – presence and damage is recorded at a level that does not cause significant risk to rehabilitation. Domesticated stock - presence and damage is recorded at a level that does not cause significant risk to rehabilitation.	Threats to rehabilitation.	Rehabilitation monitoring reports.
				7. Specific habitat structures as required by the development consent, have been installed and are structural sound / stable	Specific habitat structures	Statement provided by suitably qualified ecologist

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A7, J4	Grassy Box Gum Woodland Vegetation Community	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.	Foliage cover of species allocated to the 3 dominant growth form groups for the target PCT as determined by the PCT benchmarks for cover (see Bionet Vegetation Classification or BAM Calculator) is within the 10th-90th percentile variation range of the specified reference sites/data; and, For wooded target PCT(s) only: Stem abundance and diameter at breast height for trees in size classes <5cm, 5-10, 10-20 and 20-30cm is within the 10th-90th percentile variation range of the specified reference sites/data	Cover and abundance of plant growth forms recorded from 0.04 hectare fixed monitoring plots are characteristic of the target vegetation community (e.g. target community type), or an ongoing trend toward becoming characteristic is evident from the monitoring data	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
	A1, A4, A7, J4	Grassy Box Gum Woodland Vegetation Community	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.	Minimum number of species recorded is within the 10th and 90th percentile of reference site values of the target vegetation community	Native plant species recorded from 0.04 hectare fixed monitoring plots are characteristic of the target vegetation community (e.g. target community type)	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A7	Grassy Box Gum Woodland Vegetation Community	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.	1. Litter cover is within 10th-90th percentile variation range of the analogue communities	Indicators of nutrient cycling are suitable for sustaining the targeted vegetation communities (PCT1329/NA237, PCT1383/NA226, PCT1313/NA228, PCT88/NA179 and/or PCT27/NA219)	Biodiversity Monitoring rehabilitation assessment reports demonstrate long-term function of rehabilitated landform (i.e. suitable trends demonstrated).
				2. Second generation individuals of trees are within the 10th-90th percentile variation range of reference sites/data and Number of native plant species flowering / fruiting	Evidence of plant regeneration from 0.04 hectare fixed monitoring plots or a walk over of the ecological rehabilitation area	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				3. Foliage cover of 'high threat exotic' (HTE) weeds (as defined by BAM Calculator) is within 10th-90th percentile variation range of reference sites/data or at a level that does not cause significant risk to rehabilitation.	Cover of exotic species within 0.04 hectare fixed monitoring plots is low	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required). Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				4. Total organic carbon is within 10th 90th percentile variation range of reference sites/data; and Total microbial biomass is within 10th-90th percentile variation range of reference sites/data The ratio of fungus to bacteria (fungal:bacterial) biomass is within 10th-90th percentile variation range of reference sites/data	Soil health is suitable to sustain the target vegetation community(s) (e.g. PCT)	Rehabilitation monitoring reports, independent soil reports (where required) that demonstrate long-term function of rehabilitated landform. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				5. Suitable levels of coarse woody debris have been installed to meet habitat requirements.	Coarse woody debris	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met.
				6. Vertebrate pest species – presence and damage is recorded at a level that does not cause significant risk to rehabilitation. Domesticated stock - presence and damage is recorded at a level that does not cause significant risk to rehabilitation.	Threats to rehabilitation.	Rehabilitation monitoring reports.
				7. Specific habitat structures as required by the development consent, have been installed and are structural sound / stable	Specific habitat structures	Statement provided by suitably qualified ecologist

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A7	Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.	1. Litter cover is within 10th-90th percentile variation range of the analogue communities	Indicators of nutrient cycling are suitable for sustaining the targeted vegetation communities (PCT78/NA193, PCT84/NA191 and/or PCT102/NA181)	Biodiversity Monitoring rehabilitation assessment reports demonstrate long-term function of rehabilitated landform (i.e. suitable trends demonstrated).
				2. Second generation individuals of trees are within the 10th-90th percentile variation range of reference sites/data and Number of native plant species flowering / fruiting	Evidence of plant regeneration from 0.04 hectare fixed monitoring plots or a walk over of the ecological rehabilitation area	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				3. Foliage cover of 'high threat exotic' (HTE) weeds (as defined by BAM Calculator) is within 10th-90th percentile variation range of reference sites/data or at a level that does not cause significant risk to rehabilitation.	Cover of exotic species within 0.04 hectare fixed monitoring plots is low	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required). Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				4. Total organic carbon is within 10th 90th percentile variation range of reference sites/data; and Total microbial biomass is within 10th-90th percentile variation range of reference sites/data The ratio of fungus to bacteria (fungal:bacterial) biomass is within 10th-90th percentile variation range of reference sites/data	Soil health is suitable to sustain the target vegetation community(s) (e.g. PCT)	Rehabilitation monitoring reports, independent soil reports (where required) that demonstrate long-term function of rehabilitated landform. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
				5. Suitable levels of coarse woody debris have been installed to meet habitat requirements.	Coarse woody debris	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met.
				6. Vertebrate pest species – presence and damage is recorded at a level that does not cause significant risk to rehabilitation. Domesticated stock - presence and damage is recorded at a level that does not cause significant risk to rehabilitation.	Threats to rehabilitation.	Rehabilitation monitoring reports.
				7. Specific habitat structures as required by the development consent, have been installed and are structural sound / stable	Specific habitat structures	Statement provided by suitably qualified ecologist

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A7, A8, J4	Grassy Box Gum Woodland Vegetation Community; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Final Landform is safe for future use	The final landform is safe for the intended future use and does not have an impact on public safety or the environment	No signs of land instability or active erosion. The final landform complies with the final landform construction in accordance with the Final Landform and Rehabilitation Management Plan	Rehabilitation monitoring reports
	A1, A3, A4, A8, J4	On lease exploration areas; Shrubby Woodland Vegetation Community	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.	Foliage cover of species allocated to the 3 dominant growth form groups for the target PCT as determined by the PCT benchmarks for cover (see Bionet Vegetation Classification or BAM Calculator) is within the 10th-90th percentile variation range of the specified reference sites/data; and, For wooded target PCT(s) only: Stem abundance and diameter at breast height for trees in size classes <5cm, 5-10, 10-20 and 20-30cm is within the 10th-90th percentile variation range of the specified reference sites/data	Cover and abundance of plant growth forms recorded from 0.04 hectare fixed monitoring plots are characteristic of the target vegetation community (e.g. target community type), or an ongoing trend toward becoming characteristic is evident from the monitoring data	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
	A1, A3, A4, A7	Riverine Woodland Vegetation Community	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.			

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A8, J4	On lease exploration areas; Shrubby Woodland Vegetation Community	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.	Minimum number of species recorded is within the 10th and 90th percentile of reference site values of the target vegetation community	Native plant species recorded from 0.04 hectare fixed monitoring plots are characteristic of the target vegetation community (e.g. target community type)	Before and after photos, rehabilitation monitoring reports, independent ecological reports (where required) that validate rehabilitation completion criteria have been met. Depending on the nature, scale and risks associated with a specific site, achievement of criteria may need to be evaluated over a number of years (e.g. 5 years to 15+ years).
	A1, A3	Riverine Woodland Vegetation Community	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.			
Groundwater	A1, A3, A4, A7, B1, B3, B7, J4, J5	Final void landform; Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; Riverine Woodland Vegetation Community;	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.	1. Water quality discharged from rehabilitated mining operation meet specifications in Environment Protection Licence and or ANZECC guidelines for specific environment.	1. Water quality parameters selected from Australian and New Zealand Guidelines for Fresh and Marine Water Quality 2000 and or Environment Protection Licence	1. Independent hydrological assessment report.

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
		Shrubby Woodland Vegetation Community		2. Post-mining groundwater management and treatment system implemented and operating in accordance with design specifications	2. Design specifications for groundwater management and treatment post-closure, including underground sealing infrastructure (seals, bulkheads etc.)	2. Independent hydrological assessment report.
			Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation	Measured or modelled groundwater level and or flow is consistent with development consent or within an acceptable level of change from a defined reference condition.	Groundwater levels, groundwater flow	Water quality monitoring reports. Independent hydrological assessment report.
Land Contamination	A1, A3, A4, A7, B1, B3, B7, G3, J4	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community; Water storage (excluding final void)	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.	1. Risk of acid rock drainage is minimised	1. Coal seams with NAPP > 0 and/or %S>0.5 will be capped with no less than 80 metres noncarbonaceous material	1. Test reports. Design and as constructed drawings
				2. Risk of coal seam spontaneous combustion minimised	2(a). Coal seams with Intrinsic Spontaneous Combustion Propensity (ISCP) (McCowan et al, 1978) > Class I will be capped with >5m of noncarbonaceous material. 2(b). Coal seams with Self-Heating Temperature (SHT) (US Bureau of Mines, 1989) <100 will be capped with > 5m of non-carbonaceous material.	2. Test reports. Design and as constructed drawings

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				3. Hazardous substances (hydrocarbons/ heavy metals) identified and removed	3. All hazardous substances/materials removed in accordance with relevant procedures and guidelines.	3. Phase 2 audit report(s). Soil and water testing. Certificates of removal. Waste streams tracked.
				4. Contaminated land is identified and removed or remediated	4. Contaminated land remediated in accordance with relevant procedures and guidelines.	4. Phase 2 audit report(s). Soil and water testing. Rehabilitation monitoring reports.
Landform Stability	A1, A3, A4, A7, A8, B1, B3, B7	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Safe, stable and non-polluting.	1. Absence of untreated dispersive soil and spoil likely to result in landform stability issues	Exchangeable Sodium Percentage (ESP) $\leq 6\%$, or as otherwise determined to be appropriate by a suitably qualified person	Grab samples. As constructed reports. Landform erodibility assessment. Rehabilitation monitoring reports.
				2. Landform stability	No visible signs of instability (slumping/cracking)	Biodiversity Monitoring rehabilitation assessment reports. Rehabilitation monitoring reports.
				3. Soil surface cover	Soil surface $\geq 70\%$ vegetative cover	Biodiversity monitoring rehabilitation assessment reports
				4. No uncontrolled access	Rehabilitation areas clearly defined and access restricted	Inspection report, including photographs

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method	
				5. Minimal active erosion	No erosion rills or gullies that require ongoing management and maintenance works and no evidence of tunnel erosion.	Biodiversity Monitoring rehabilitation assessment reports. Rehabilitation monitoring reports.	
				6. Landform slopes are constructed to stable grade	Slope gradient ≤5° or as otherwise determined to be stable by a suitably qualified person.	As constructed reports. Geotechnical stability report.	
	J4	Grassy Box Gum Woodland Vegetation Community; Shrubby Woodland Vegetation Community		1. Low wall slopes are constructed to stable grade	Linear batter of gradient ≤10° (17.5%) at a height of 20 m or as otherwise determined by a suitably qualified person.	As constructed reports. Geotechnical stability report	
				2. High wall slope – in situ rock materials	Scarp retreat rates equivalent to natural conditions as determined by a suitably qualified person	As constructed reports. Geotechnical stability report	
				3. High wall slope – nonrock/weathered materials	Slopes regraded to ≤10° (17.5%) at a height of 20 m or as otherwise determined by a suitably qualified person.	As constructed reports. Geotechnical stability report	

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				4. Absence of untreated dispersive soil and spoil likely to result in landform stability issues	Exchangeable Sodium Percentage (ESP) ≤6%, or as otherwise determined to be appropriate by a suitably qualified person.	Grab samples. As constructed reports. Landform erodibility assessment. Rehabilitation monitoring reports.
				5. Landform stability	No visible signs of instability (slumping/cracking)	Biodiversity Monitoring rehabilitation assessment reports Rehabilitation monitoring reports.
				6. Minimal active erosion	No erosion rills or gullies that require ongoing management and maintenance works and no evidence of tunnel erosion	Biodiversity Monitoring rehabilitation assessment reports
	G3	Water storage (excluding final void)		1. Absence of untreated dispersive soil and spoil likely to result in landform stability issues	Exchangeable Sodium Percentage (ESP) ≤6%, or as otherwise determined to be appropriate by a suitably qualified person	Rehabilitation monitoring reports. Landloch gully activity rating system (2003)
				2. Landform stability	No visible signs of instability (slumping/cracking)	Biodiversity Monitoring rehabilitation assessment reports. Rehabilitation monitoring reports.
			3. Minimal active erosion	No erosion rills or gullies that require ongoing management and maintenance works and no evidence of tunnel erosion.	Biodiversity Monitoring rehabilitation assessment reports. Rehabilitation monitoring reports.	

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A7, A8, B1, B3, B7, J4	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Landform generally blends in with the surrounding landscape.	1. Landform constructed to detailed landform design which integrates with the surrounding landform	Landform design is compliant with Conceptual Final Landform design within SSD 09_0182. Landform constructed as per detailed landform design. Landform is assessed to blend in/integrate with surrounding landform (wherever possible).	As constructed final landform survey. Visual and landscape assessment by suitably qualified person
				2. Free draining landform	Landform is shaped to avoid ponding, to maximise sheet flow and minimise concentration of flows (wherever possible).	As constructed reports. Rehabilitation monitoring reports.
Removal of Infrastructure	A1, A3, A4, A7, A8, B1, B3, B7, G3	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community; Water storage (excluding final void)	All open cut mining infrastructure decommissioned and removed.	1. Disconnection of services (including power, communications and water)	Services disconnected and removed.	Inspection report
				2. Infrastructure and services removed	Removal of infrastructure and services	Inspection report
				3. Dams and sediment management structures removed	Dams removed apart from those required for POLU purposes	Rehabilitation monitoring reports

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	A1, A3, A4, A7, A8, B1, B3, B7	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community.	All open cut mining infrastructure decommissioned and removed.	4. Roads and hardstand surfaces removed	Bitumen and gravel roads and hardstands removed	Inspection report
	A1, A3, A4, A7, A8, B1, B3, B7	Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community.	Exploration drill holes / groundwater piezometers decommissioned and sealed.	Exploration drill holes/groundwater piezometer stand pipes removed and sealed	Bentonite seal and remove standpipe	Rehabilitation completion report
Retention of Infrastructure	G3	Water storage (excluding final void)	Any infrastructure that is to be retained as part of the final landuse (subject to agreement with the Resources Regulator) must be safe and not pose any hazards to the community.	Potential hazards have been effectively isolated and secured	Potential hazards (e.g. electrical, mechanical) have been effectively isolated and secured.	Statement provided by suitably qualified engineer
	A1, A3, A4, A7, A8, B1, B3, B7	Grassy Box Gum Woodland Vegetation Community; Native pasture for low	Constructed landforms drain to	1. Surface runoff does not impact downstream properties	Surface runoff is diverted to neighbouring drainage lines	Water monitoring reports

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
Surface Water		intensity grazing purposes; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	the natural environment.	2. Water / sediment management structures incorporated into final landform to convey surface runoff from constructed mine landform	Water / sediment management structures installed as per design.	As constructed reports. Rehabilitation monitoring reports. Assessment from suitably qualified person.
				3. Integrity and functionality of water/sediment management structures	No evidence of erosion requiring ongoing management and maintenance.	Water monitoring reports. Rehabilitation monitoring reports.
				4. Water management structures are stable	No evidence of active erosion within the water/sediment control structures, identifying that these structures can be removed from final landform (where required).	Rehabilitation monitoring reports.
	A1, A3, A4, A7, A8	Grassy Box Gum Woodland Vegetation Community; On lease exploration areas; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community	Water quality non-polluting and appropriate for conservation end land use.	Water quality of surface runoff and seepage meet specifications in EPL and/or ANZ Guidelines 2018 for specific environment	Water quality meets parameters suitable for land use chosen from Australia and New Zealand Guidelines for Fresh and Marine Water Quality 2000.	Water monitoring reports

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
	B1	Native pasture for low intensity grazing purposes	Water quality non-polluting and appropriate for agricultural end land use.	Water quality of surface runoff and seepage meet specifications in EPL and/or ANZ Guidelines 2018 for specific environment	Water quality meets parameters suitable for land use chosen from Australia and New Zealand Guidelines for Fresh and Marine Water Quality 2000.	Water monitoring reports
	B3, B7	Native pasture for low intensity grazing purposes	Water quality non-polluting and appropriate for intended final land use.	Water quality of surface runoff and seepage meet specifications in EPL and/or ANZ Guidelines 2018 for specific environment	Water quality meets parameters suitable for land use chosen from Australia and New Zealand Guidelines for Fresh and Marine Water Quality 2000.	Water monitoring reports
	G3	Water storage (excluding final void)	Runoff water quality from mine site does not present a risk of environmental harm	1. Rock scour protection	Rock scour protection implemented to water management structure(s) as determined by a suitably qualified expert.	Final landform survey

Objective Category	Spatial Reference /s	Domains	Approved Objective	Proposed Completion Criteria	Proposed Completion Criteria Indicator	Proposed Validation Method
				3. Water management structures are stable	No evidence of active erosion or failure of water management structures	Rehabilitation monitoring reports
Water approvals	A1, A3, A4, A7, B1, B3, B7, G3, J4, J5	Final void landform; Grassy Box Gum Woodland Vegetation Community; Native pasture for low intensity grazing purposes; Riverine Woodland Vegetation Community; Shrubby Woodland Vegetation Community; Water storage (excluding final void)	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take	Water approvals / licences are granted by relevant NSW Government Agency	Final landform considers advice from relevant Government Agency whether sufficient licence shares are available in the water source to account for water stored in voids and dams in the proposed final landform	Confirmation from relevant Government Agency that relevant water approvals / licences are able to be granted

4.2 Rehabilitation objectives and rehabilitation completion criteria – Stakeholder Consultation

Extensive consultation has been undertaken throughout development of the BCM, including liaison with government agencies, the community and Aboriginal community groups, as detailed in the following subsections. Specific consultation undertaken by BCOPL for the preparation of historical Mining Operations Plans is summarised below.

BCOPL has undertaken ongoing consultation with the agencies listed in **Table 4-2** throughout the approvals process for the BCM. The rehabilitation objectives, completion criteria and indicators were initially developed for inclusion within the latest version of the BCM Mining Operations Plan Amendment A dated March 2020 (MOP) which was approved by the Resources Regulator. A comprehensive stakeholder engagement program was undertaken as part of the process for obtaining the 2012 MP 09_0182, details of which are provided in the 2010 EA (Hansen Bailey, 2010).

Table 4-2: Summary of agency consultation undertaken over the life of the project

Agency	Issues
DPHI (formerly DPE and formerly DP&E)	Consultation in relation to the 1989 Development Consent (DA 36/88), the current MP 09_0182 and various compliance issues.
DCCEEW – Water Division (formerly DPE - Water Division and formerly DPI Water)	Consultation in relation to licences required under the <i>Water Act 1912</i> , consent under the <i>Water Management Act 2000</i> , associated Water Environmental Management Plans and water modelling undertaken.
	Consultation in relation to Part 3A licence applications.
ENSIS	Consultation with ENSIS, a joint venture of CSIRO and SCION in relation to the development of the RMP.
Water NSW	State Water Corporation in relation to licence details under the <i>Water Act 1912</i> and the <i>Water Management Act 2000</i> .
Department of Primary Industries and Regional Development (DPIRD) (formerly Department of Primary Industries (DPI) and formerly Department of Industry (DoI))	Former Department of Lands (now DoI – Lands & Water) (Soil Conservation Service) in relation to the assessment of Rural Land Capability and development of the RMP.
	Former NSW Department of Industry, DoI (Fisheries) in relation to Part 3A licence applications.
	Former NSW Department of Industry, DoI (Agriculture) in relation to the RMP.
DCCEEW – Biodiversity Conservation and Science Division (BCSD) (formerly DPE - Biodiversity Conservation and Science Division (BCSD) and formerly OEH)	Former OEH in relation to flora and fauna, archaeology, EPL application, mine rehabilitation and green offsets.
Forests NSW	Forestry Corporation of NSW (Forests NSW) in relation to the Project property management and the RMP.
Department of Primary Industries and Regional Development – Resources NSW - Resources Regulator (formerly DRE, DRG)	Resources Regulator within the Resources NSW which forms part of the Department of Primary Industries and Regional Development in relation to EMP requirements, historical MOP requirements, lease issues and rehabilitation objectives.

Agency	Issues
TfNSW (formerly RMS)	NSW Roads and Maritime Services (RMS) in relation to traffic and transport requirements, particularly with regard to the intersections and bridges over the Kamilaroi Highway.
NSC	Presentation to the NSC Development Committee and on-site field days. Various planning and engineering staff have been consulted with respect to roads and planning issues. A member of NSC is also a member of the BCM Community Consultative Committee (CCC).
GSC	GSC in relation to planning and transport issues.
North West LLS (formerly Namoi CMA)	North West LLS in relation to the development of the previous version of the RMP (which has now been incorporated into this RMP).

A summary of key stakeholder expectations and agreements in relation to post mining land use, rehabilitation objectives and completion criteria is presented in **Table 4-3**. These include submissions to the then PAC in relation to the MP 09_0182 and comments received from the DPHI have been considered, where relevant. It should be noted that this version of the RMP to address the Rehabilitation Reforms has relied upon post mining land use, rehabilitation objectives and completion criteria previously presented within the MOP/RMP documents and will be subject to ongoing consultation throughout the life of the BCM.

Table 4-3: Stakeholder Expectations

Stakeholder/Source	Concern	Comment
PAC Submissions (various) (2011)	The extent of the final void should be minimised as much as possible to reduce the long-term impacts on the landscape.	The nature and extent of the final void is addressed in this RMP.
	The proponent should work with adjoining mines to minimise final landscape/ biodiversity impacts and enhance biodiversity and environmental management outcomes.	BCOPL and Whitehaven Coal have developed regional strategies for environmental management, required as part of the MP 09_0182. These include strategies for the sharing of environmental monitoring networks. An agreement is in place between BCM and Tarrawonga Coal Mine to ensure that an integrated final landform is established in accordance with relevant conditions of the SSD approvals for both mines.
	The ability to rehabilitate the forest to its pre-mining conditions is doubtful; Concern that soil depths suggested are insufficient for establishment of rehabilitation.	The RMP outlines the approach that will be taken to rehabilitation, including topsoil management and placement. Topsoil depths have been researched as part of this and are considered adequate for sustaining proposed vegetation communities.
References to DPHI comments on the RMP (received 2013)	The final mix and areas of natural vegetation communities will need to be in accordance with the approved Biodiversity Management Plan.	The final mix and areas of vegetation have been established based upon conditions of the MP 09_0182, commitments in the EA and other requirements. This is addressed and documented in the BMP and this RMP.

Stakeholder/Source	Concern	Comment
	Investigations into proposed final landforms should be considered to start earlier to allow for alternative landform designs to be considered.	BCOPL will consider accelerating studies into alternative final landform designs.
	Land zoning post closure will need to be considered and addressed.	A strategy for final land uses is included in the RMP. A rezoning application may be required to achieve final land uses.
	Need to ensure consistency between the RMP, the MOP and mine closure planning.	<i>Mining Amendment (Standard Conditions of Mining Leases – Rehabilitation) Regulation 2021</i> introduces new standard mining lease conditions for mine rehabilitation including the requirement for a Rehabilitation Management Plan (this document) to replace the MOP, former RMP and mine closure planning.
	Final landforms should provide information on land capability and agricultural suitability.	Land capability and agricultural suitability is addressed in this RMP.
	Need to consider Commonwealth approval conditions in preparation of management plans.	The Commonwealth approval has been considered in the preparation of management plans. In particular, extensive changes have been made to the BMP, Site Water Balance, Surface Water Management Plan, Water Management Plan and Groundwater Management Plan in response to the Commonwealth approval.
DPHI comments on the RMP (received February 2015)	Update references to approval conditions following granting of MOD 5. Update ENV-RHB-PRO-001 Soil Management Protocol (SMP) with domains consistent with target vegetation communities in RMP.	The previous version of the RMP and MOP, which has now been incorporated into this RMP was updated to address DPHI review comments and issued to relevant agencies for consultation. Subsequent feedback from agencies has been addressed in this RMP.
Resources Regulator comments on the RMP (received 13 November 2024)	Update the RMP and associated rehabilitation reform documents to reflect the grant of ML 1883 and the receipt of the relevant approvals for MOD 8. Update the RMP to be consistent with the Resources Regulator Form and Way.	The grant of ML 1883 and receipt of relevant approvals for MOD 8, including changes to the final landform design have been considered in the latest revision of this RMP. The latest revision of this RMP has been updated to remain consistent with the Resources Regulator Form and Way.

Further consultation with the Rural Fire Service and Forests NSW will continue to occur to discuss the retention and reinstatement of access roads for firefighting purposes throughout the Final Landform Design. Accordingly, future iterations of this RMP will reflect the outcomes of this consultation and future processes for consideration in the Final Landform.

Feedback that has been received over rehabilitation activities at the BCM as summarised above has been considered and incorporated into this RMP. This RMP, including the proposed Rehabilitation Outcomes Documents (including the proposed Final Landform and Rehabilitation Plan and the proposed Rehabilitation

Objectives and Completion Criteria) were distributed to the relevant regulatory stakeholders for review and comment. BCOPL has considered the comments received, and revised Rehabilitation Outcomes Documents have been submitted to the Resources Regulator for approval.

Community Consultation

BCOPL has undertaken extensive community consultation as part of the development and operation of the BCM. This has included the establishment of the BCM CCC. BCOPL also maintains ongoing communication with residents immediately neighbouring the BCM through direct correspondence. Where possible, BCOPL has utilised local residents and contractors throughout the development and operation of the BCM.

BCOPL also maintains a community enquiry and complaints hotline **1800 BOGGABRI** (1800 2644 2274).

Aboriginal Consultation

Consultation with Aboriginal stakeholders has been undertaken on an ongoing basis as part of previous approvals processes and development of the site's Heritage Management Plan (HMP). A representative of the Aboriginal stakeholder group is also part of BCOPL's CCC.


To facilitate ongoing Aboriginal stakeholder consultation, an Aboriginal Stakeholder Consultative Forum (ASCF) has been initiated. The ASCF is open to all stakeholders involved in the various BCOPL projects. The ASCF provides a platform for information exchange between BCOPL, stakeholders and is a method of efficiently disseminating information to the Aboriginal community.

Key concerns from the ASCF have been mostly related to preservation of cultural heritage, access to land and employment opportunities.

5 FINAL LANDFORM AND REHABILITATION PLAN

BCOPL submitted the spatial theme data to the NSW Resources Regulator through the mine rehabilitation portal to support the Final Landform and Rehabilitation Plan on the 25 November 2022. Spatial data was prepared using theme data submitted to the mine rehabilitation portal as per *Form and Way: Rehabilitation Objectives, Rehabilitation Completion Criteria and Final Landform and Rehabilitation Plan for Large Mines* (NSW Resources Regulator, 2021). On 1 February 2023, the Resources Regulator refused the spatial theme data and provided comments to be addressed and requested that the spatial theme data be resubmitted onto the mine rehabilitation portal. The revised spatial theme data was submitted on the mine rehabilitation portal on 15 and 16 March 2023. The Resources Regulator provided further comments on 6 September 2023 on the final landform and rehabilitation plan spatial data. On 29 September 2023, revised spatial data addressing the Resources Regulators comments was uploaded on the rehabilitation portal.

Revised spatial theme data for the Final Landform and Rehabilitation Plan was submitted to the mine rehabilitation portal in March 2025. This spatial theme data considers the grant of ML 1883 on 24 September 2024, and the receipt of final state and commonwealth approvals for MOD 8 to MP 09_0182 (as amended). A PDF copy of the proposed Final Landform and Rehabilitation Plan (which is yet to be endorsed by the Resources Regulator) spatial data has been printed from the portal and is included in **Figure 5-1**.

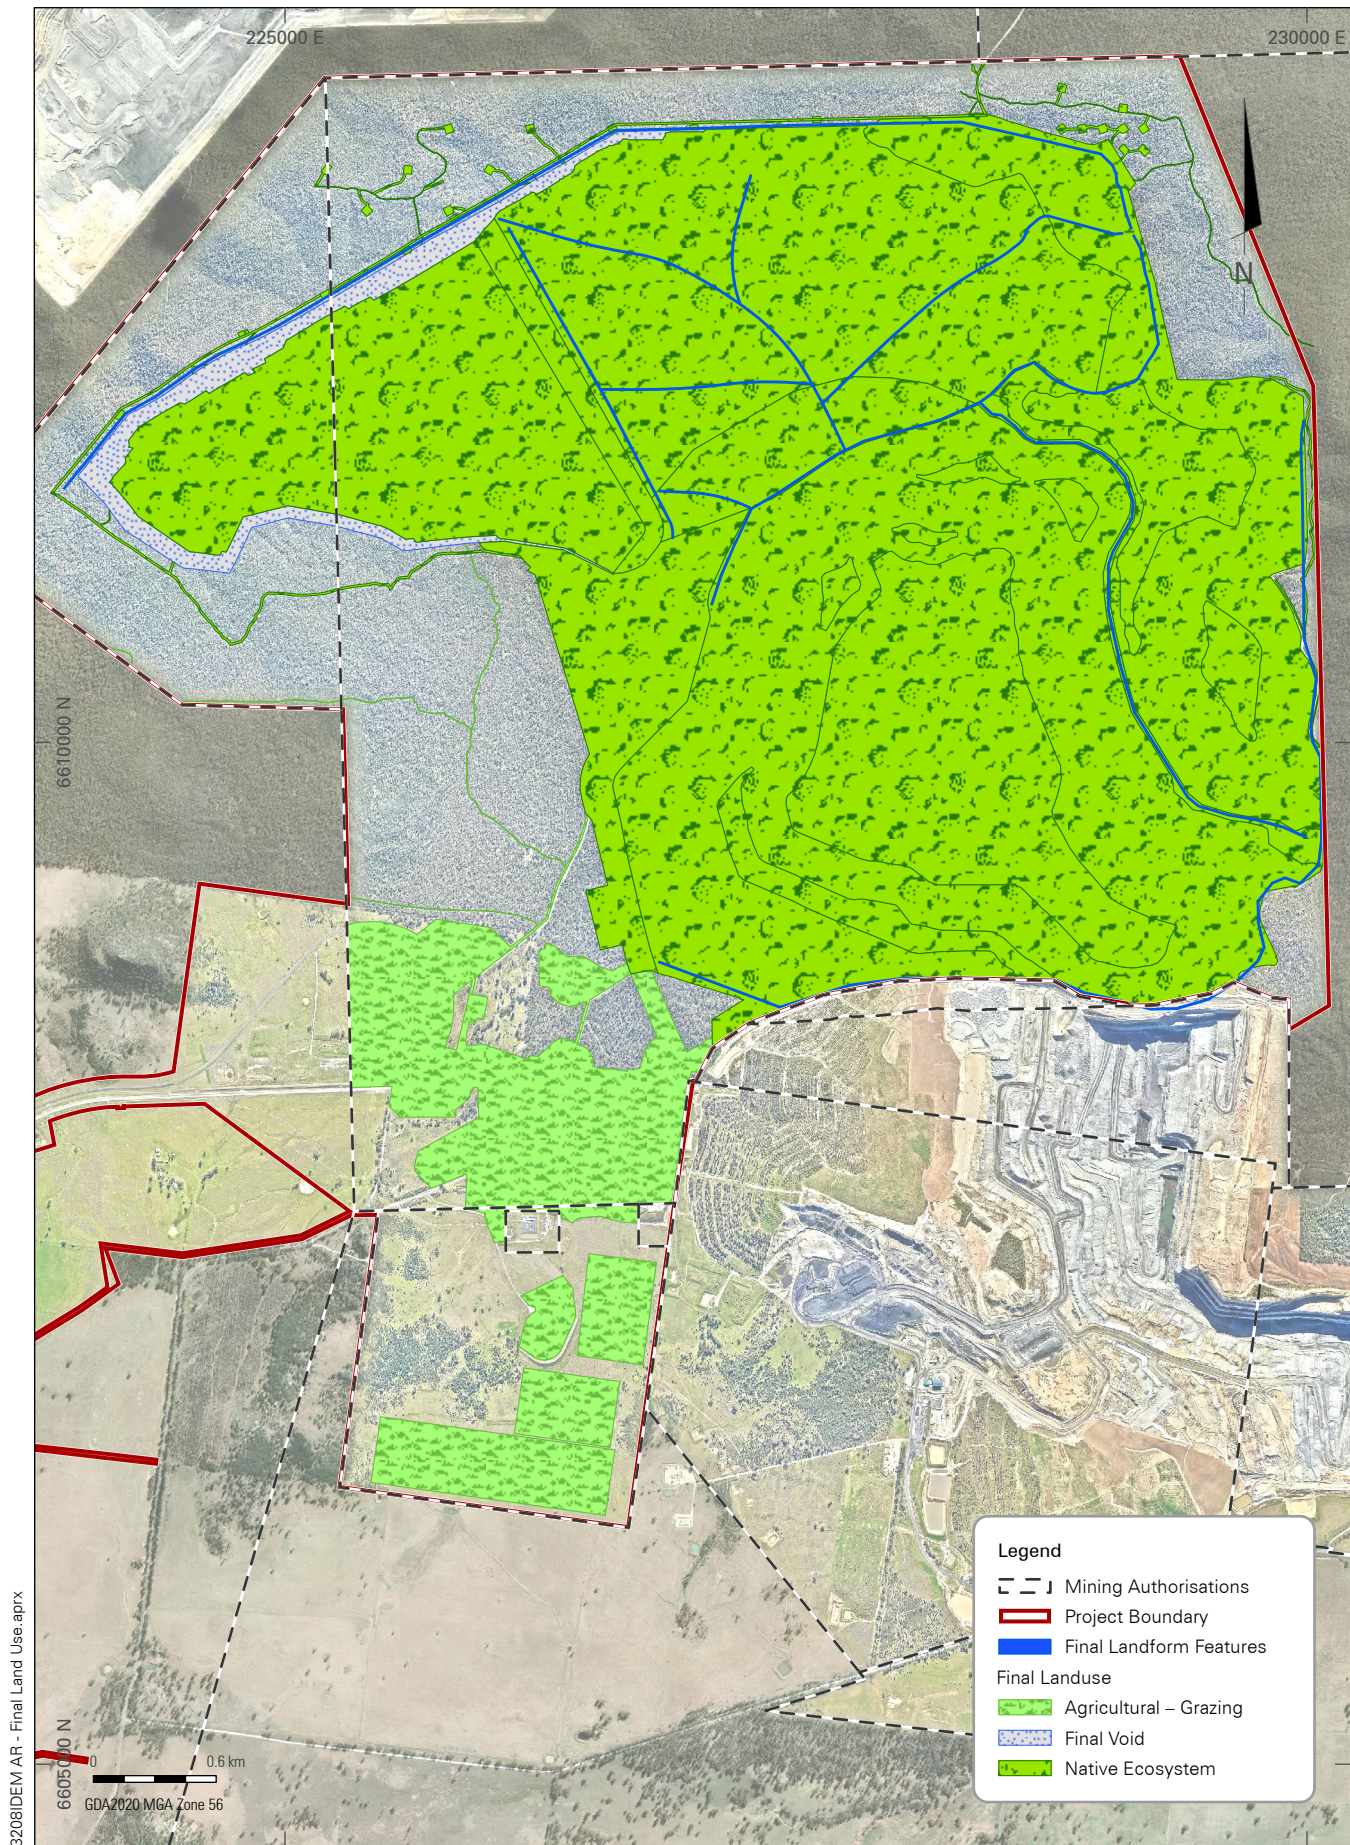

BOGGABRI COAL MINE

Final Landform and Rehabilitation Plan

FIGURE 5-1

6 REHABILITATION IMPLEMENTATION

6.1 Life of Mine Rehabilitation Schedule

MP 09_0182 provides approval for mining operations to continue until the end of 2036. However, additional coal resources are known to exist within the BCM mining authorities which may be mined subject to the relevant approval under the EP&A Act. The mining of the additional coal resources within the existing mining authorities was contemplated within the Boggabri EA, which illustrated a Year 28 Mine Plan. MOD 8 (as amended) was granted approval on 22 January 2024 for an increase to the maximum depth of mining down to the Templemore Coal Seam to recover an additional 61.6 million tonnes of ROM coal and extend mine life by 6 years. MOD 8 was subsequently granted EPBC approval 2021/8875 on 19 December 2025. Actions associated with MOD 8 are therefore approved subject to relevant EPBC conditions.

BCOPL is currently preparing an application to seek approval to mine additional areas to the north of the existing approved Mine Disturbance Boundary (MOD 10 to MP 09_0182). Similarly, this RMP will be reviewed to reflect changes associated with MOD 10 following approval.


Throughout the life of mining at BCM, the rehabilitation program is primarily focussed on rehabilitating the Overburden Emplacement Areas (OEAs) which have been developed to the approved Conceptual Final Landform design, temporary rehabilitation of unused areas around infrastructure areas and the establishment of long term water management structures. Rehabilitation programs are also being undertaken to enhance the habitat of the BCOPLs regional BOAs. These rehabilitation programs on the mine site and the BOAs aim to establish a regional east west regional biodiversity corridor which will extend between the Namoi River and the Pilliga State Forest to the west and the Nandewar Ranges to the east of the BCM.

Rehabilitation at BCM is undertaken progressively as areas are no longer required for operational purposes become available. A vast majority of the southern and western faces of the main OEA have now been subject to mine rehabilitation (and have primarily progressed into the Ecosystem and Land Use Development phase). **Figure 6-1** illustrates the status of mining and rehabilitation activities at BCM as at the end of December 2023. As mining operations advance to the north and north west, the advancing OEAs will be progressively rehabilitated.

Figure 6-2 and **Figure 6-3** illustrate the conceptual staged plans from the Boggabri EA (2010) for Years 10 (2022) and 21 (2033). BCOPL received state and commonwealth approval to modify MP 09_0182 (MOD 8 as amended) to facilitate some changes to the approved mine plans. These mine plan changes will result in minor adjustments to the progression of mining operations towards the north and will also result in adjustments to the approved Conceptual Final Landform design. The approved MOD 8 mine plans are provided in **Figure 6-4** and **Figure 6-5**.

BCOPL is progressing with a further application to modify MP 09_0182 (MOD 10) to facilitate the extension of mining operations into an area outside of the approved Mine Disturbance Boundary, however remaining within the approved BCM Project Boundary. This modification to MP 09_0182 will result in further changes to the currently approved mine plans and adjustment to the approved Conceptual Final Landform. Accordingly, future revisions of this RMP (post approval of MOD 10) will include additional staged plans to present the scheduled mining and rehabilitation progression out to the end of approved mining operations.



The existing mine infrastructure areas, CHPP and train loadout facilities will remain in place throughout the remainder of approved mining operations. At the completion of mining, all mining related infrastructure will be decommissioned and removed to enable these areas to be rehabilitated to the approved final land uses.


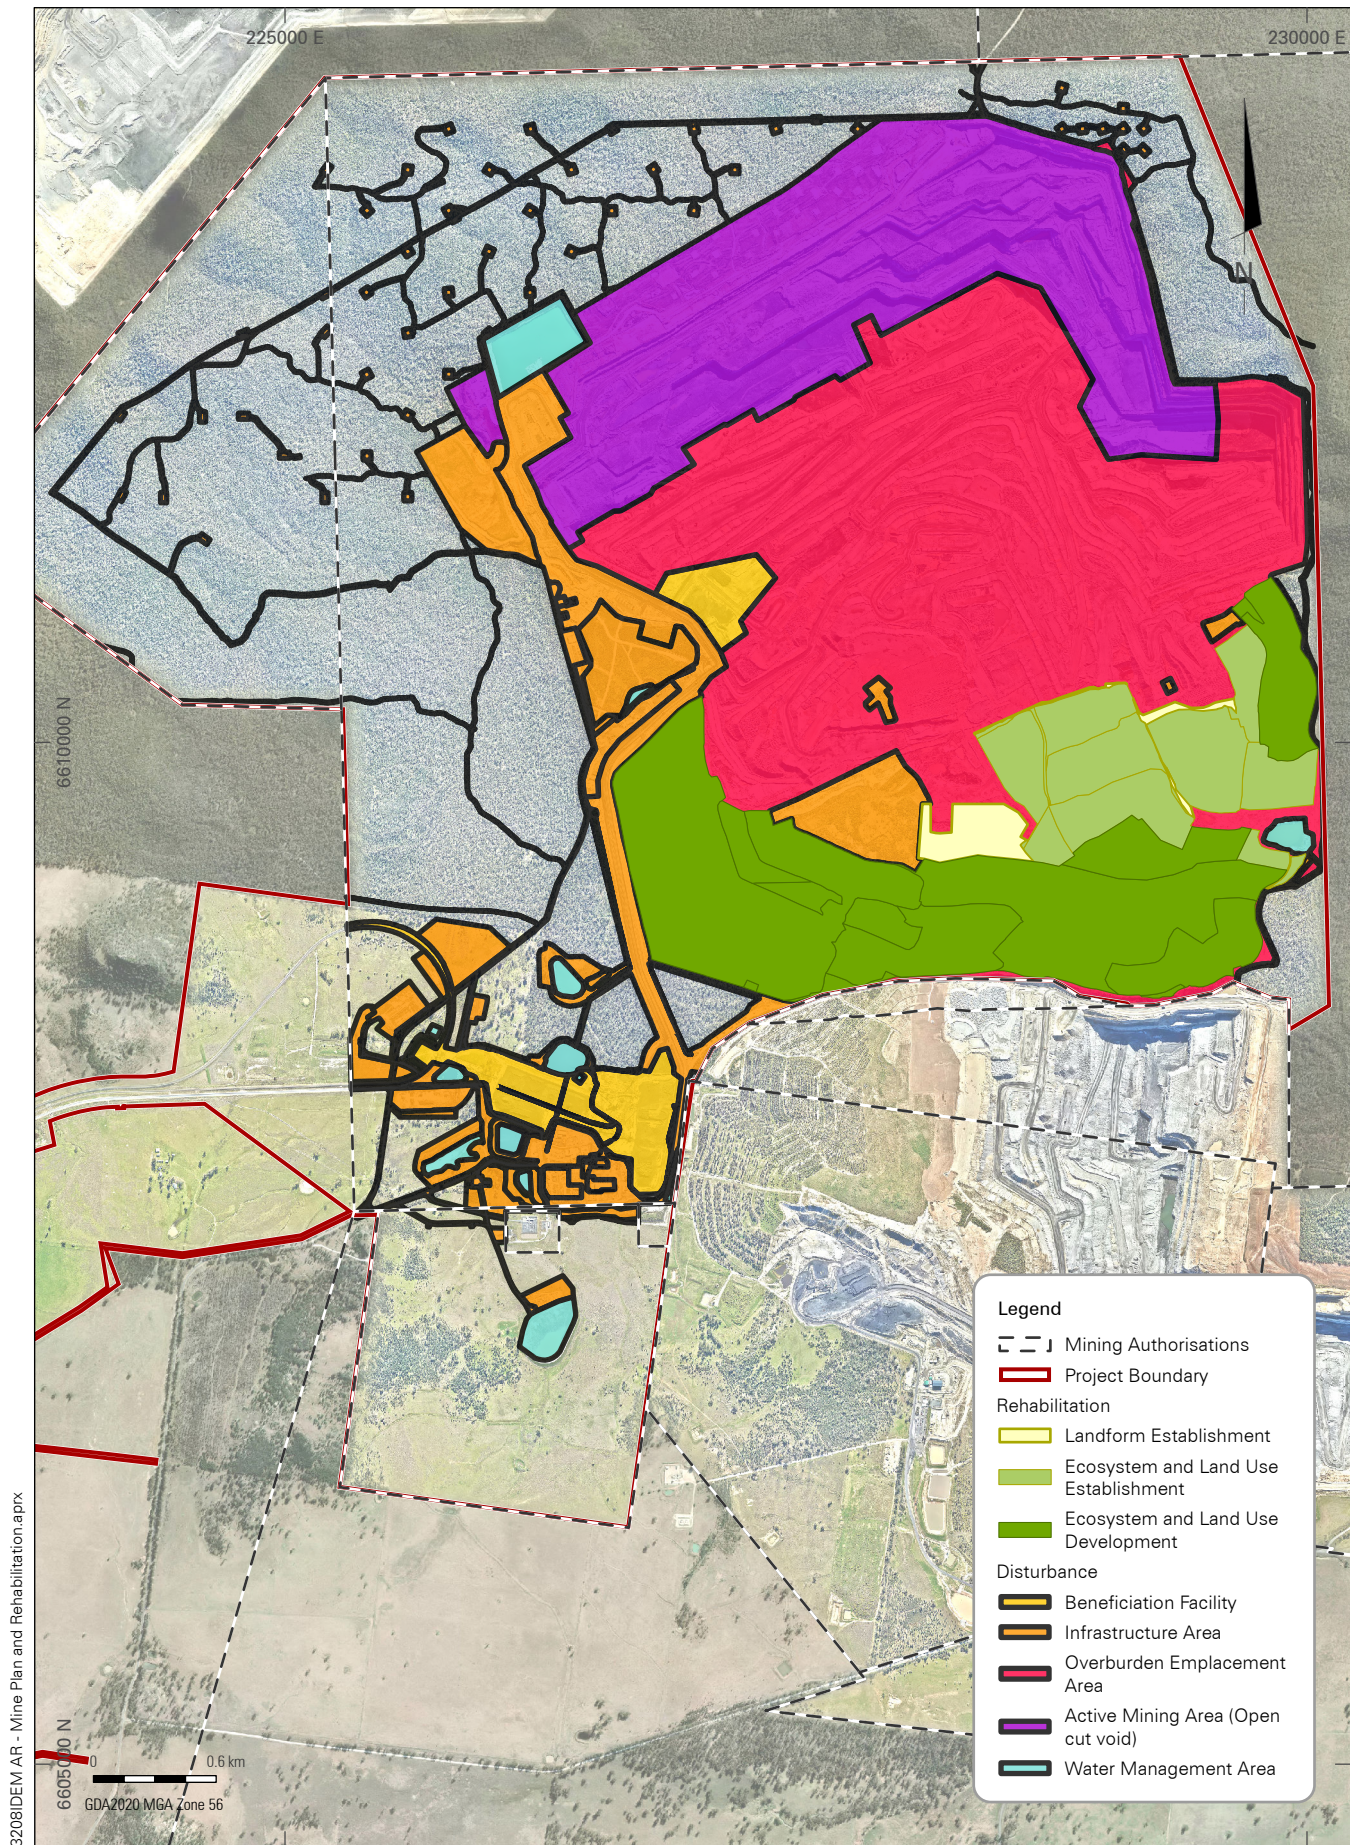


BOGGABRI COAL MINE


Mine Plan and Rehabilitation

FIGURE 6-1

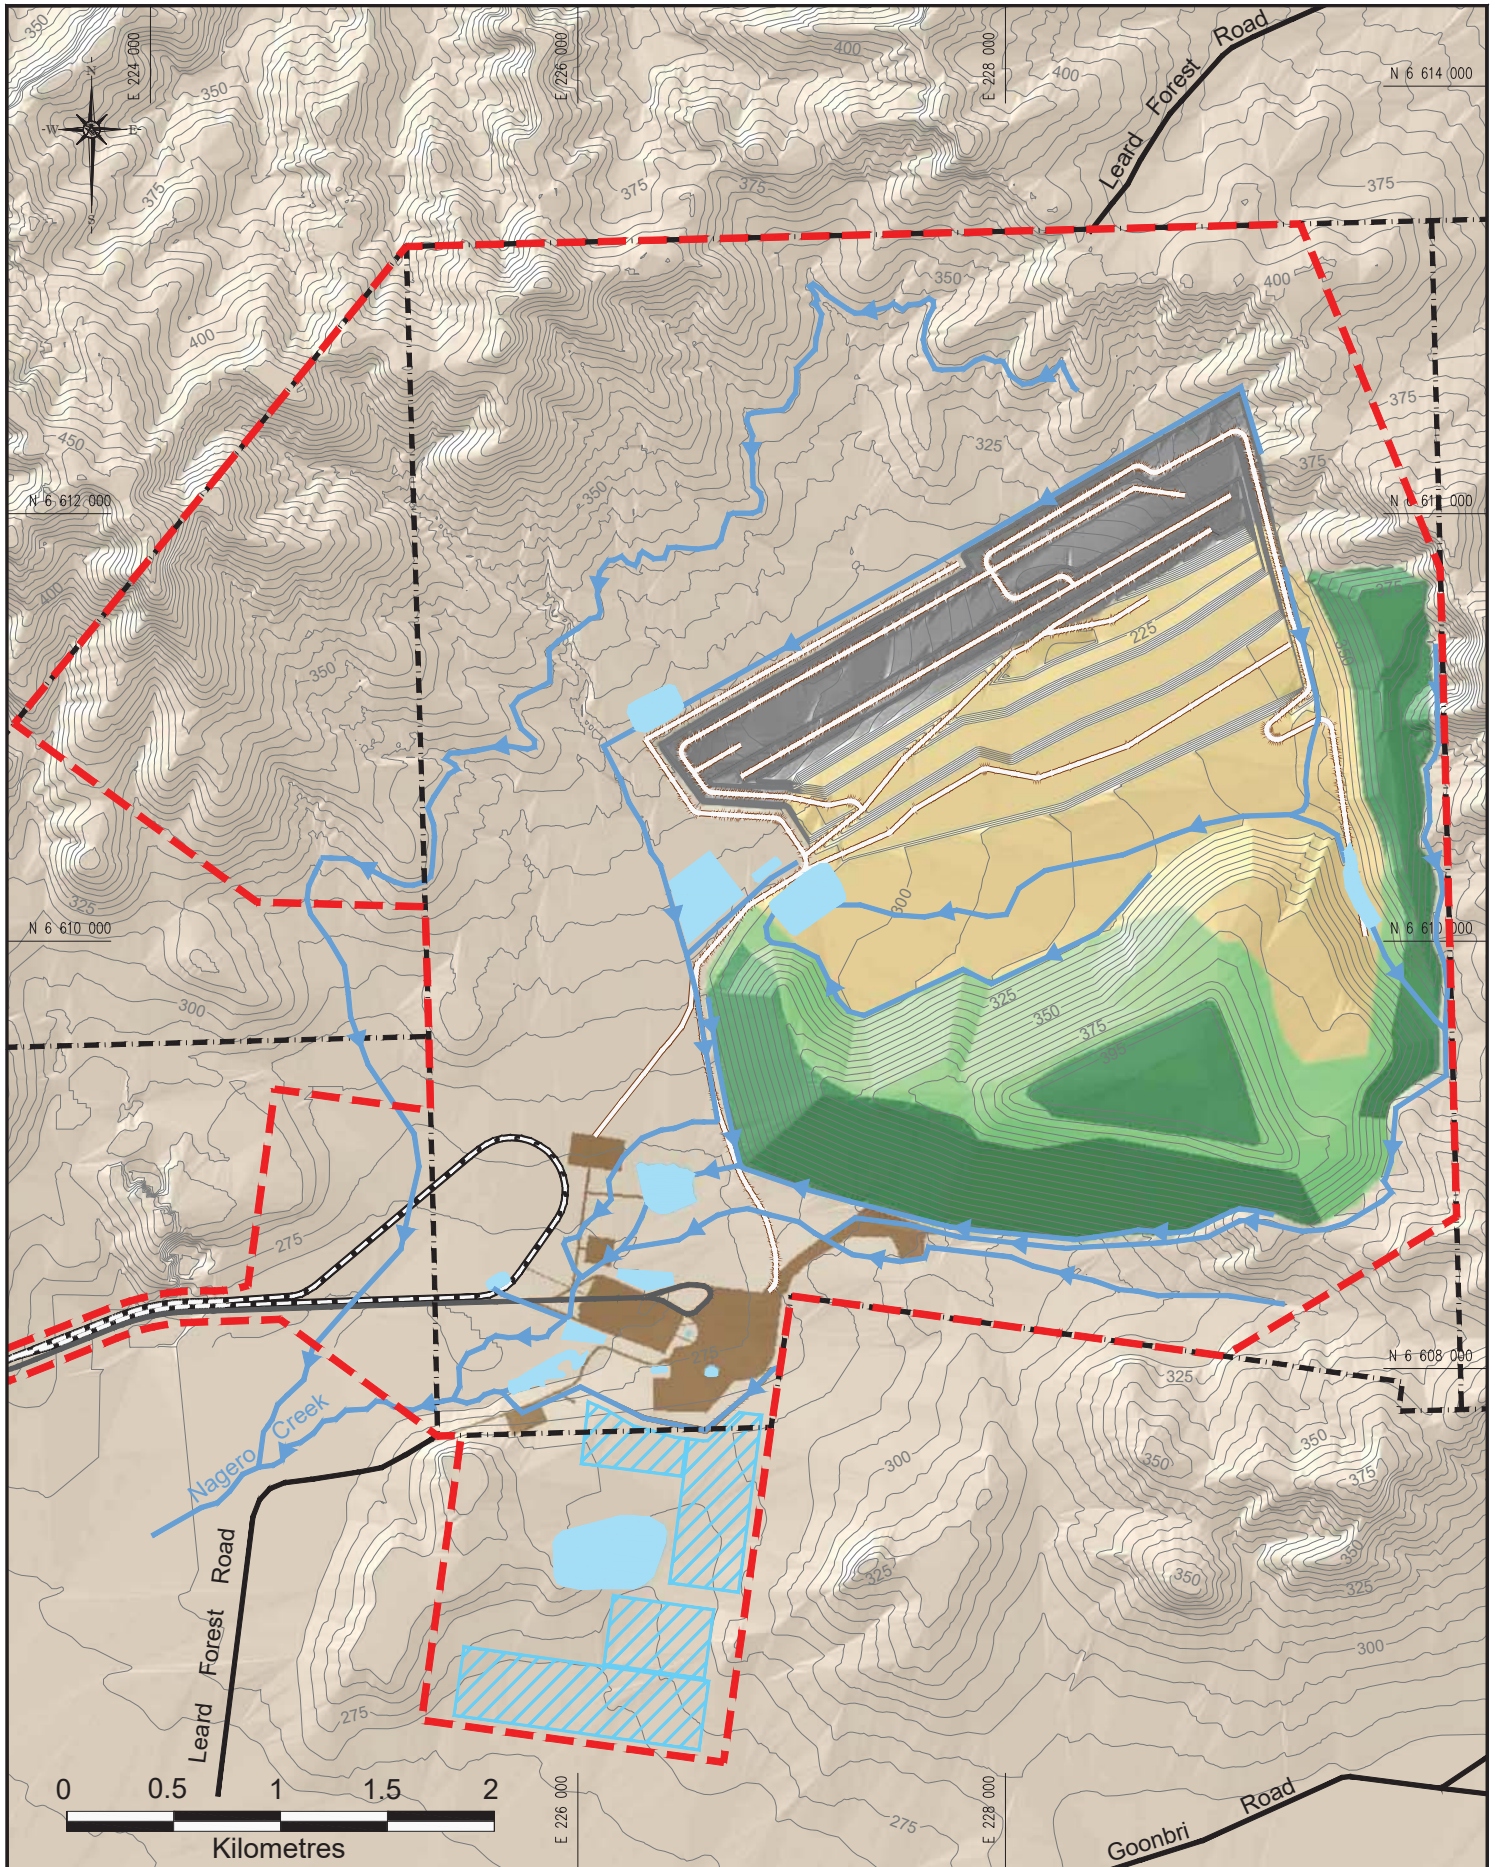

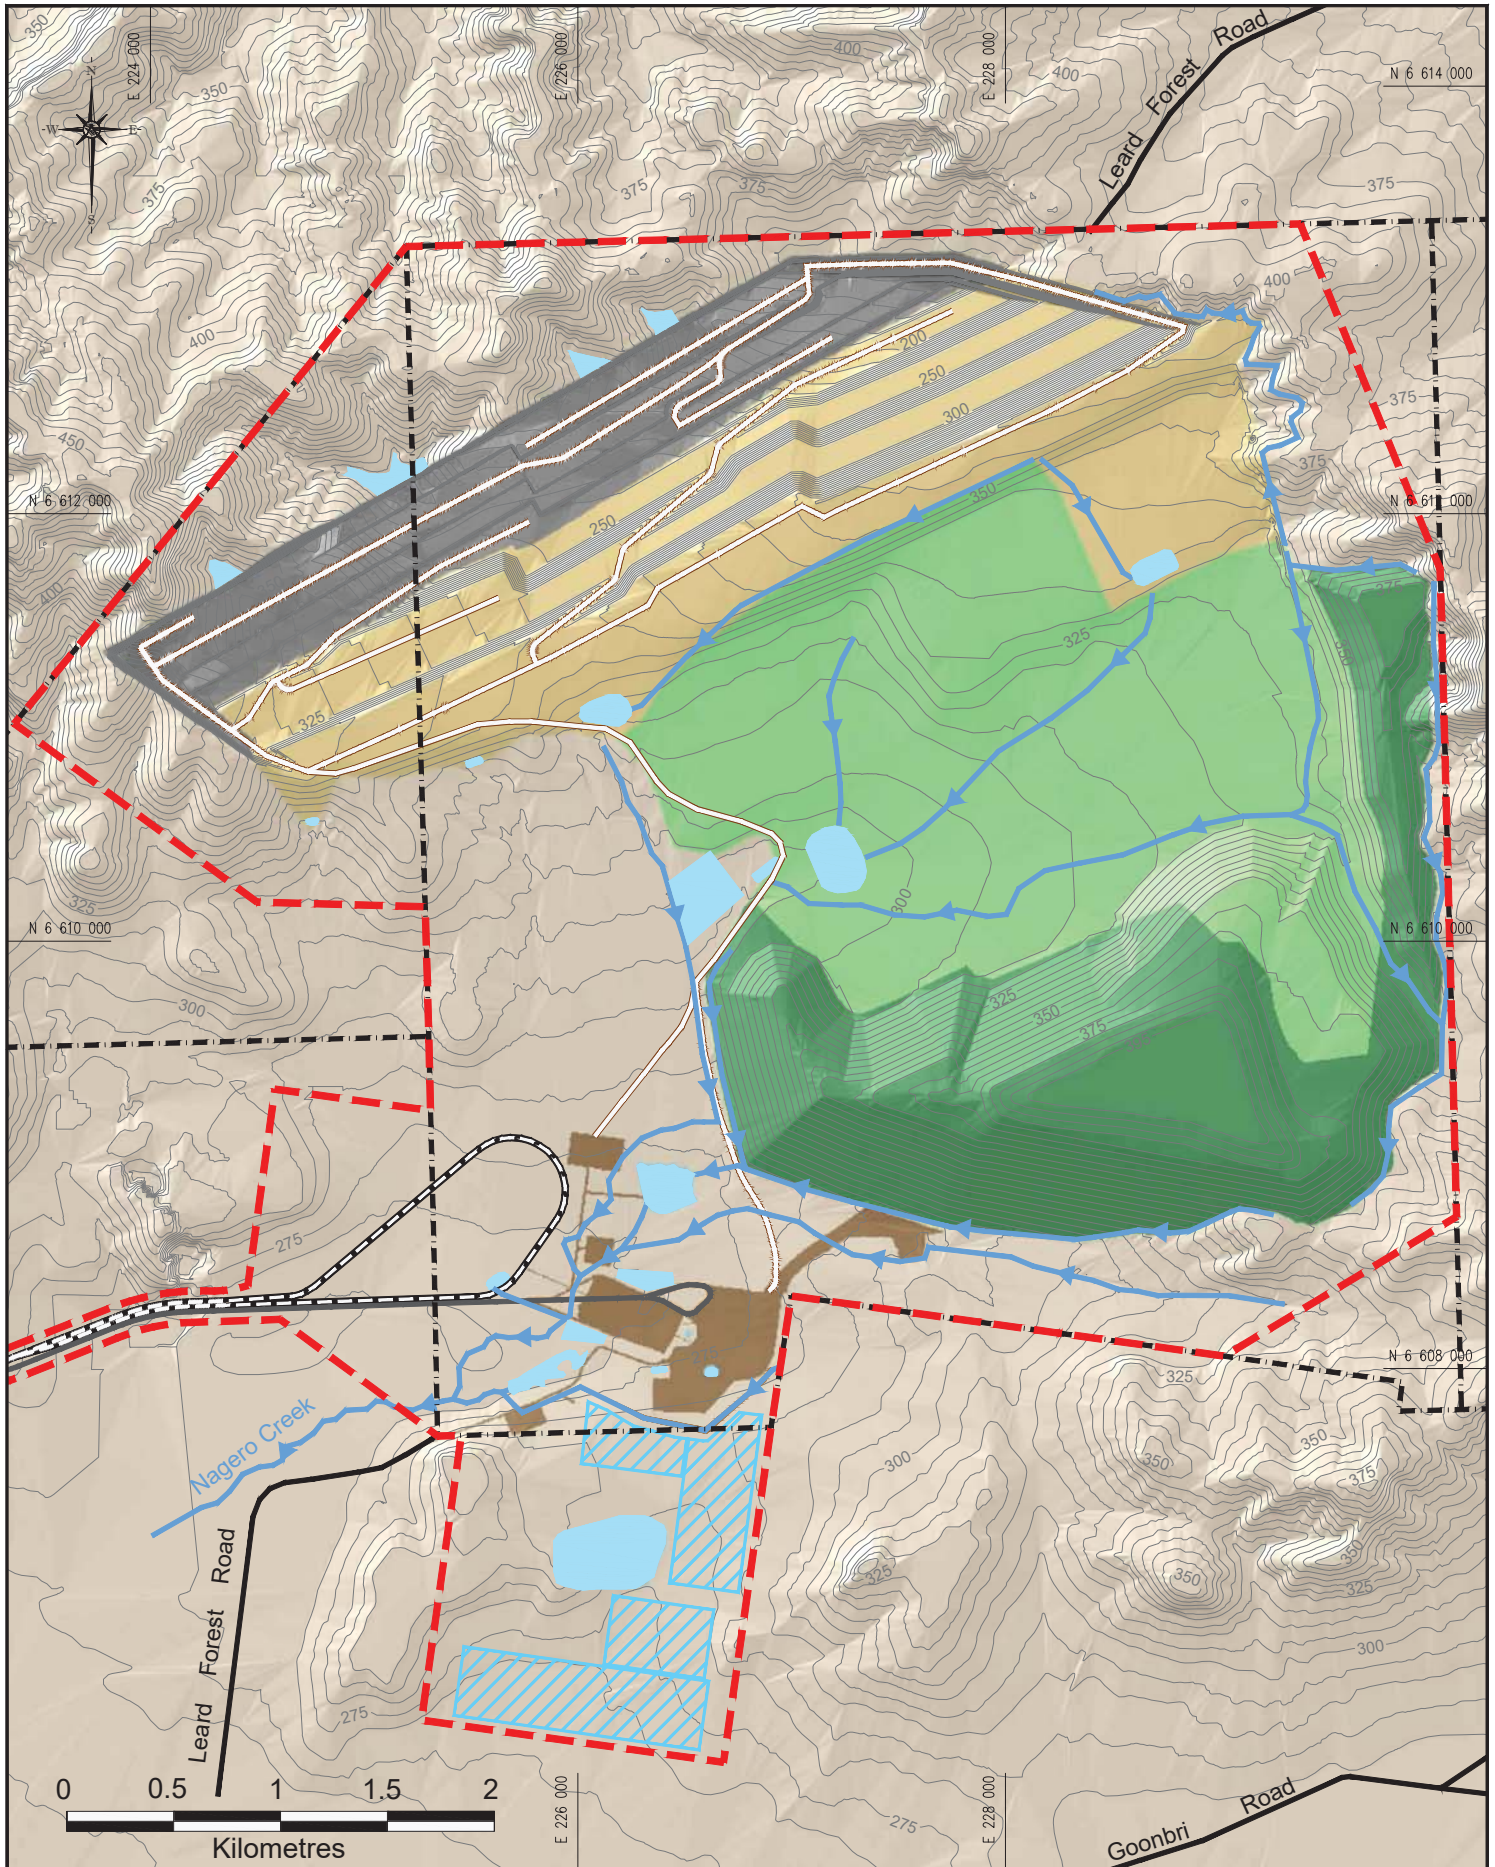

BOGGABRI COAL MINE		
Conceptual Year 21 Mine Plan		
Cad File: 06048G.dwg	Date: 21.06.2010	Drawn: CP
		Figure 6-3

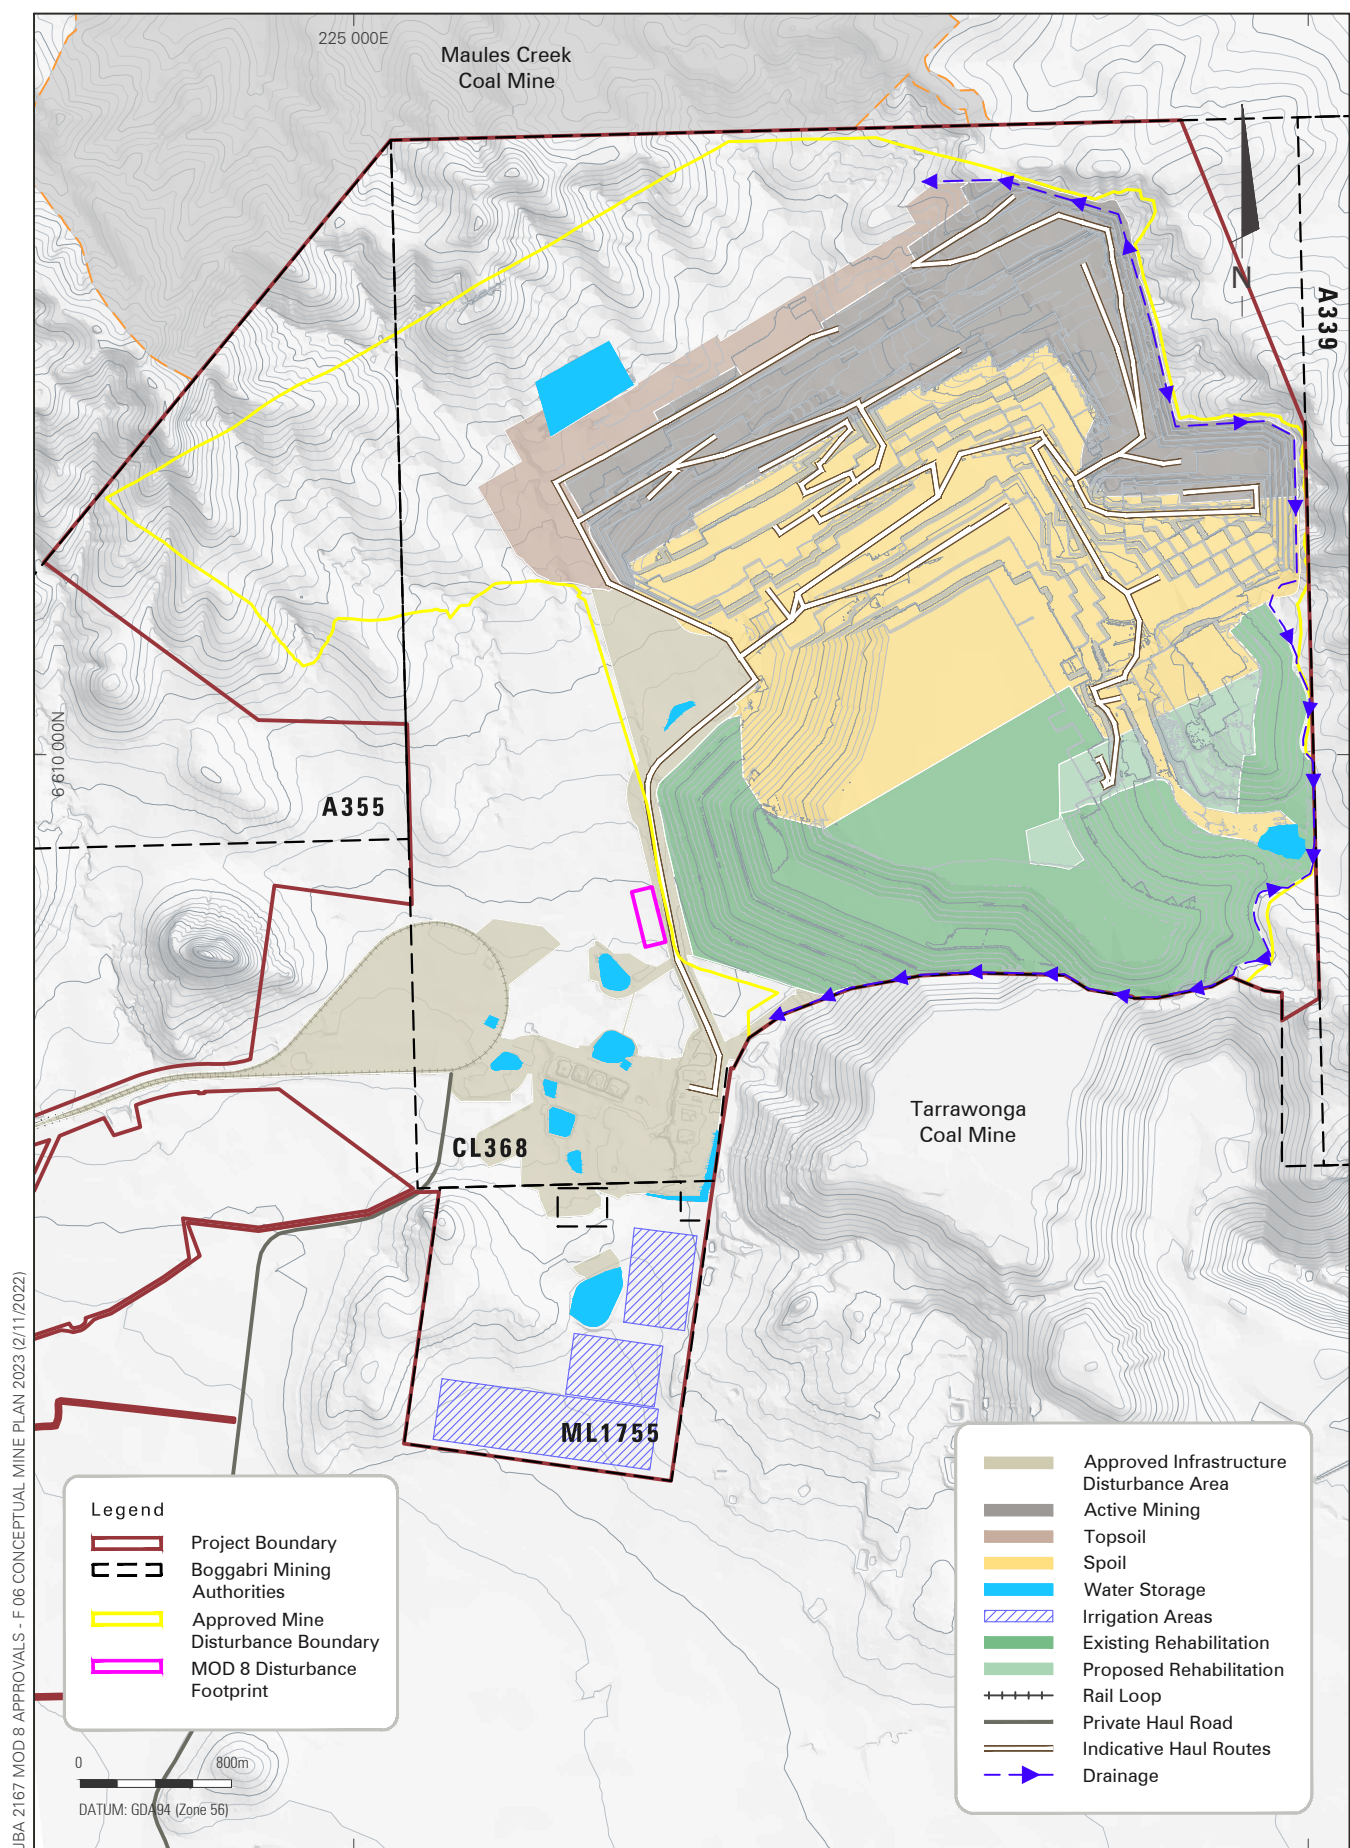


BOGGABRI COAL MINE

Conceptual Mine Plan 2023

FIGURE 6-4

JBA 2167 MOD 8 APPROVALS - F 07 CONCEPTUAL MINE PLAN 2027 (14/09/2022)

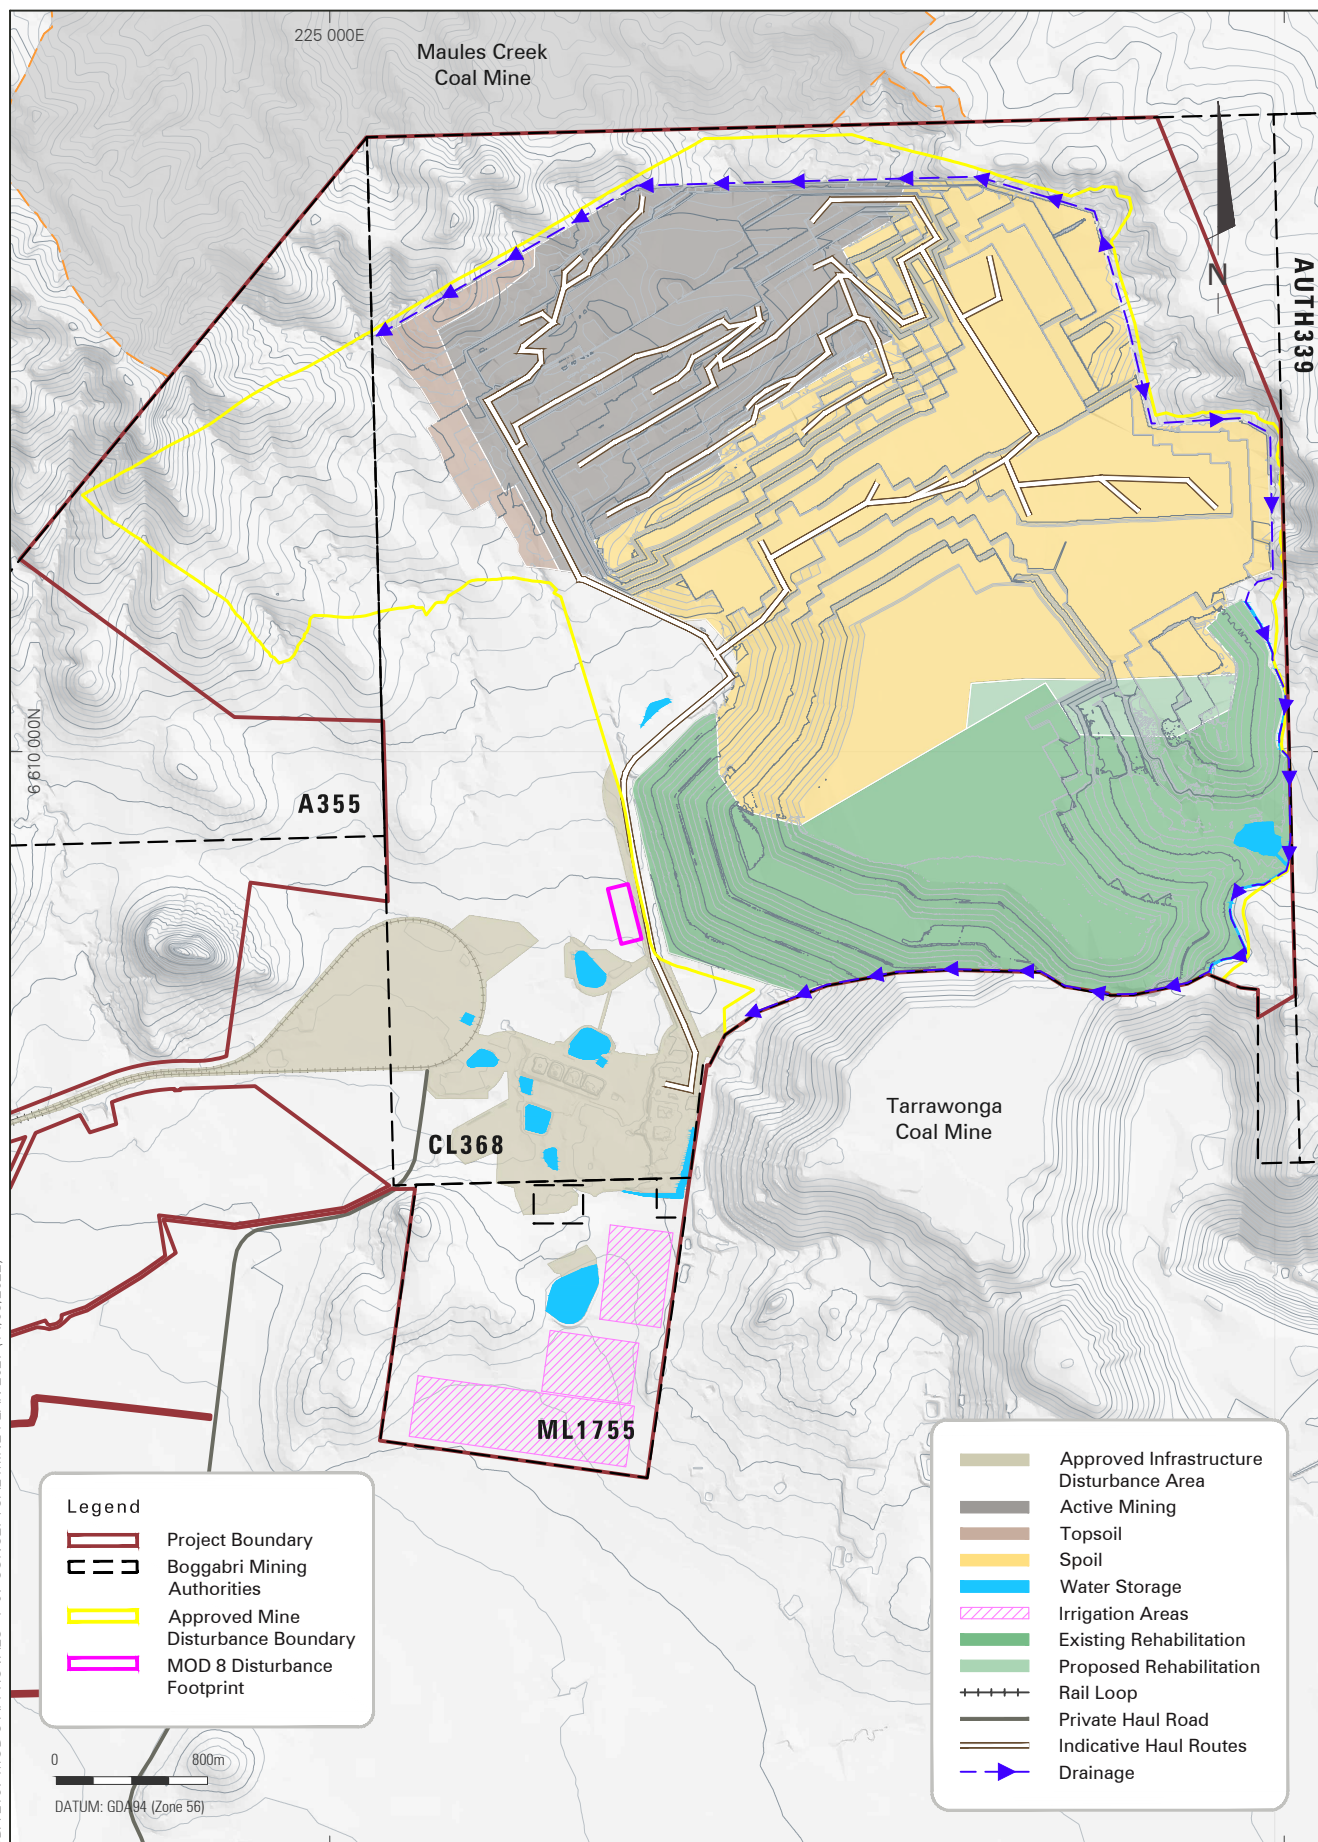

BOGGABRI COAL MINE

Conceptual Mine Plan 2027

FIGURE 6-5



6.2 Phases of Rehabilitation and General Methodologies

The method of mining will continue as an open cut truck and shovel operation. Vegetation clearing and topsoil stripping is undertaken ahead of mining. Cleared vegetation and topsoil is either directly placed onto areas ready for rehabilitation on OEAs or stockpiled for later use in the rehabilitation process. This is followed by drilling and blasting of the underlying overburden and ROM coal. ROM coal is loaded onto haul trucks and hauled to a ROM pad to the south-west of the mining area or an in-pit ROM stockpile.

Overburden is loaded into haul trucks using hydraulic excavators and hauled to the OEAs which are being developed to progressively backfill the mining void. Emplacement of overburden will be undertaken until the OEA reaches the planned landform heights, consistent with the approved Conceptual Final Landform design. Once overburden emplacement reaches the desired landform heights, the overburden materials will be bulk shaped in preparation for rehabilitation.

A bund will be temporarily maintained at the crest of the existing rehabilitated OEAs to manage sediment laden runoff from active sections of the OEA. Once an area has been bulk shaped, required water management structures will be installed and the surface prepared for the growth medium to be applied. Where required, rock lined drop structures on existing rehabilitation will be extended to convey runoff from the newly rehabilitated area. These drop structures will be tied into 5 m wide contours shaped with a 1% horizontal grade at 20 m intervals. Surface preparation will involve contour ripping, topsoil and subsoil spreading (where appropriate), application of ameliorants (as required) and scarification prior to or during seeding. Following surface preparation, the area will be seeded with a cover crop and direct seeded or planted out with tube stock species required to achieve the post mining land uses (Native Ecosystem), as detailed in **Section 6.2.5**.

Management strategies that will be implemented during each stage of the mining and rehabilitation process are outlined in **Section 6.2**.

Rehabilitation activities at BCM have historically been assessed and reported annually as part of the Annual Review required under MP 09_0182 and former conditions of the existing mining leases. It is intended that the Annual Rehabilitation Report(s) required under the new conditions for each mining lease in accordance with Schedule 8A of the *Mining Regulation 2016* will continue to be reported as part of the Annual Review. BCOPL has previously made the relevant applications to align the reporting period and associated reporting due date for the Annual Rehabilitation Report(s) to align with those for the Annual Review under MP 09_0182.

The various rehabilitation phases undertaken at BCM are described in **Table 6-1**. Phases of rehabilitation or rehabilitation phases relates to the stages of actions required to rehabilitate disturbed areas to the desired final land use. These rehabilitation phases have been developed to align with those described within the *Guideline: Rehabilitation Management Plans for Large Mines* (Resources Regulator 2021).

Table 6-1: Rehabilitation Phases

Objective	Measurement
Active Mining	The process of undertaking mining and associated activities including controls implemented to manage risks and enhance rehabilitation outcomes.
Decommissioning	The process of removing plant and equipment from active services and rendering the area safe including removal and/or remediation of contaminants and hazardous materials.
Landform Establishment	The process of shaping unformed rock or other sub-stratum material the approved final landform. This includes earthworks activities such as cut and fill, rock raking, water storage and drainage construction.
Growth Medium Development	The process of establishing and enhancing the physical structure, chemical properties and biological properties of a soil stratum suitable for plant growth. This includes contour ripping, placing and spreading soil and application of ameliorants.

Objective	Measurement
Ecosystem and Land Use Establishment	The process of seeding, planting and transplanting plant species to establish the desired vegetation communities.
Ecosystem and Land Use Development	The process of applying management techniques to encourage an ecosystem to grow and develop towards a desired and sustainable post mining land use outcome and ensure they meet the Rehabilitation Objectives and Completion Criteria.
Rehabilitation Completion	When rehabilitation areas can be demonstrated that they achieve their Rehabilitation Objectives and Completion Criteria, an application will be submitted to the NSW Resources Regulator for final sign off.

The Rehabilitation Risk Assessment undertaken by BCOPL as described in **Section 3** identified a number of controls to manage the risks of rehabilitation activities achieving the rehabilitation objectives for the site. The following sub-sections present a summary of the key management measures and controls implemented at BCM to address key rehabilitation risks.

6.2.1 Active Mining Phase

The Rehabilitation Risk Assessment addressed the Active Mining Phase of rehabilitation under the heading of Rehabilitation Materials and Biological Resources. During this phase, various rehabilitation materials and biological resources are required to be recovered to assist in rehabilitating the mined landform and to achieve the post-mining land uses at BCM. The findings from the Rehabilitation Risk Assessment have been addressed within the following sections as relevant.

a. Soil and Materials

BCOPL will be mining through vegetation communities, which are part of the Leard State Forest. Translocation of the topsoil and vegetative material containing an appropriate seed bank, plant nutrients and organic carbon sources will be used to rehabilitate areas to assist in the recreation of understorey species consistent with the target post-mining vegetation communities. Suitable subsoil materials are also recovered to assist in establishing a suitable growth medium for the intended post-mining vegetation communities. The appropriate management of these soil resources is a fundamental component of rehabilitation success which needs to be managed throughout the active mining phase.

The management of soil resources is described in detail in the SMP. BCOPL is currently completing a review of the SMP to incorporate further details for the ongoing management of the growth media that is stored in long term stockpiles to ensure its longer term viability. The SMP will also need to be updated to incorporate an established set of criteria to monitor growth media suitability for rehabilitation proposing to establish the desired final land use. This detail will be included in future revisions to this RMP.

The soil sampling and analysis methods contained in the SMP sets out the testing, witness and hold points requirements for each step of the soil management process.

The SMP incorporates an estimate of salvageable soils within the approved Mine Disturbance Boundary as well as the materials required for the effective rehabilitation of the final landform. These estimates are reviewed and updated annually. Alternative growth mediums are also reviewed in the event that these estimates indicate that available resources are insufficient.

Relevant information from the soil management measures implemented as part of the SMP are fed into the LOM and 3YP planning systems. This ensures that adequate information is provided in the mine planning processes to identify required resources, suitable stockpile locations and to plan for the use of any salvaged materials as part of the progressive rehabilitation activities.

The LOM and 3YP planning systems identify the required rehabilitation materials and stockpile locations for inclusion into the ENV-RHB-STR-001-ATT-003 Forward Works Program documentation.

Characteristics of Emplacement and Cover Material

Some site soils and mine spoils are generally poor, have low organic carbon, are sodic and are dispersive. Soil testing will be undertaken to determine amelioration requirements and rates. Characterisation of topsoil, subsoil and spoil for erosion (primarily dispersion) and agronomic (pH, electrical conductivity (EC), Cation Exchange Capacity (CEC), Organic Carbon (OC), metals) parameters will be undertaken prior to stripping (topsoil and subsoil) and prior to resspreading (spoil). Sampling will determine if the topsoil, subsoil and spoil is suitable for reuse as a growth media or if it requires amelioration or selective handling and placement. Unsuitable subsoil and spoil parameters are shown below in Table 6-2.

Table 6-2: Unsuitable Subsoil and Spoil Parameters

Parameter	Unsuitable range
pH	<5.0 or >8.5
Exchangeable sodium percentage	>6% if clay content >10%
EC (1:5 suspension)	>1.0 dS/m

Following characterisation, the suitable and unsuitable materials will generally be able to be identified visually. If not able to be ameliorated, unsuitable spoil and subsoil will be capped with a minimum of 1.0 m of suitable spoil (compacted depth) or, more appropriately, capped to a depth greater than the minimum rooting depth of the vegetation. Capping spoil will need to be ameliorated and contour ripped prior to the placement of the ameliorated subsoil and topsoil.

Ameliorants will be mixed in with the subsoil and topsoil material (when required) as part of the stripping operation, irrespective if the soil material is to be placed in storage or directly applied to a rehabilitation area. Soil materials to be placed in storage may also require further amelioration prior to being applied to rehabilitation areas. The application of ameliorates as part of the stripping process is more cost effective, and also gives the ameliorants additional time to react and modify the soil and to assist in the maintenance of soil conditions suitable for plant development. However, amelioration may be required following the placement of these materials onto the rehabilitation materials (particularly if it is required to be stored in stockpiles for a lengthy period of time).

Mine soil and spoils will typically be ameliorated with:

- Agricultural gypsum - to treat for dispersion, and improve the calcium to magnesium ratio, structure, water holding capacity;
- Compost - to increase organic carbon levels (mulch can be used but is less desirable), water holding capacity, soil biota;
- Fertiliser - to improve nutrients levels; and
- Wetting agents – for hydro-phobicity.

Where topsoil is unavailable or of insufficient quality, subsoils and/or mine spoil may be ameliorated to form a suitable growing media.

Topsoil/Subsoil Stripping and Handling

Soil sampling will be undertaken to:

- Identify the soil resource prior to stripping;
- Assist with the preparation of a soil balance or inventory to assist with rehabilitation planning; and
- Determine if the soil requires amelioration to ensure the soils' characteristics are within recommended ranges.

The process of soil stripping will also involve the continual evaluation of soil throughout the depths of the profile as areas and layers are exposed. Current topsoil reuse and stockpile management at BCM illustrates forest topsoil contains a large amount of stored seeds from the native vegetation communities. This is an

important reserve of indigenous plant seeds and soil micro flora, which will assist with the preservation of local genetic material and the reestablishment of a similar range and mix of species of the original vegetation in the rehabilitation area.

Management of soils and stripping depths during this process is dynamic and generally requires soil observations to be made on site on the day topsoil stripping is occurring. This enhances decision making and operational modifications can be adopted to best utilise the available soil resources available.

The depth of topsoil and subsoil stripping is important for a number of reasons. Most native seeds are concentrated in the first few centimetres of the topsoil (there is no O horizon with these soils). Over-stripping can result in the stored seeds being buried too deep, which will reduce germination. Accordingly, it is important to monitor topsoil stripping closely to ensure the various layers of the topsoil are stripped separately.

Topsoil stripped from each vegetation community will be used in areas identified for rehabilitation for the corresponding vegetation community. Where topsoil cannot be used for rehabilitation immediately it will be stockpiled. Topsoil from each vegetation community and / or quality will be separately stockpiles and recorded within the soil register.

The following techniques will be used to prevent excessive soil deterioration:

- Soil will not be stripped during excessively wet or dry conditions;
- Where practical, stripped material will be placed directly onto reshaped overburden and spread immediately (if mining sequences, equipment scheduling and weather conditions permit) to avoid the requirement for stockpiling;
- As part of the planning process, sufficient area for stockpiling, placement or burial of topsoil will have been identified prior to stripping and these areas will be accessible;
- As part of the planning process, temporary drainage, erosion and sediment control measures will be employed to minimise erosion and pollution of waters if required;
- Grading or pushing soil into windrows with graders or dozers will be undertaken for later collection by front-end loaders/hydraulic excavators and dump trucks;
- Vegetation not salvaged for habitat relocation to rehabilitation areas will be stockpiled, chipped and then managed aerobically to form compost that is to be incorporated into the soil. The salvaging of commercial products (logs, fence posts and fire wood) will only occur if not to the detriment of the soil improved by the process involving wood chip incorporation;
- The vegetation remaining following salvaging of commercial products (logs, fence posts and fire wood) will be collected and stored for placement onto the rehabilitation areas following seeding, or tub ground and managed aerobically to form compost to be incorporated into the soil;
- A record will be kept of the nature and quantities of salvaged bush rocks, timber etc. to ensure the salvage of these items is maximised;
- Where possible, stockpiled material will be located in areas away from drainage lines and drainage will be diverted around stockpiles to prevent erosion;
- Sediment controls will be installed downstream from stockpiles to prevent contamination of clean water;
- More erodible materials will be placed on flatter areas to minimise the potential for erosion;
- The surface of soil stockpiles shall be contour scarified in order to promote infiltration and minimise erosion until vegetation is established;
- The duration of topsoil stockpiling will be minimised, as periods longer than three months may cause structural degradation and death of seeds and micro-organisms;
- Stockpiles will be seeded with cover crops to protect the stockpile from raindrop splash erosion, aerate the soil to reduce anaerobic conditions, enhance organic carbon levels and suppress weeds; and

- Soil material stockpile locations, volumes and date of soil stripping will be recorded within a Soil Stripping and Placement Plan, as required by the SMP.

Suitably trained and experienced operators will be used during the stripping process to ensure that the above measures are implemented.

b. Flora

Impacts to flora and fauna will be managed in accordance with the BMP. The BMP provides practical instruction for managing and controlling risks to biodiversity associated with the Project and directs the implementation of the Biodiversity Offset Strategy.

Management measures and procedures contained in the BMP provide a framework for managing biodiversity values within the Project Boundary, BOAs and wider locality, throughout and beyond the operation of the Project. Preparation of the BMP has been undertaken with reference to best practice environmental management standards in accordance with the MP 09_0182 and other statutory requirements.

Pre-clearing vegetation surveys will be undertaken to establish the following factors:

- Species, including weeds, occurrence;
- Condition and type of vegetation community;
- Topsoil and subsoil type; and
- Amelioration rates.

The surveys will aim to identify and manage threat-listed flora within the clearing footprint and reduce the impacts of clearing on native fauna through relocation. Pre-clearing surveys will be undertaken in accordance with the Clearing and Fauna Management Procedure (CFMP). These surveys will be undertaken by a suitably qualified ecologist.

Resource recovery inspections will be undertaken during clearing to ensure available seed, topsoil and mulch is salvaged for use in the rehabilitation of disturbed areas, in accordance with the CFMP (BMP Appendix B) and the SMP. The Pre-clearing surveys will also identify weed occurrences which require control prior to stripping taking place.

c. Fauna

Resource recovery inspections will be undertaken during clearing to ensure available habitat features (logs, bushrock, tree hollows, etc.) are salvaged for use in the rehabilitation of disturbed areas, in accordance with the CFMP (BMP Appendix B) and the SMP.

The salvaged materials will be placed directly onto rehabilitation areas or stored in designated storage locations identified as part of the mine planning process. These materials will be documented within the Soil Stripping and Placement Plan as required by the SMP.

Rock materials which are salvaged during day to day mining activities are planned on the short term basis at a site level. The rehabilitation risk assessment identified that further work is required for the management of these rock materials for long term planning works. Future revisions to this RMP will outline the additional processes adopted to ensure that long term mine planning considers the management of these materials as part of the mining process.

The progress and effects of salvaging and reusing habitat resources will be monitored and reported annually in the Annual Review.

d. Rock/Overburden Emplacement

The OEAs are designed to optimise post-mining land capability, long-term stability and minimise the costs in achieving an optimal land use.

The mine disturbance areas, in particular the OEAs and low walls, represent the largest area of rehabilitation landform at the BCM. A batter slope design has been modelled for the OEAs and a final landform design will be modelled to confirm long-term stability of the final landform to be constructed. Outcomes of the initial batter slope design modelling are summarised below.

Water Erosion Prediction Project (WEPP) modelling of the current batter slope design (i.e. 10° batter gradient and 20 m high lift) indicates that with adequately ameliorated soil and diversion banks, (which will be removed once target vegetation levels are achieved), it is possible to provide an erosional stable landform with acceptable rates of erosion (i.e. <10 tonnes per hectare per year (t/ha/y)).

The final landform design requires further investigation for the low wall and the OEA slopes (yet to be established) to develop a safe, stable and non-erosive final landform based on the final land use, climate, topography and soils, which incorporates:

- Batter slopes;
- OEA height and footprint;
- Drainage;
- Landform evolution; and
- Construction method.

Throughout the mining process, suitable rock and other substrates which may be suitable for use in water management structures for the final landform rehabilitation are identified, salvaged and stored for later use. Rock testing is undertaken to ensure these materials are suitable for use in water management structures. Mine planning processes consider sourcing suitable materials for use in mine rehabilitation activities throughout the mining process.

e. Waste Management

As presented in the Boggabri EA (Hansen Bailey, 2010), potentially contaminated sites within the Project Boundary include pre-existing sheep dips, workshops/machinery sheds used for fuel, chemical and fertiliser storage and landfills. No contaminated lands have been identified within the Project Boundary that will be disturbed for mining or mining related purposes.

Soil contaminated by hydrocarbons as a result of spills will be contained and transported to an in-pit bioremediation area for treatment and subsequent in-pit disposal.

Furthermore, each activity with the potential for a hydrocarbon spill will be identified through a risk management process. Management controls will be developed as required and will include:

- Locating spill kits in high-risk areas around mine infrastructure and construction areas within the Project Boundary;
- Ensuring all BCM personnel are trained in incident and emergency response procedures. Specific training will also be provided to those personnel required to handle hazardous materials;
- All workshop and vehicle wash down water shall be directed to a sump/separator for containment and subsequent treatment or appropriate disposal;
- Vehicles, plant and equipment leaking fuel, oil coolant or any other hydrocarbons will not be operated where practicable and repaired at the earliest opportunity;
- All hazardous materials facilities on site will be designed, constructed and operated in accordance with all relevant legislation, standards and guidelines, with particular reference to AS 1940:2004 – The Storage and Handling of Flammable and Combustible Liquids; and
- Refuelling operations will be undertaken within areas specifically designated for that purpose, where practicable.

Following the decommissioning and removal of infrastructure in areas with potentially contaminated soils, a contamination assessment is undertaken to identify potentially problematic materials which requires

remediation. This will ensure that contaminated materials are appropriately treated prior to final rehabilitation activities commence.

f. Geology and Geochemistry

The Boggabri EA (Hansen Bailey, 2010) included an assessment of waste rock geology and geochemistry. The outcomes of that assessment, with regard to its potential to pose a risk to rehabilitation success, are summarised as follows:

- The concentration of total metals in overburden solids is well below applied guideline criteria for soils and is unlikely to present any environmental issues associated with revegetation and rehabilitation;
- Most overburden materials will generate slightly alkaline and relatively low-salinity run-off and seepage following surface exposure. The major ion chemistry of initial surface runoff and seepage from overburden materials is likely to be dominated by sodium, bicarbonate, chloride and sulphate;
- The concentration of dissolved metals in initial runoff and seepage from overburden materials is unlikely to present any significant environmental issues associated with surface and groundwater quality; and
- Most overburden materials are sodic and likely to have structural stability problems related to potential dispersion. Some near surface and conglomerate overburden materials are likely to be less sodic and may be the most suitable materials for revegetation and rehabilitation activities (as a growth medium). For all other sodic overburden materials, it is likely that treatment would be required if these were to be considered for use as vegetation growth medium.

In light of these assessment outcomes, the following management strategies will be implemented:

- Placement of overburden at the emplacement area will be undertaken in a manner that limits the risk of exposure of highly sodic material and subsequent runoff and erosion;
- Surface water will be monitored for pH, EC, total suspended solids and dissolved metals to ensure that concentrations remain within the criteria listed in the Surface Water Management Plan; and
- Out-of-pit dumping will only occur to a maximum RL of 395 m.

Should surface water monitoring indicate that seepage from overburden is outside the appropriate criteria, a review of overburden emplacement practices will be undertaken.

The geochemical assessment undertaken for the Boggabri EA also identified the potentially acid forming (PAF) qualities of some overburden and potential coal reject materials at BCM to be selectively managed, which is further discussed in Section h.

g. Material Prone to Spontaneous Combustion

Spontaneous combustion is controlled by avoiding disposing of combustible material in waste emplacement areas and emplacing combustible materials in locations where oxygen ingress is minimised (i.e. deep in-pit burial, away from rehabilitation areas).

There will be four main components to the management on spontaneous combustion at BCM:

- Prevention;
- Detection;
- Control; and
- Incident management.

BCOPL and its contractors currently employ these principles to minimise the occurrence of spontaneous combustion and have had significant success in reducing the area affected by spontaneous combustion. However, there are practical impediments to applications of these principles. Areas that are currently being mined cannot be capped and, in some cases, it is not practical to cap areas which will need to be reworked in the near or medium future.

BCOPL and relevant contractors will monitor and manage spontaneous combustion throughout the life of the Project. Measures that will continue to be implemented include:

- Managing spontaneous combustion in accordance with the mining operator's Spontaneous Combustion Management Plan;
- Capping all areas of spontaneous combustion with inert material;
- Emplacing any identified combustible materials deep within in-pit emplacement areas; and
- Monitoring of coal stockpiles for signs of spontaneous combustion and responding through action as required.

There have been minimal spontaneous combustion issues over the life of the mine to date. The Boggabri EA (Hansen Bailey, 2010) reported that spontaneous combustion presents a low risk of causing environmental impacts at the BCM. It is therefore considered a low risk to rehabilitation at BCM. Whilst the risk of spontaneous combustion is considered low it is still required to be managed.

In this regard, materials with potential to result in spontaneous combustion (i.e. carbonaceous materials) are emplaced well away from the final landform surface in accordance with the MIN-PRO-009 Rejects Management and Operations.

h. Material prone to generating acid mine drainage

The Boggabri EA (Hansen Bailey, 2010) included an assessment of the potential for mining and overburden activities to cause acid mine drainage. The outcomes of that assessment, with regard to its potential to pose a risk to rehabilitation success, are summarised as follows:

- Most overburden is likely to have negligible (<0.1%) total sulphur content and is therefore classified as non-acid forming (NAF). Overburden also has excess acid buffering capacity typical of a moderate Acid Neutralising Capacity value, which will compensate for any acid that could potentially be generated from the small amount of overburden materials with uncertain acid generating classification.
- Most potential coal reject materials are likely to have negligible (<0.1%) total sulphur content and are therefore classified as NAF-barren. These materials have a high factor of safety with respect to potential acid generation.
- A small proportion of the potential coal reject materials located within siltstone near the roof of the Braymont Seam have a relatively high total sulphur content and negligible buffering capacity and are classified as PAF – High Capacity. However, geochemical analysis undertaken during 2016 indicates that the vast majority of reject from the Braymont seam is NAF. As most overburden materials are likely to be NAF and have a high factor of safety with respect to potential acid generation, the overburden can be regarded as a NAF unit.

An additional geochemistry assessments were completed in 2021 & 2025 by RGS Environmental. The assessment found that the majority of the interburden and potential coal reject materials contain negligible sulfur, have excess Acid Neutralising Capacity and are classified as NAF.

Based on these outcomes, the risk of acid mine drainage at BCM is considered low. BCOPL will continue to manage PAF material through the following processes:

- Confirming the geochemical and physical characteristics of coal reject materials as bulk samples become available from the CHPP; and
- Undertaking in-pit burial of identified PAF coal reject materials including materials from the Braymont and Jeralong seams.

Undertake water quality monitoring in-line with Mod 8 requirements to go deeper and assess in accordance with the approved Water Management Plans - EPBC 2021/8875.

BCOPL has in place a Reject Management Plan, MIN-PRO-009 Rejects Management And Operations which ensures that these materials are appropriately identified, selectively handled and disposed deep within the mining area.

i. Ore beneficiation waste management (reject and tailings disposal)

The following paragraphs provide a summary of the potential geochemical risks to rehabilitation from coarse and fine rejects emplacement and an overview of the management strategies that will be implemented to manage the identified risks. The summary is based on the geochemistry assessment completed in the EA (Hansen Bailey, 2010) and the results of a PAF testing program completed at the BCM during 2016. The concentration of total metals in potential coal reject solids is well below applied guideline criteria for soils and is unlikely to present any environmental issues associated with revegetation and rehabilitation.

Most potential coal reject materials will generate slightly alkaline and relatively low-salinity run-off and seepage following surface exposure. The exception is potential coal reject material from the Braymont seam where PAF materials may generate acidic and more saline run-off and seepage. However, geochemical analysis undertaken during 2016 indicates that the vast majority of reject from the Braymont seam is NAF.

The major ion chemistry of initial surface runoff seepage from potential coal reject materials is likely to be dominated by sodium bicarbonate, chloride and sulfate. The initial concentration of soluble sulfate in runoff and seepage is expected to remain within the water quality guideline criterion that was applied during the EA, although further exposure to oxidising conditions could lead to increased soluble sulphate concentrations. The concentration of dissolved metals in initial runoff and seepage from potential coal reject materials is unlikely to present any significant environmental issues associated with surface and groundwater quality.

Most potential coal reject materials are sodic and likely to have structural stability problems related to potential dispersion. These materials are unlikely to be suitable for use as a vegetation growth medium.

The coarse reject and tailings disposal strategy provides adequate disposal options and capacity for all coal waste produced throughout the life of the Project whilst contributing to the mine rehabilitation outcomes.

The ongoing management of potential coal rejects material will consider the geochemistry of materials with respect to their potential for environmental impacts and suitability for use in rehabilitation. BCOPL will implement the following management strategies:

- Placement of reject materials in-pit and/or co-disposal with overburden in accordance with MIN-PRO-009 Rejects Management and Operations and MIN-PRO-008 Dumping Operations;
- In pit burial of PAF potential coal reject materials will be in accordance with the Reject Management and Operations Procedure and the management measure outlined above;
- For the co-disposal option, placement of NAF potential coal reject material in a manner that limits the risk of surface exposure of highly sodic materials and subsequent runoff and erosion (i.e. inward side of OEA and at least 5 m below final RL);
- Continued confirmation of the geochemical and physical characteristics of coal rejects material when bulk samples become available from the CHPP for at least 12 months after mining below the merriown seam and when mining turns north. Current characterisation has shown rejects continue to be low risk and the management procedure effective in This will ensure that characterisation of the rejects continues to be low risk; and
- Water sampling in accordance with the federal approval EPBC 2021/8875 to ensure potentially acid forming materials are managed.

Whilst the above measures are implemented during day to day mining activities and are planned on the short term basis at a site level, the rehabilitation risk assessment identified that further work is required for the management of reject materials within long term planning works. Future revisions to this RMP will outline the additional processes adopted to ensure that long term mine planning considers the management of these materials as part of the mining process.

j. Erosion and Sediment Control

The Soil and Land Resource Assessment (GSS Environmental, 2010) completed for the EA (Hansen Bailey, 2010) included laboratory analysis of soils at the BCM. All samples were tested for dispersion using the Emerson Aggregate Test and sodicity using the Exchangeable Sodium Percentage (ESP). These tests

provided an indication of the susceptibility of the soils at BCM to lose their structure and binding capacity when wet and therefore their erosion potential. The results showed a similar pattern across the site, with the upper soil layers generally identified as being non-dispersive and non-sodic whilst the subsoils tended to exhibit moderate to high dispersion potential and high sodicity with depth. The risk of erosion was considered low for upper layers of the soil profile and high for subsoils. As such, minimising surface exposure of subsoils and overburden material will continue to form a key strategy for reducing the risk of erosion within rehabilitation areas.

Other potential risks to rehabilitation from erosion and sedimentation are summarised as follows:

- Slope slumping and/or failure due to poor landform establishment and incorrect surface preparation;
- Rill and gully erosion due to poor drainage design or slope instability; and
- Loss of topsoil on stockpiles and rehabilitation areas from wind and water erosion due to poor groundcover.

The erosion and sediment control measures listed in Section 6.2.4 will be implemented, as a minimum, for all rehabilitation works. The implementation of these mitigation measures renders erosion and sedimentation a low risk to rehabilitation. Some of the measures listed are recommended by the Blue Book – Managing Urban Stormwater; Mines and Quarries (DECC, 2008) and others are recommendations from the soils study undertaken for the EA (GSS Environmental, 2010).

Erosion and sedimentation impacts are managed in accordance with the SWMP. All construction and mining contractors will be required to establish and implement a monitoring and inspection programme to ensure appropriate installation and operational control of erosion and sediment controls.

k. Ongoing Management of Biological Resources for Use in Rehabilitation

Concurrent with vegetation clearing, habitat logs and other suitable habitat materials will be collected and stockpiled for placement in the rehabilitation areas in accordance with the Clearing and Fauna Management Procedure. Quantitative surveys of habitat resources within the clearing footprint will allow a comparison between the extent of existing and salvaged habitat features.

The following data will be recorded on the Clearing Extent and Site Feature Checklist as described in the BMP and includes:

- Hollow-bearing trees;
- Abundance of hollows, categorised by size;
- Bush rocks (m²); and
- Fallen timber (m) – at least 5 cm Diameter at Breast Height (DBH) and 1 m long.

Materials salvaged during construction, such as hollow bearing trees or stags will be used as part of the rehabilitation in a manner which does not place fauna in danger of injury (i.e. hollow bearing trees/stags should not be placed next to the haulage route). The progress and effects of salvaging and reusing habitat resources will be monitored as part of the Project's biodiversity and rehabilitation monitoring program and reported annually in the Annual Review.

Whilst the above measures are implemented during day to day mining activities and are planned on the short term basis at a site level, the rehabilitation risk assessment identified that further work is required for the management of biological resources within longer term planning works. Future revisions to this RMP will outline the additional processes adopted to ensure that long term mine planning considers the management of these materials as part of the mining process.

Native seed collection will be undertaken as required to provide seed from the local area for direct seeding and propagation of seedlings for planting. Seed collection will be undertaken throughout the mine lease and local areas consistent with the BMP. Seed viability testing will be undertaken annually prior to rehabilitation planting and seeding.

Seed collection and storage will be undertaken by suitably qualified and experienced personnel to ensure the viability of the seed for reuse in mine rehabilitation activities. Ecologists will undertake seed collection

opportunisticly throughout the year, for example, during tree clearing programs and after flowering events. Offsite local and regional seed will be collected using suitably qualified and experienced consultants and contractors. BCOPPL will consider inspections during suitable seasons (i.e. when seed is available on canopy and ground layer species) for seed collection events.

The BMP guides the RMP and the seed mix attributes which are based on a mixture and abundance of the target species requirement. Any changes to the seed mix will occur in consultation with ecologists and in accordance with the BMP. Objective 10, of the BMP states that seed will be collected from a range of sites across the locality to capture local variations within both the BOAs and Project Boundary in accordance with relevant guidelines.

Where climatic conditions or seasonal variation prevents seeding at the time of soil placement, a cover crop will then be used to stabilise the soils until the appropriate design species can be introduced to the area. Establishing vegetation cover as soon as practicable following disturbance is critical to minimise the potential for erosion and weeds.

This will involve the application of a temporary sterile cover crop (or native grasses) using species that are not likely to impede revegetation of the desired ecosystem and provide options for remediating erosion including adjusting seed and planning densities to maximise ground cover.

An indicative revegetation schedule is provided in Appendix E of the BMP.

As described previously in Section a, the appropriate management of topsoil resources is a fundamental component of rehabilitation success. The management of topsoil resources is described in detail in the SMP. The soil sampling and analysis methods contained in the SMP sets out the testing, witness and hold points requirements for each step of the soil management process.

Direct return should always be encouraged rather than stockpiling because it better preserves soil structure and seed viability. Current topsoil reuse and stockpile management at BCOPPL demonstrates that forest topsoil contains a large quantity of seeds stored in the topsoil. This is an important reserve of indigenous plant seed and soil microflora, which will assist with the preservation of local genetic material and the re-establishment of a range of species similar to the original vegetation in the rehabilitation area. Where stockpiling is unavoidable, the following process is to be followed:

- Stockpile heights should ideally be less than 0.6 m, but are not to exceed 3 m. This is to limit the degree of composting processes that may occur and so preserve soil quality and the seedbank of native vegetation.
- Stockpiles that are to remain undisturbed for more than two months will be seeded. This will provide a faster stabilisation of the soil surface, improve infiltration, increase nitrogen and organic matter content, and encourage micro-organisms and the establishment of native plants from the soil seed bank.
- The surface of soil stockpiles will be shaped in a manner to promote infiltration and minimise erosion until vegetation is established. Examples include undulating dump mounds or ripping of the surface.
- If levelled after placement, the top of the stockpile will be ripped and seeded.
- Large depressions should be avoided to prevent water ponding for extended periods.
- Stockpiles will be in areas away from drainage lines. Run-on will be diverted around the stockpiles to prevent erosion and waterlogging. Sediment controls will be installed downslope from the stockpiles where there is a risk of contaminating clean water.
- Records will be maintained of the stockpile locations, the date of establishment, area, volume and source of materials.

Prior to use in rehabilitation, an assessment will be undertaken of weed infestation and what remedial actions such as soil amelioration might be appropriate to ensure it is appropriate to establish the intended post-mining land use.

Topsoil/subsoil materials that are stripped ahead of mining operations and are subsequently stockpiled to contain a natural seedbank and microbial activity which is highly beneficial to rehabilitation activities. Stockpiling of the soil materials for long periods of time has the potential for seedbank and microbial activity to deteriorate if not appropriately managed. Soil stockpiling is managed in accordance with Section 4.5 of the SMP. This is where the balance between ideal direct placement of soils, and long-term stockpiling (>2 months) due to operations constraints, is considered.

Section 4.6 of the SMP describes whether further work is required on the growth media prior to salvaging from the stockpiles for reuse on mine rehabilitation areas to ensure soils are suitable. BCOPL is undertaking trials for continuous improvement to rehabilitation practices given the nature of the soils available and the soil deficit. Findings will be incorporated into this RMP or SMP, and sub documents such as the QAPs as required.

l. Mine Subsidence

BCM is not within a mine subsidence district and no underground mining activities are proposed. As such, mine subsidence management is not considered relevant to this RMP.

m. Management of Potential Cultural and Heritage Issues

Aboriginal and historic heritage is managed in accordance with the approved CHMP. In addition to the CHMP, a regional Aboriginal Heritage Conservation Strategy has been prepared in consultation with Aboriginal stakeholders and neighbouring mines in the BTM Complex. Copies of the CHMP and ACHS are available on the Boggabri Coal website.

Through the CHMP, BCOPL will implement a variety of management strategies to address impacts to the archaeological and cultural values at the BCM. BCOPL will utilise a project archaeologist to work with Registered Aboriginal Parties in undertaking field work prior to and during construction and operational phases in accordance with the management plan.

n. Exploration Activities

Drilling boreholes located within active mining areas pose a low risk to rehabilitation. Boreholes drilled outside of the active mining area will be rehabilitated in accordance with the Exploration Code of Practice: Rehabilitation (DRG, July 2015).

A description of the process for the disposal of drilling muds within the approved mining areas is included in Section e.

Drilling Outside Approved Mine Disturbance Boundary

As part of the 2020 to 2024 Exploration Program, BCOPL is proposing to undertake large diameter exploration boreholes within CL 368. However, approximately 13 boreholes are proposed outside BCM's approved mine disturbance boundary. BCOPL has consulted with the DPHI and DCCEEW regarding the appropriate approval pathway for these activities under the EP&A Act and EPBC Act as appropriate.

Each borehole site will involve a drill pad (with a disturbance area of approximately 40 metres by 40 metres in size) which includes set down, work areas, soil stockpile areas and in ground sumps (where physically possible). Excavation works may be required at some sites in order to develop a safe drilling location.

Topsoil (generally between 0 to 300 mm depth) will be stripped prior to excavation. Stripped topsoil will be stockpiled separately to subsoil which will be subsequently used in rehabilitation activities. All exploration bore holes will be rehabilitated in accordance with the Borehole Sealing Guideline (DTI – Resources and Energy 2012) and the Exploration Code of Practice: Rehabilitation (DRG, July 2015). The 13 proposed exploration borehole sites (indicated by a red arrow pointing towards each site) along with the existing and proposed new access tracks are shown on Figure 6-6. These exploration boreholes have largely been established to date. Further exploration drilling that is undertaken beyond the approved Mine Disturbance Boundary in the future will obtain the necessary Assessable Prospecting Operations approvals from the Resources Regulator under the Mining Act 1992.

In accordance with advice received from DPHI and DCCEE, an environmental assessment was undertaken and included within the approved 2020 to 2024 Mining Operations Plan Amendment A, from which provided the relevant approval under Part 5 of the EP&A Act. The environmental assessment included specialist impact assessment studies for:

- Biodiversity impacts;
- Aboriginal heritage impacts; and
- Groundwater impacts.

Impacts related to soils, surface water, traffic, air quality, noise and vibration, non-Aboriginal heritage, visual amenity, socio-economic, resource use, land use, waste and bushfires were not expected to significantly change as a result of the proposed drilling outside of the approved mining disturbance boundary and will be managed in accordance with the existing mitigation measures in the relevant environmental management plans.

Mitigation measures for the management of impacts from drilling activities outside the disturbance boundary include:

- Existing access tracks will be used wherever possible. Where sites require the construction of new access tracks, excavation and woodland vegetation removal will be avoided where practicable. Where excavation is required, a track of approximately 5 m wide will be cleared;
- All boreholes will be rehabilitated in accordance with the Exploration Code of Practice: Rehabilitation (NSW Resources Regulator, July 2015);
- If previously unidentified non-Aboriginal heritage items are encountered during the proposed drilling, these would be managed in accordance with the approved CHMP;
- Erosion and sediment controls will be established at each drilling site prior to excavation to manage the potential for impacts to the neighbouring environment;
- Additional Biodiversity mitigation measures:
 - An ecologist will be present during the clearing of native vegetation to relocate any displaced fauna to nearby habitat;
 - Limit disturbance of vegetation to the minimum necessary to construct works;
 - Mark the limits of clearing and install fencing around the proposed impact area prior to construction activities commencing to avoid unnecessary vegetation and habitat removal;
 - Hollow bearing trees will be preserved/avoided where possible;
 - Implement clearing protocols, including:
 - Marking trees to be removed and preparing an inventory of trees and hollows to be removed;
 - Checking hollow-bearing trees for the presence of bird nests and arboreal mammals, such as possum, gliders and bats, prior to felling;
 - Animals found to be occupying trees will be safely removed before the clearing of trees if possible and relocated into nearby woodlands;
 - Where practicable, displaced woody debris and bush rock will be relocated into adjacent bushland;
 - Restrict equipment storage and stockpiling of resources to designated areas in cleared land;
 - Implement where appropriate erosion and sediment controls in accordance with:
 - Erosion and sediment control on unsealed roads (OEH 2012).
 - Managing Urban Stormwater – Soils and Construction, Vol 1 (Landcom 2004).
 - Managing Urban Stormwater – Soils and Construction, Vol 2 (DECC 2008);

- Vehicles and other construction equipment (i.e. excavators, dozers, etcetera) are to be received free of soil, seeds and plant material before entering the proposed works area to prevent the spread of potential pathogens into the construction site;
- Implement where appropriate in general accordance with:
 - Arrive Clean, Leave Clean Guidelines (Department of Environment, 2015);
 - Hygiene Protocol for the control of disease in frogs (National Parks and Wildlife Service, 2008);
- Weed management actions will be developed to manage weeds during the proposed works;
- Notify wildlife service if injured fauna is identified during construction;
- Additional Groundwater mitigation measures:
 - All exploration boreholes will be rehabilitated in accordance with the borehole sealing guidelines to prevent impacts to groundwater, such as cross-contamination between the coal seams.

6.2.2 Decommissioning

a. Site Security

The site security measures which are currently in place will continue to be maintained following the cessation of mining operations. No unrestricted public access is currently permitted to the BCM. Security fencing, safety bunds and warning signage is used to restrict access to the active mine site by member of the public. Final rehabilitation activities may require some adjustment to these security measures, although these adjustments will ensure public access remains restricted as per current practice.

Existing fencing that is to be retained continue to be structurally assessed and repaired or replaced where necessary.

b. Infrastructure to be Removed or Demolished

Infrastructure will be removed during mine closure, unless otherwise approved by the Resources Regulator. This will include:

- Any buildings including the workshop, offices, stores etc.;
- CHPP;
- Product coal stockpiling and conveyor infrastructure;
- Rail and loading infrastructure;
- Utilities, services and fuel infrastructure (including pipelines – underground and surface, powerlines, fuel tanks and hazardous material storage tanks);
- Any remote infrastructure (e.g. monitoring equipment);
- Concrete foundations and footings; and
- Hardstand and bitumen sealed areas, haul roads and access tracks.

No decommissioning or demolition works is proposed to be undertaken during the next three years as detailed within the ENV-RHB-STR-001-ATT-003 Forward Works Program.

c. Buildings, Structures and Fixed Plant to be Retained

Infrastructure will be removed during mine closure, unless otherwise approved by the Resources Regulator. Two dams currently utilised to manage mine water at BCM are proposed to be retained post-mining. These dams will be retained to manage water runoff from the rehabilitated final landform.

A 6 km section of Leard Forest Road was closed during 2014. Only the southern and northern sections of the road will remain open for public use. These sections will also be closed on a temporary basis when blasting and other mining-related activities are being undertaken in close proximity. These closures will vary depending on the mining schedule. The former private haul road previously used to transport product coal from the BCM to the Boggabri Coal Terminal for loading to trains has been repurposed as the main access road for the BCM. The road provides heavy vehicle access, general access to the mine, ongoing access to the former Boggabri Coal Terminal, and for property and infrastructure maintenance purposes.

The former Boggabri Coal Terminal will be retained and subject to a remediation program that allows for its ongoing care and maintenance. BCOPL is currently entertaining proposals from other industries interested in utilising the former Boggabri Coal Terminal infrastructure. The side dumping b-double trucks that were used to haul product coal from the Mine Infrastructure Area to the former Boggabri Coal Terminal prior to commissioning of the TLO and rail spur in 2015 will be retained on site for possible emergency coal haulage in the event of unforeseen operational issues with the Boggabri rail spur.

d. Management of Carbonaceous / Contaminated Material

The decommissioning of the CHPP and associated coal handling areas will entail the removal of hardstands and access roads which are likely to contain carbonaceous materials. These materials will be removed and disposed within the final void with at least 5 m of inert overburden materials in accordance with current practices during mining operations.

During decommissioning and mine closure Phase 1 and Phase 2 Assessments in accordance with requirements of the Contaminated Land Management Act 1997 and POEO Act will be undertaken and

Remedial Action Plans, to outline remediation works for any contaminated areas, will be developed and implemented, as required.

e. Hazardous Materials Management

The primary risks to rehabilitation associated with infrastructure removal is contamination. A number of areas of potential hydrocarbon contamination exist at the BCM. These areas are associated with maintenance workshops, designated storage areas and refuelling and filling points for:

- Diesel, bio-diesel; and
- Hydraulic/ lubricating oils and waste oils.

BCOPL operates in-pit bioremediation areas for the treatment of contaminated material produced at the workshop, the wash pad pit and other areas of the mine.

During decommissioning and mine closure Phase 1 and Phase 2 Assessments in accordance with requirements of the Contaminated Land Management Act 1997 and POEO Act will be undertaken and Remedial Action Plans, to outline remediation works for any hydrocarbon impacted areas, will be developed and implemented, as required.

Additional procedures and controls will be developed as BCM nears the cessation of mining.

f. Underground Infrastructure

The BCM is an open cut mine and therefore no underground mining infrastructure is onsite. As such, underground infrastructure is not relevant to this RMP.

6.2.3 Landform Establishment

The Final Landform associated with the open cut mining area at BCM will generally comprise three landform elements, the elevated OEAs constructed to RL395 m, the infilled mining areas and the partially infilled final void. Various water management structures will be required to manage water runoff from the landform.

a. Water Management Infrastructure

Re-grading of overburden dumps has and will continue to be undertaken to produce slope angles, lengths and shapes that are compatible with land capability classifications suitable for the proposed land use and have a low potential to erode. The design profile and associated landform establishment methods are broadly consistent with rehabilitation techniques employed on parts of the existing rehabilitated OEAs. Integrated with this will be a drainage pattern which is capable of conveying runoff from the newly created catchments and diverting these flows into the Nagero Creek catchment by sheeting water towards natural drainage lines of associated ephemeral creeks.

Temporary erosion and sediment control measures will be required whilst the rehabilitation areas are establishing (e.g. contour banks, contour ripping, graded banks, erosion blankets, ground-cover vegetation, rip-rap). Whilst groundcover is being established on these rehabilitated landforms, drainage flows will be captured within sediment basins/dams to treat sediment loads within the water prior to it being released into the Nagero Creek catchment. Sediment basins/dams will be decommissioned once the groundcover of the surrounding rehabilitated area reaches 80% coverage. After the desired ground coverage is reached the sediment dams will be decommissioned and land rehabilitated to enable surface water to be directed towards the Nagero Creek catchment.

Infiltration characteristics for rehabilitated areas are expected to be similar to pre-mining conditions. The quality of runoff from rehabilitated areas is expected to be similar to pre-mining conditions. Based on the conclusions of the geochemical impact assessment completed within the Boggabri EA (2010), it is considered unlikely that leachate generated from overburden and coal reject materials would significantly impact surface water quality downstream of the site if these materials are managed in accordance with the mitigation measures described within Section f.

A Final Void and Mine Closure Plan will be prepared by the end of 2025 in accordance with Schedule 3, Condition 72 of MP 09_0182. This plan will include a detailed assessment of the hydrochemistry, hydrogeology and hydrology components of the final void and landform design. This detailed assessment will be independently reviewed by suitably qualified, experienced and independent personnel approved by the Secretary.

All soil conservation and erosion control drainage structures (graded banks, chutes and flumes) will be designed in accordance with the NSW Soil Conservation Service, Design Manual for Soil Conservation Works – Technical Handbook No. 5 (Aveyard, 1982). All sediment and/or pollution control facilities will be designed in accordance with Volume 1 and Volume 2E of Managing Urban Stormwater: Soils and Construction (Landcom, 2004; DECC, 2008 respectively).

b. Final Landform Construction: General Requirements

The final landform will be developed in a manner that is generally consistent with the Conceptual Final Landform design illustrated within Appendix 9 of MP 09_0182. The final landform design requires further investigation for the low wall and overburden emplacement slopes to develop a safe, stable and non-erosive final landform based on the final land use, climate, topography and soils, which incorporates:

- Batter slopes;
- Overburden emplacement height and footprint;
- Drainage;
- Landform evolution; and
- Construction method.

The following risks associated with the management of rehabilitation slopes have been identified:

- Erosion and sedimentation.
- Surface water pollution.
- Vegetation management.
- Stable drainage system/landform.

Initial laboratory analysis has been undertaken to provide a basic material characterisation to enable further examination of erodibility parameters for three common materials including topsoil, topsoil/mulch and overburden. The WEPP model has been used to assess interactions between slope height and gradient for all three materials supplied. The key findings relating to the initial landform assessment include:

- The overburden is more saline than the topsoil materials assessed, although these levels are unlikely to adversely affect plant growth;
- The overburden material is classified as sodic (ESP > 6%), but the topsoil samples are not;
- The topsoil materials, although not sodic, may be prone to dispersion as indicated in the Conceptual Landform Study (Landloch, 2012) and in materials having an Electrochemical Stability Index < 0.05. Gypsum will be incorporated into topsoil to reduce the potential for dispersion and surface crusting at rates described in the SMP; and
- Vegetation is a crucial component of slope stability. Provided that the target levels of vegetation contact cover can be established promptly, the current landforms being constructed have potential to be stable and sustainable which is confirmed by the rehabilitation works undertaken to date.

Rehabilitated landforms will be free draining and integrate with surrounding catchments. Slope design typically incorporates a lineal batter gradient of 10° (17.5%) and lifts to a height of 20 m. Slopes are initially constructed with diversion banks (berms) that are subsequently removed once target vegetation ground cover is achieved. Batter slopes will be sheeted with a topsoil mulch mix to a minimum depth of 150 mm. Topsoil and other growth mediums will be subject to amelioration as necessary in accordance with the SMP.

BCOPL has been working with the operators of the neighbouring mine (Tarrawonga Mine) since 2014 to identify opportunities and conduct integrated mine planning with adjoining mines to minimise environmental impacts of final landforms. BCOPL has and will continue to implement its requirements under the Common Boundary Integrated Management Plan (CBIMP), which details the planning and integration of the final rehabilitated landform of the Tarrawonga northern emplacement and southern extent of the BCM OEA.

Additional erosion and geotechnical assessment of the highwall will be undertaken to determine a design that provides a geotechnically stable highwall. Assessments will be undertaken and included in the Final Void and Mine Closure Plan, which will be prepared by the end of December 2025.

c. Final Landform Construction: Reject Emplacement Areas and Tailings Dams

There are no reject emplacement areas or tailings dams located at BCM. Operation of the CHPP will produce approximately 10 Mt of coal reject over the life of the mine. Rejects will continue to be co-disposed with overburden within the OEA and mining areas. Methodologies for disposal are summarised in Section 6.2.1.

d. Final Landform Construction: Final Voids Highwalls and Low Walls

As per the Conceptual Final Landform design provided within Appendix 9 of MP 09_0182, the final void will be located within the northern section of the BCM. BCOPL has committed to partially infilling the final void area with overburden to RL 285 m, which was defined within the Boggabri EA (2010) as a level greater than the pre-mining groundwater levels within this area. BCOPL will also reshape the high wall of the final void to ensure it is safe, stable, non-erosive and revegetated as is practical. The long-term stability of a high wall can be affected by a number of factors including:

- Structure and strength of the high wall and end walls;
- Resistance of the in situ sedimentary rock to rainfall-induced weathering processes;
- High wall and end wall drainage;
- Ponding of water in final void can cause rapid breakdown of sediments in contact with water and progressive back-cutting of the inundated strata leading to major wall failure; and
- Extended saturation-softening of the base of the low-wall also has the potential to cause major failure.

A final high wall landform will be developed following an assessment by geotechnical and erosion specialists to determine appropriate geotechnical and erosion parameters. This will be incorporated into the Final Void and Mine Closure Plan and completion criteria prior to the end of December 2025.

e. Construction of Creek / River Diversion Works

The Conceptual Final Landform proposes a drainage network that travels east to west through the previously mined and backfilled overburden material at the completion of mining operations. The drainage network will enable surface water collected in the clean water catchment to the east to be diverted through mine rehabilitation areas and enter the natural drainage catchment of Nagero Creek to the west. Nagero Creek, a tributary of the Namoi River, is an ephemeral stream that flows westward to the Namoi River.

The Conceptual Final Landform drainage network will be designed and implemented in such a way to enable the constructed landforms to drain to the natural environment and whilst maintaining a safe, stable and non-erosive environment.

BCM is conducting ongoing investigations in relation to the final landform design and the associated drainage network. Details of these investigations will be provided within future revisions of this RMP. The drainage network constructed for the Final Landform will be monitored periodically and assessed against the rehabilitation objectives and completion criteria to ensure that these drainage lines safely convey surface runoff at non-erosive velocities whilst also ensuring sustainable vegetation and long term landform sustainability is achieved.

Integration with Tarrawonga Coal Mine

The SSD Approval for the Tarrawonga Coal Mine (PA 11_0047) (located immediately adjacent to the south west of BCM's mine lease area CL 368) approves a greater degree of integration with the BCM Conceptual Final Landform, namely:

Continued development of mining operations in the Maules Creek Formation, including to the north into the southern parts of BCM (now within ML 1685 and ML 1749) which adjoin Tarrawonga's ML 1579;
Use of upgraded BCM Mine Infrastructure Area facilities for the handling and processing of up to 3 Mtpa ROM coal from Tarrawonga, and the loading of product coal to trains for transport on the BCM private rail spur to the port of Newcastle. Note: no commercial agreement was reached and these activities are no longer proposed; and
Expanded emplacement of waste rock in the Northern Emplacement as mining develops, ultimately integrating with the southern extent of the BCM emplacement.

Common Boundary Integrated Management Plan

Integration of the Tarrawonga Northern Emplacement and the southern extent of the BCM waste rock emplacement presents an opportunity to enhance connectivity between the post mining landforms of both mines. Detailed planning to optimise integration of the final rehabilitated landform has been undertaken and documented in the CBIMP.

The CBIMP was prepared in consultation with Resources Regulator and was formally endorsed/signed-off by BCPL (now BCOPL) and Tarrawonga Coal Pty Limited (TCPL) in August 2015. It includes a definition of working areas and responsibilities, details of scheduling of emplacement area development, progressive rehabilitation activities, a nominal point of emplacement area integration and the conceptual integrated final landform. It also includes details on the integrated water management strategies for both the development and rehabilitation phases of the emplacement area integration and responsibilities for water management (including on-going maintenance). The CBIMP also outlines a process for the management of topsoil resources for placement on the final shaped emplacement area and identifies criteria and methodologies, to establish native woodland/forest communities that integrate across the mine lease boundary and with Leard State Forest.

Overburden Emplacement Integration – Timing

Relevant lease transfers for the southern portion of BCOPLs CL 368 to enable Tarrawonga to undertake open cut pit and overburden emplacement area development in their northern extension area was completed in 2017. As at the end of 2020, BCOPL completed the rehabilitation of the relevant sections of its landform design to integrate with the proposed landform at Tarrawonga. Tarrawonga is currently progressing mining operations along the common boundary. In accordance with the CBIMP, Tarrawonga will develop its final landform and associated drainage infrastructure to integrate with the landform which has previously been completed by BCM. BCOPL regularly meet with Tarrawonga to discuss the required actions by both parties under the CBIMP.

Overburden Emplacement Integration – Rehabilitation

The lease boundary defines the area of prime responsibility between BCOPL and TCPL. The CBIMP defines the rehabilitation goals for that area. The rehabilitation standard currently in place within the Leard State Forest area, as demonstrated by BCOPL, has been adopted for the lease transfer area to ensure the landform and rehabilitation of both operations is consistently applied and an integrated landform is achieved. Further information regarding rehabilitation of the overburden integration area is provided in the CBIMP. In accordance with Condition 7 of Schedule 2 of MP 09_082, BCOPL will maintain a 250 m wide barrier between the lease boundary for the BCM and the Maules Creek Coal Project to retain the vegetated buffer between the two mines. No mining related disturbance is permitted within this area.

6.2.4 Growth Medium Development

Soil

Topsoil and subsoil materials will be reused to rehabilitate areas with corresponding final landuse domain vegetation communities. The topsoil is particularly important in this regard to utilise the stored seed in the topsoil.

Topsoil will be spread to a minimum depth of 150 mm on all regraded spoil. When required (based on soil sampling results) contour ripping of the topsoil will be undertaken to incorporate gypsum into the mine spoil and to encourage infiltration of water.

The respread topsoil surface will be scarified prior to, or during seeding. Where possible, ripping will be undertaken when the soil is moist and immediately prior to sowing. Contour scarification will incorporate soil ameliorants into the plant rooting zone (to a depth of 100 mm). Scarification will also increase rainfall infiltration, reduce run-off and provide a micro-habitat allowing plants to germinate and establish.

Topsoil placement inspections will ensure topsoil is applied to the appropriate thickness and slope and in the predetermined location. These surveys will be undertaken by the BCOPL Environment Superintendent (or delegate).

As described in Section 6.2.1, some site soils and mine spoils are generally poor, have low organic carbon, are sodic and can be dispersive. Soil testing will be undertaken to determine amelioration requirements and rates in accordance with the SMP. Characterisation of topsoil, subsoil and spoil for erosion (primarily dispersion) and agronomic (pH, EC, CEC, OC, metals) parameters will be undertaken prior to stripping (topsoil and subsoil) and prior to resspreading (spoil). Sampling will determine if the topsoil, subsoil and spoil is suitable for reuse or if it requires amelioration or selective handling and placement.

Some site soils and mine spoils require amelioration to:

- Reduce dispersion and improve drainage;
- Increase organic matter content;
- Increase or reduce pH; and
- Improve nutrient status.

Amelioration of site soils and spoil is described in the SMP.

Where required, the application of gypsum to the spoil prior to the final trim will be undertaken so that it can be well incorporated with earthworks. Contour ripping of spoil is undertaken to the target depth of 0.6 m with final trim earthworks to incorporate ameliorations and reduce compaction.

Amelioration of the overburden and topsoil will be undertaken in accordance with the SMP with the aim of increasing infiltration rates, and resistance to erosion to support vegetation communities and minimise surface runoff.

Section 2 of the SMP describes soil within the primary disturbance area and details previous soil surveys pre-disturbance. This guides the project on the soil landscapes and the associated vegetation. This is the criteria that soil monitoring monitored and managed and describes amelioration processes where the soils require additional management.

BCOPL is developing criteria for which the quality of growth media to be utilised on rehabilitation areas will be monitored and managed. This detail will be reflected within the SMP and will be detailed within future revisions to this RMP.

Erosion and Sediment Control

Drainage and sediment control structures will be designed in accordance with Table 6.1 of DECC (2008). Where practicable, sediment basins and other water storage devices will not be located on overburden dumps to reduce the potential for tunnel erosion.

Erosion control will focus on treating dispersive soils and spoils, providing soil surface cover and minimising concentrated flow conditions. Erosion control works will include:

- Amelioration of dispersive spoil to minimise the risk of rill, gully and tunnel erosion and to allow the infiltration of surface water (reduce the amount and velocity of surface water);
- Contour scarification of compacted surfaces to encourage infiltration and surface roughness;
- Utilisation of cover crops including salt tolerant grasses and legumes to minimise raindrop and sheet erosion of reshaped areas;
- Engineered channel banks, slope drains and energy dissipaters in concentrated flow situations to reduce erosion. Drainage and sediment control structures will be designed in accordance with Table 6.1 of the Blue Book Volume 2E. Sediment Basins and other water storage devices will not be located on overburden dumps to reduce the potential for tunnel erosion;
- In the larger drainage systems such as clean water drains and modified natural drainage systems, redirective erosion control methods such as cross vanes, rock vanes and J-hook vanes will be used to provide channel bed and bank protection;
- Post disturbance regrading will be undertaken to produce slopes, angles and lengths and shapes that are compatible with the proposed land use and not prone to an unacceptable rate of erosion;

- Contoured furrows or contour banks will be constructed at intervals down the slope – to divide a long slope into a series of short slopes preventing runoff from reaching a depth or velocity that would cause erosion;
- Intercepted runoff will be diverted via engineering waterways using erosion blankets, ground-cover vegetation and/or rip rap to safely dispose of runoff down slope;
- Stockpiles will be trimmed, deep ripped to 500-800 millimetres, immediately sown with native species;
- Stormwater runoff will be diverted around any active or rehabilitated mining areas;
- Contours will be placed every 5 m down slope for erosion control and moisture retention. Cultivation will be undertaken with a tined implement to blend topsoil into the overburden or waste rock in preparation for sowing – this will leave the soil surface in a roughened condition creating a ‘key’ between the soil and the spoil; and
- Preventing vehicles to enter topsoiled rehabilitation areas to prevent damage to vegetation and soil structure.
- The management of erosion and sediment control for all mining and associated disturbance is described in detail in the Surface Water Management Plan (SWMP) and CFMP (Appendix B of the BMP).

Additional stabilisation works may be undertaken as required and include reshaping, the installation of grade stabilisation structures, and amelioration of dispersive soil, revegetation, fencing and de-silting. Stabilisation works are inspected annually as part of the annual rehabilitation inspection and where required works will be monitored as part of the formal rehabilitation monitoring program.

Weed and Pest Control

A Weed and Pest Management Strategy (Appendix C of the BMP) and a CFMP have been developed for activities and processes that pose a significant risk to biodiversity within the Project Boundary and for the management of BOAs.

All priority weeds within the Project Boundary will be controlled in accordance with the requirements of the Biosecurity Act 2015. The implementation of the monitoring, inspection and reporting program detailed within the BMP will reduce the potential for weed introduction and spread and allow continual monitoring and control. Pest animals will also be identified and controlled as part of the program. This program ensures both a proactive and reactive approach to weed and pest animal management.

Compliance with the BMP in accordance with the MP 09_0182, licences, permits and other legislative controls is maintained by a schedule of inspections, monitoring and reporting. The monitoring, inspection and reporting program for the project and management of BOAs is set out in the BMP. Monitoring results are also reported in the Annual Review.

Habitat Value

Rehabilitation of the BCM will require the provision of significant fauna habitat resources to encourage fauna use and functioning of the natural ecosystem representative of the analogue site. Concurrent with vegetation clearing, habitat logs will be collected and stockpiled for placement in rehabilitation areas in accordance with the CFMP (Appendix B of the BMP). Quantitative surveys of habitat resources within the clearing footprint will allow a comparison between the extent of existing and salvaged habitat features.

The following data will be recorded on the Clearing Extent and Site Feature Checklist as described in the BMP:

- Hollow-bearing trees;
- Abundance of hollows categorised by size;
- Bush rocks (m²); and
- Fallen timber (m) – at least 5 cm DBH and 1 m long.

Materials salvaged during construction, such as hollow bearing trees or stags will be used as part of the rehabilitation in a manner which does not place fauna in danger of injury (i.e. hollow bearing trees/stags

should not be placed next to the haulage route). The progress and effects of salvaging and reusing habitat resources will be monitored as part of the Project's biodiversity and rehabilitation monitoring program and reported annually in the Annual Review.

6.2.5 Ecosystem and Land Use Establishment

Revegetation

The key to successful rehabilitation of native species is the management of the topsoil seed resource. Where practicable topsoil will aim to be reused to rehabilitate areas with corresponding vegetation communities. Where direct placement is possible or the age of the stockpile is such that it contains limited viable seed resources, direct seeding will be undertaken where required to supplement the in-situ seed resources. Revegetation works are aimed to be carried out in spring and autumn where practicable, and if needed will also be undertaken throughout the year to establish the vegetation communities.

BCOPL has demonstrated native vegetation can establish from the seed resources contained within the topsoil. This is demonstrated by the high level of diversity observed in rehabilitation (including trials) to date (refer to Section 9).

Given the nature and scale of proposed future rehabilitation activities, it will be necessary to consider direct seeding techniques. Direct seeding trials will be undertaken to determine the optimum method for vegetation establishment. A combination of all three techniques is likely to be used.

In terms of native vegetation establishment, revegetation works will involve direct native seeding and/or supplementary tube stock planting. Revegetation works are best carried out in spring and autumn when conditions are optimal. In the first instance groundcover vegetation should be established to prevent raindrop and sheet erosion from occurring. Natural seed germination from the soil seed bank will be assisted with direct seeding and where applicable seed will be treated to enhance germination rates. Planting of tube stock will supplement areas of low success rates from the natural regeneration through the seed bank and direct seeding.

Where necessary, BCOPL supplements natural regeneration with tube stock planting. Seedlings are supplied from a reputable nursery to provide a mature tree density of 150 to 300 trees per hectare. The seedlings are propagated from seed sourced from the targeted vegetation communities within the local area and on site.

Fertilising of tube stock will be undertaken at the time of planting by adding 100 g of DAP (di-ammonium phosphate) under the soil surface within 250 mm of the tube stock.

Watering the revegetated areas may be required to assist plant germination in situ and to assist the supplementary stock planted. Watering (if required) will be undertaken in response to the prevailing weather conditions and monitoring of the plants.

Where it is not practicable to complete native revegetation works, interim rehabilitation works such as temporary seeding with cover crops or the application of soil polymers may be undertaken to minimise soil erosion and degradation, and dust generation.

Cover crops with drought tolerance will be implemented to ensure biomass production is maintained during prolonged dry periods. The cover crops will hay off creating an increased dispersion of organic matter and humid conditions for native seeds to promoting vegetation cover. This will involve the application of a temporary sterile cover crop (or native grasses) using species that are not likely to impede revegetation of the desired ecosystem and provide options for remediating erosion including adjusting seed and planting densities to maximise ground cover (see Section k for further information on seed collection and mix). Where climatic conditions or seasonal variation prevent seeding at the time of soil placement, a cover crop will then be used to stabilise the soils until the appropriate design species can be introduced to the area. Establishing vegetation cover as soon as practicable following disturbance is critical to minimise the potential for erosion and weeds.

BCOPL considers timing of revegetation activities for optimal seasonal conditions (e.g. to avoid drought, frost, and summer heat). An indicative revegetation schedule is provided in Appendix E of the Biodiversity Management Plan and the Phase 5 QAP considers this as a checkpoint during the rehabilitation process.

Vegetation Species

The seed mixes for each of broad vegetation community types (grassy woodland, shrubby woodland/open forest, and riparian forest) including the Threatened Box-Gum woodland community will need to contain species which are representative of these communities, details of which are provided in the BMP. The revegetation works will aim to establish three broad native vegetation classes community types (grassy woodland, shrubby woodland/open forest, and riparian forest). In addition to the existing native vegetation types the species and habitat characteristics of derived native grassland community are also provided for the purpose of native pasture revegetation.

See Section k for further information relating to seed collection and mix..

6.2.6 Ecosystem and Land Use Development

Rehabilitated areas will be actively managed based on the approved final landuse. A management and maintenance program will be implemented based on the outcomes of the rehabilitation monitoring program detailed in Section 8. Maintenance/contingency works in the rehabilitation areas will be completed as required to address any issues of concern or unpredicted impact identified during monitoring.

Maintenance/contingency activities may include a range of activities including:

- Excluding all activities/access from the rehabilitation areas, typically with OCE approval only;
- Supplementary seeding of vegetated areas;
- Weed and pest control;
- Application of soil ameliorants;
- Repair of any eroded areas;
- Water monitoring and management; and
- Land management activities.

Supplementary Seeding

Direct seeding is aimed to be undertaken to establish groundcover vegetation to minimise the potential for soil erosion. Natural seed germination from soil seed bank will also assist with the direct seeding to establish vegetation. In areas of low success rates, planting of tube stock may be used to assist in revegetating these areas.

Supplementary seed broadcasting may be undertaken in areas where native regeneration is considered insufficient following monitoring, seed for broadcasting will be treated where necessary prior to broadcasting to maximise germination rates. Supplementary seed broadcasting will focus on the desired vegetation density and diversity to be established in the rehabilitation areas.

Weeds and Pest Control

Weed and pest control management is described in the Weed and Pest Management Strategy, which is in Appendix C of the BMP.

Priority weeds within the Project Boundary will be controlled in accordance with the requirements of the Biosecurity Act 2015. The implementation of the monitoring, inspection and reporting program detailed within the BMP will reduce the potential for weed introduction and spread, and allow for monitoring and control. Pest animals will be identified and controlled as part of the monitoring, inspection and reporting program. BCOPL will aim to minimise the introduction and spread of weed species by complying with the CFMP (outlined within the BMP) during clearing activities, restricting access to areas of native vegetation.

Erosion Repair

Additional stabilisation works may be undertaken as required and include reshaping, the installation of grade stabilisation structures, and amelioration of dispersive soil, revegetation, fencing and de-silting. Stabilisation works are inspected annually as part of the general rehabilitation inspections and where required, these works will also be monitored as part of the formal rehabilitation monitoring program.

Environmental Monitoring and Management of Water

Water management at the BCM is guided by the Water Management Plan (WMP), which provides a framework for water management requirements listed under Section 75J of the EP&A Act (Schedule 3, Condition 38). The framework provided for under the WMP will be utilised throughout the completion of rehabilitation activities up to the completion of the relevant completion criteria.

The key objectives of the BCM surface water management system are to:

- Segregate clean runoff, dirty runoff and coal contact water generated from rainfall events and mining operations;

- Minimise the volume of coal contact water (surface runoff draining to pit and groundwater seepage that has been in contact with coal) generated by the BCM;
- Preferentially reuse coal contact water for dust suppression and coal washing;
- Provide sufficient on-site storage to avoid releases of coal contact water that could affect the quality of downstream watercourses; and
- Treat all dirty runoff from non-rehabilitated overburden areas to settle coarse suspended solids.

Existing and proposed water management dams and drains are shown on Figure 1-6.

Clean water catchments will be diverted around disturbed areas where this is reasonable and feasible to achieve. Dirty water runoff will be captured in sediment dams to encourage the settling of suspended solids. The key components and objectives of dirty water management at BCM include the following:

- Dirty water catchments are planned to ensure surface runoff from disturbed areas is collected in sediment dams to facilitate settlement of suspended solids within runoff water;
- Dirty water diversion drains designed for the peak 100 year ARI time of concentration storm event for the contributing catchment; and
- Dirty water sediment dams will be sized in accordance with the guidelines Managing Urban Stormwater – Soils and Construction – Volume 1 (Landcom, 2004) using a 90th percentile 5-day rainfall total of 38.4 mm and will be based on the 'Type F' design given the local soil conditions.

Coal contact water will be captured in sediment dams or mine water dams for storage and reuse and will not be released to the receiving environment. The water management system will aim to reuse as much coal contact water as possible onsite, which will be used as a priority for dust suppression and coal washing. Surplus coal contact water will be stored in-pit or mine water dams for later reuse within the mine water management system.

BCOPL conducts surface water monitoring at the BCM to ensure the water management system is being appropriately managed to minimise impacts to the neighbouring environment. The water monitoring program will identify when water runoff from rehabilitated areas is of a suitable quality to be released to the environment and assist in confirming that the dirty water management structures can be removed. Information gathered from the water monitoring program will also be used to refine closure criteria and modify BCM rehabilitation practices as required.

Land Management

Poorly managed livestock grazing can cause significant damage to patches of remnant vegetation and rehabilitation areas; however, if managed appropriately, grazing can be used as an effective tool to control weeds, manage bushfire risks, reduce biomass and positively manipulate species composition and vegetative structure. Following the establishment of any areas of Final Landuse Domain B, an investigation into sustainable livestock carrying capacities will be undertaken to assess the feasibility of introducing a strategic livestock regime.

Crash and seasonal grazing may be used to control weed species and encourage native species diversity. This is likely to be undertaken between late autumn and mid spring before weeds go to seed and while palatability and nutrient content is still high. Crash grazing would be restricted to small, temporarily fenced areas by allowing large numbers of livestock to graze for very short periods as described in the BMP. Grazing pressure associated with live-stock and native species will be monitored annually as part of Annual Review and biodiversity monitoring programs. These monitoring programs will also identify any additional land management activities such as weed management, fencing, and track repair.

Rehabilitation Completion

In NSW, mining companies must submit evidence demonstrating mine rehabilitation has been completed and the final land use identified in their development consent has been achieved.

The Resources Regulator assesses whether the evidence submitted is sufficient and demonstrates mine rehabilitation completion before a company's mining lease is ended and the security deposit is returned.

A guideline has been prepared to assist mining lease holders to demonstrate rehabilitation completion and achieve regulatory obligations under the Mining Act 1992 before mining lease relinquishment. Read the “Guideline: Achieving rehabilitation completion (sign-off)”.

6.3 Rehabilitation of Areas Affected by Subsidence

BCM is not within a mine subsidence district and no underground mining activities are proposed. As such, mine subsidence management is not considered relevant to this RMP.

7 REHABILITATION QUALITY ASSURANCE PROCESS

Implementation

Key management personnel and their relevant roles and responsibilities with regard to implementation of this RMP are detailed below in **Table 7-1**.

Table 7-1: Roles and Responsibilities for Implementation of the RMP

Role	Responsibility
BCOPL General Manager	Providing sufficient environment resources to ensure the effective implementation of environment management requirements, as outlined in this RMP.
BCOPL Technical Services Manager	- Ensuring mining and rehabilitation activities are undertaken in accordance with the commitments in this RMP. - Develop mine plans to allow for progressive rehabilitation of mined land.
BCOPL Mining Manager	Ensuring mining and rehabilitation activities are undertaken in accordance with the commitments in this RMP.
BCOPL Environment and Community Manager	- Liaising with regulatory authorities regarding BCOPL's mining and rehabilitation management obligations as detailed in this RMP. - Reviewing and updating all environment management documents referred to in this RMP. - Ensuring all employees and contractors are aware of their environment management obligations in accordance with this RMP. - Engaging specialists to undertake specific monitoring and environmental management activities in accordance with the commitments outlined in this RMP. - Communicating the mining and rehabilitation requirements outlined in this RMP to all affected parties at BCM.
BCOPL Environment Superintendent	- Undertaking environmental management activities to facilitate compliance with this RMP as directed and instructed by the BCOPL Health, Safety, Environment and Training Manager. - Implementing environment management obligations in accordance with the documents referred to in this RMP. - Developing and implementing specific procedures for the employees and subcontractors under their responsibility as required to facilitate compliance with the documents referred to in this RMP. - Ensuring all employees and subcontractors under their responsibility are aware of their environment management obligations. - Providing relevant environment data to assist BCOPL with environment reporting.
Mine Personnel	- Follow direction provided by the BCOPL Environment Superintendent / Site Supervisor. - Notify the Environment Superintendent / Site Supervisor in the event that uncontrolled rehabilitation risks are identified at the BCM.

Assurance Process

Detailed rehabilitation objectives and rehabilitation completion criteria have been developed for each mining and final landuse domain and are detailed in **Section 4**. Proposed Validation methods have been developed to demonstrate the completion criteria have been satisfied at each phase of rehabilitation and how this process will be formally documented and recorded. These processes are detailed in **Table 7-1**.

Further to this, it is important to note the Rehabilitation Objectives and proposed Completion Criteria (as described within **Section 4**) identify various indicators and validation methods to be used to demonstrate whether the Rehabilitation Completion Criteria at the end of rehabilitation activities has been achieved.

8 REHABILITATION MONITORING PROGRAM

The rehabilitation monitoring program will:

- Obtain data from reference sites to provide a range of values from replicated examples of similar vegetation communities;
- Compare rehabilitation areas to reference sites to best represent the final land use vegetation community and management conditions;
- Recognise the dynamic nature of ecosystems and be monitored simultaneously to the reference sites over time to account for changes in:
 - Seasonal variations; and
 - Climatic conditions;
- Management practices; and
- Unexpected disturbance events.

Monitoring of rehabilitation areas and analogue sites will be undertaken by specialist independent consultants on an annual basis using a modified Landscape Function Analysis and include factors such as:

- Cover abundance of each species;
- Overall cover abundance of each stratum;
- Condition of vegetation;
- Soil stability;
- Soil moisture;
- Colonisation of rehabilitated areas with fauna;
- Stems per hectare of commercial forestry crops;
- Vegetation – species and weed diversity;
- Birds – species diversity and numbers;
- Bats – species diversity and numbers;
- Invertebrates – species diversity (Berger-Parker index); and
- Other factors considered beneficial as a result of the research undertaken on the trial plots.

It is well documented that natural systems experience significant natural, spatial and temporal variability and, therefore, to be able to detect environment impact associated with anthropogenic disturbance, sampling designs must be capable of accounting for and explaining this variability.

8.1 Analogue Site Baseline Monitoring

Native Woodland PMLU

Monitoring of flora and fauna communities within and beyond the surrounding Leard State Forest (analogue sites beyond the CL 368 boundaries) is currently being conducted as part of the ongoing biodiversity monitoring program for the BCM. This monitoring program will continue and should be undertaken to provide comparative data for assessment of the success of the rehabilitation works. The analogue monitoring program will be updated to incorporate soil parameters to be measured. The findings of this work will drive the development of soil-based closure criteria. Soil monitoring at analogue sites will also be undertaken.

The data obtained from the analogue sites will provide a range of values from replicated examples of similar vegetation communities. Rehabilitation areas are compared to reference sites which best represent the final land use, vegetation community and management conditions to which they will be subjected.

These analogue sites will also provide detailed information on fauna assemblage (birds, bats and invertebrates), their habitats and utilisation within both the eastern and western portions of Leard State Forest. The analogue sites will allow rehabilitation monitoring to determine the successful establishment of fauna assemblages within the rehabilitation areas, their distribution across the rehabilitation areas and relative success of the proposed regional wildlife corridor identified within the BCOPL Biodiversity Offset Strategy (Parsons Brinckerhoff, 2010a).

A summary of the indicative species and structures of these four broad vegetation types is provided in Table 8.1 below.

Table 8-1 Vegetation Community Structures

Vegetation type	Grassy Woodland on Fertile Soils (Box Gum Woodland)	Riverine Woodland	Shrubby Woodland/Open Forest on Skeletal Soils	Derived Native Grassland for Pasture
Final Landuse Domain	Aa	Ab	Ac	B
Photo				
Canopy	To 20 m in height and 15-30% cover dominated by <i>E. albens</i> with a sub-canopy of <i>Callitris glaucophylla</i> .	To 25 m in height and 25-35% cover dominated by <i>E. blakelyi</i> and occasional <i>E. melliodora</i> .	To 20 m in height and 30-65% cover dominated by <i>E. crebra</i> , <i>E. dwyeri</i> , <i>E. albens</i> , <i>E. melanophloia</i> and <i>Notelaea macrocarpa</i> .	Isolated paddock trees (<5% cover) of <i>Eucalyptus populnea</i> subsp. <i>bimil</i> and <i>E. albens</i> .
Shrub layer	Generally sparse, however contains <i>Dodonaea</i> spp., <i>Cassinia</i> spp., and <i>Acacia</i> spp.	Moderately dense (20-30%) cover containing <i>Dodonaea</i> spp., and <i>Acacia deanei</i> .	Moderately dense (>30%) cover containing <i>Notelaea macrocarpa</i> , <i>Bursaria spinosa</i> , <i>Dodonaea</i> spp., <i>Cassinia</i> spp., and <i>Acacia</i> spp.	Generally sparse, however contains <i>Dodonaea</i> spp., <i>Cassinia</i> spp., and <i>Acacia</i> spp.
Ground layer	A diverse range of grasses forbs and sedges with >75% cover including; <i>Cyperus gracilis</i> , <i>Aristida ramosa</i> , <i>Cymbopogon refractus</i> and <i>Austrostipa scabra</i> .	A diverse range of grasses, forbs and sedges with 30-50% cover including; <i>Chloris truncata</i> , <i>Bothriochloa macra</i> , <i>Lomandra longifolia</i> and <i>Austrostipa verticillata</i> .	A diverse range of grasses forbs and sedges with 30-50% cover including; <i>Aristida ramosa</i> , <i>Austrodanthonia racemosa</i> , <i>Cheilanthes distans</i> and <i>Rostellularia adscendens</i> .	A diverse range of grasses, forbs and sedges with >75% cover including: <i>Enchylaena tomentosa</i> , <i>Einadia nutans</i> subsp. <i>linifolia</i> , <i>Aristida ramosa</i> , <i>Calotis cuneifolia</i> <i>Austrostipa scabra</i> subsp. <i>scabra</i> , <i>Austrostipa verticillata</i> , <i>Bothriochloa macra</i> , <i>Calotis cuneifolia</i> ,

Vegetation type	Grassy Woodland on Fertile Soils (Box Gum Woodland)	Riverine Woodland	Shrubby Woodland/Open Forest on Skeletal Soils	Derived Native Grassland for Pasture
Final Landuse Domain	Aa	Ab	Ac	B
				Vittadinia cervicularis var. cervicularis.
Leaf litter	Leaf litter varied across this habitat but was generally 1-2 cm deep with a percent coverage ranging from 30 to 70%.		Leaf litter varied across this habitat but was generally <1 cm deep with a percent coverage ranging from 20 to 40%.	Leaf litter varied across this habitat but contained areas of dense grass clumps with a percent coverage ranging from 30 to 70%.
Fallen timber	A moderate amount of fallen timber was present in this habitat, with sizes ranging from 50 to 300 mm.	A sparse to moderate amount of fallen timber was present in this habitat, with sizes ranging from 50 to 300 mm.	A moderate amount of fallen timber was present in this habitat, with sizes ranging from 50 to 300 mm.	Generally absent.
Tree hollows and stags	Numerous small (<5-10 cm diameter), medium sized (10-20 cm diameter) and large sized (20->30 cm diameter) tree hollows were recorded within this habitat A sparse number of hollow-bearing stags were recorded within this habitat.	Numerous small (<5-10 cm diameter), medium sized (10-20 cm diameter) and large sized (20->30 cm diameter) tree hollows were recorded within this habitat.	Numerous small (<5-10 cm diameter) and medium sized (10-20 cm diameter) tree hollows were recorded within this habitat. Large tree hollows (20->30 cm diameter) were sparse except for survey site S9, which recorded 9. A sparse number of hollow-bearing stags were recorded within this habitat.	Generally absent

Agricultural grazing PMLU

Currently, no grazing PMLU areas are available for rehabilitation. Therefore, no analogue sites are required. Suitable analogue monitoring assessment site will be established prior to the grazing areas being rehabilitated at BCM. These sites should represent low productivity pastures in the region. They will provide baseline criteria for soil, pasture composition and productivity values.

8.2 Rehabilitation Establishment Monitoring

In order to demonstrate rehabilitation success or succession toward rehabilitation success, specific indicators will be expected to equal or exceed values obtained from the reference site under the same set of conditions or demonstrate a positive trend towards target values. Criteria will also be set for stages of rehabilitation to show progression towards rehabilitation success. Proposed criteria can be found in

The rehabilitation monitoring program and reference sites has been expanded to include grassland areas. Final Landuse Domain B have a grazing post mining land use. Grazing rehabilitation assessments consider agricultural productivity parameters together with establishment of appropriate pasture species criteria.

The monitoring uses a combination of Landscape Function Analysis, soil analyses and various measurements of ecosystem diversity and habitat values (adapted from CSIRO Gibbons 2002) to assess key indicators of ecosystem function, including landscape organisation and soil surface condition as a measure of how well the landscape retains and uses vital resources.

Ecological rehabilitation monitoring will be undertaken at three replicate sites per each stage of rehabilitation on a 1:14,000 scale to provide statistically valid data that can be used to guide rehabilitation maintenance activities and to demonstrate rehabilitation success.

The rehabilitation area survey will use a combination of stability and erosion assessments, soil analyses and various measurements of ecosystem diversity and habitat values (as described in the BMP) to assess against benchmark biodiversity data and key indicators of ecosystem function, including landscape organisation and soil surface condition to measure how the landscape retains and uses vital resources.

Individual observations of soil surface indicators allow an assessment of how the site is functioning in relation to the indices of stability, infiltration and nutrient cycling. Soil condition can also be compared directly with vegetation data to show a cause and effect understanding of the whole site.

Between two and six transects will be surveyed for each rehabilitated vegetation type site to account for the size of the rehabilitated vegetation community areas and slope variations. Sites will be surveyed yearly for the first five years with the frequency of surveys at each site to be reassessed following this period.

Two monitoring sites within rehabilitated areas have been monitored yearly for surveying flora, vertebrates and invertebrates as described above. Additional surveys will be undertaken with the next annual survey and additional rehabilitation survey sites will be added, based on progressive rehabilitation areas.

Soil testing and erosion monitoring will also be undertaken to assess the presence of active erosion and dispersive soil and spoil. The results of this testing will be used for comparison with domain completion criteria.

Flora, vertebrate and invertebrate monitoring described in the BMP will be used to determine progress towards, or achievement of the completion criteria, averaged data from each stratification within the monitoring sites will be compared with the averaged benchmark data (Table 9.4 of the BMP).

The results of the rehabilitation monitoring will be incorporated into continuously developing the species list and procedures for rehabilitation.

As a minimum, the long term rehabilitation monitoring program will allow for adaptive management by reviewing substandard performance from a rehabilitation area and evaluating the probability of an event occurring; evaluating the consequence; and using a risk based approach to determine trigger levels (both upper and lower) where response or action is required. A TARP will be implemented to respond in the event of poor rehabilitation performance or unexpected result (refer to **Section 9.2**).

8.3 Measuring Performance Against Rehabilitation Objectives and Rehabilitation Completion Criteria

In order to receive closure sign-off of rehabilitation, it will be necessary to demonstrate rehabilitated areas have reached their established completion criteria.

The completion criteria are objective target levels or values that can be measured to quantitatively demonstrate the progress and ultimate success of a biophysical process. The proposed completion criteria have been developed for each phase of rehabilitation so that the success can be tracked throughout the life of the mine. The validation methods and assurance process at each phase of rehabilitation are detailed in **Table 7-1**.

The key mechanism for reviewing compliance against the rehabilitation objectives and completion criteria is the Annual Review (which will similarly include the Annual Rehabilitation Report and ENV-RHB-STR-001-ATT-003 Forward Works Program). Additionally, ad hoc reporting may be undertaken in the event of an environmental incident occurring that is related to mine rehabilitation or other environmental issues

BCOPL prepares and submits an Annual Review which outlines the environmental performance of the Project over the preceding calendar year. The Annual Review must be submitted within 90 days of the end of the reporting period in accordance with Schedule 5, Condition 4 of MP 09_0182. The Annual Review for BCOPL will discuss rehabilitation management issues and performance for the BCM. This reporting will include:

- Results of ongoing monitoring;
- A quantitative and qualitative assessment of the rehabilitation progress;
- Identification of and reporting on the progress of non-conformance issues and corrective action requests identified during periodic audits or from community complaints;
- The performance of rehabilitation;
- The implementation and effectiveness of the rehabilitation controls and conditions specifically relating to the development;
- Results against the criteria set out in **Table 4-1**;
- Key trends in monitoring results and progression towards achievement of rehabilitation objectives and completion/relinquishment criteria as detailed in **Table 4-1**;
- Reporting on discrepancies between the predicted and actual results;
- Reporting of where a TARP has been implemented to counter poor/unpredicted rehabilitation results or environmental impacts;
- Results of the rehabilitation trials; and
- Details of any incidents and non-compliances.

Approval has previously been sought and obtained from the Resources Regulator to align the reporting period and reporting due date for the Annual Rehabilitation Report and ENV-RHB-STR-001-ATT-003 Forward Works Program required under the *Mining Act 1992* with the Annual Review required under MP 09_0182. This will need to be revisited for the 2025 reporting period including ML1883.

Annual Reviews will be made publicly available on the BCOPL website (www.idemitsu.com.au/boggabri).

9 REHABILITATION RESEARCH, MODELLING AND TRIALS

9.1 Current Rehabilitation Research, Modelling and Trials

Rehabilitation trials have been undertaken to optimise rehabilitation techniques. These include assessments of fertilisers, plant species, water retention, runoff, optimal planting times, quality and quantity of topsoil and ripping mounding techniques (Boden and Associates, 2011). While the initial rehabilitation trials focused on the restoration of optimal commercial timbers for forestry, the current and future rehabilitation will be principally targeting biodiversity conservation and restoration of the Threatened Box Gum Woodland community and habitats for Threatened species.

Areas which have previously been rehabilitated are described below. Rehabilitation trials have been planted in 2008, 2009, 2010 and 2011 as follows:

- 2008 Species Trial – Three trial areas the upper south, upper west and lower south trial areas, each comprising 15 species. The trials were used to test the interactions between the two aspects southerly (cool) and westerly (warm) and position in the slope.
- 2009 Plantings – A total of nine hectares were planted in April 2009. Three local species *E. crebra*, *E. pilligaensis* and *E. albens* were planted randomly within each plant line.
- 2010 Plantings – A further 8 hectares were planted in April 2010. Three local species i.e. *E. albens*, *E. crebra* and *E. pilligaensis* were planted separately in blocks each of two rows. A fertiliser trial was established in these plantings to quantify the response to various dosages of the MAP fertiliser.
- 2011 Plantings – A total of 15 hectares were planted in May-June 2011. Three local species i.e. *E. albens*, *E. crebra* and *E. pilligaensis* were planted separately in blocks each of two rows.

Ongoing rehabilitation inspections indicate that the previous rehabilitation plantings are largely reflective of a transition vegetation community within existing analogue sites of the undisturbed Leard State Forest and that they will be compatible with the proposed rehabilitation.

In general, observations of the natural regeneration within the rehabilitation area reveal a healthy development of native flora species germinating from topsoil (Boden & Associates 2011; Parsons Brinckerhoff 2011). Recent biodiversity monitoring (Parsons Brinckerhoff, 2015) indicates that vegetation within the rehabilitation area has a moderate to high diversity of native species, with approximately 69% of the flora species occurring at the analogue site within the Leard State Forest having also been found within the rehabilitation monitoring plots. The diversity of native flora species has generally increased over time. All of the monitoring plots have a relatively high number of species that are characteristic of the critically endangered community of White Box Yellow Box Blakely's Red Gum Grassy Woodland and derived native grassland as listed under the EPBC Act.

In early 2016, BCOPL commissioned a preliminary evaluation of growth media within the 2008 to 2014 rehabilitation areas (Landloch, 2016). The assessment was conducted in accordance with the procedure detailed in the SMP. Samples were subject to soil surface descriptions, morphological descriptions, field tests and laboratory analysis.

The analysis concluded that there were no major limitations to plant growth. In general terms, the growth media were considered adequate to support vegetation and are clearly able to support the growth of tube stock planted.

Nutritional differences in topsoil materials between rehabilitation sites and analogue sites were identified, however it was noted that these could be easily rectified with fertiliser application. Erosion was also noted across rehabilitation areas which may be improved through incorporation of gypsum. Overburden substrate alkalinity was observed to be high but did not appear to be impacting growth of seedlings. It was recommended that further analysis be undertaken and growth media criteria be revised. Further routine monitoring will be undertaken as part of the RMP requirements. The growth media criteria have been revised in the SMP, which forms Appendix H of the approved BMP dated October 2018.

Apart from ongoing maintenance and repairs to erosion in 2020, not further rehabilitation trials or research has been undertaken at BCM.

9.2 Future Rehabilitation Research, Modelling and Trials

Flora and Fauna

Monitoring of flora and fauna communities within and beyond the surrounding Leard State Forest (analogue sites beyond the CL 368 boundaries) is currently being conducted as part of the ongoing biodiversity monitoring program for the BCM. This monitoring program will continue and should be undertaken to provide comparative data for assessment of the success of the rehabilitation works. The analogue monitoring program will be updated to incorporate soil parameters to be measured. The findings of this work will drive the development of soil-based closure criteria. Soil monitoring at analogue sites will also be undertaken.

The data obtained from the analogue sites will provide a range of values from replicated examples of similar vegetation communities. Rehabilitation areas are compared to reference sites which best represent the final land use, vegetation community and management conditions to which they will be subjected.

These analogue sites will also provide detailed information on fauna assemblage (birds, bats and invertebrates), their habitats and utilisation within both the eastern and western portions of Leard State Forest. The analogue sites will allow rehabilitation monitoring to determine the successful establishment of fauna assemblages within the rehabilitation areas, their distribution across the rehabilitation areas and relative success of the proposed regional wildlife corridor identified within the BCOPL Biodiversity Offset Strategy (Parsons Brinckerhoff, 2010a).

In order to demonstrate rehabilitation success or succession toward rehabilitation success, specific indicators will be expected to equal or exceed values obtained from the reference site under the same set of conditions or demonstrate a positive trend towards target values. Criteria will also be set for stages of rehabilitation to show progression towards rehabilitation success.

Growth Media

Studies previously conducted (Landloch, 2016) identified that there were no major limitations to plant growth within the growth media utilised on mine rehabilitation between 2008 and 2014. Routine monitoring undertaken as part of the RMP have also indicated that the growth media being used and the methods applied to recover, store and manage the growth media are continuing to provide successful results.

Final Void and Mine Closure Plan

In accordance with Schedule 3, Condition 72 of the MP 09_0182, an updated Final Void and Mine Closure Plan will be developed before the end of December 2025.

The development of this plan will entail an extensive work program which will consider various aspects in relation to the final landform, including the partially infilled final void area. This is likely to include technical studies in (at least) the following technical fields:

- Geochemistry;
- Geotechnical;
- Groundwater;
- Surface Water; and
- Landform Evolution Modelling.

Preliminary background work on this plan has been commenced with the collection of baseline environmental monitoring and geochemical information. The detailed work program is expected to continue over the next three years.

Rehabilitation Trials

BCOPL has undertaken a tree thinning trial within previously rehabilitated areas. This is hypothesised to further promote the growth rate and health of the remaining trees and to enable the establishment of a ground layer which meets the intended open woodland community final land use. The trial was initiated in August 2024 within the 2010 and 2011 rehabilitation areas. However, unsuitable weather conditions and ecologist advice at that time subsequently caused the program to be deferred until April 2025. Accordingly, future iterations of this RMP will refer to the outcomes of this trial once included in the annual rehabilitation monitoring program in 2026.

10 INTERVENTION AND ADAPTIVE MANAGEMENT

Outcomes of the annual rehabilitation monitoring will be recorded and any mitigation actions implemented as required. Where necessary, rehabilitation procedures will be amended accordingly with the aim to continually improve rehabilitation standards.

The monitoring program will:

- Compare results against rehabilitation objectives and targets (analogue sites);
- Identify possible trends and continuous improvement;
- Link to records of rehabilitation to determine causes and explain results;
- Assess effectiveness of environment controls implemented;
- Where required, identify modifications required for the monitoring program, rehabilitation practices or areas requiring research;
- Compare flora species present against original seed mix and/or analogue sites;
- Assess vegetation health;
- Assess vegetation structure (i.e. upper, mid and lower storey); and
- Where applicable, assess native fauna species diversity and the effectiveness of habitat creation for target fauna species.

If rehabilitation failure has occurred further investigation to establish a cause and appropriate remediation strategy(s) will be undertaken. The issues to consider will include the following:

- Nutrient availability;
- pH, salinity and metal toxicity;
- Shallow root depth;
- Other soil limitations;
- Insect attack;
- Lack of N-fixing legumes;
- Lack of organisms involved in litter breakdown (i.e. fungal fruiting bodies) and nutrient cycling (i.e. puff balls);
- Excessive grazing;
- Predation;
- Evidence of drought effects or storm damage;
- Poor soil preparation; and
- Weed competition.

As a minimum, the long term rehabilitation monitoring program will allow for adaptive management by reviewing substandard performance from a rehabilitation area and evaluate the probability of an event occurring; evaluating the consequence; and using a risk-based approach to determine trigger levels (both upper and lower) where response or action is required.

If rehabilitation failure has occurred, further investigation to establish a cause and appropriate remediation strategy(s) will be undertaken. The rehabilitation monitoring program allows for adaptive management by reviewing substandard performance from a rehabilitation area and evaluate the probability of an event occurring; evaluating the consequence; and using a risk-based approach to determine trigger levels (both upper and lower) where response or action is required.

Table 10-1: Rehabilitation Trigger Action Response Plan

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Changes in legislation or approval conditions requiring a review of rehabilitation criteria or change to land use or ecological community.	New legislation implemented, but no impact on current closure land use or criteria.	New legislation implemented that requires changes to land-use or closure criteria e.g. slope gradients or vegetation community. Required changes are such that they can be implemented without requiring major redesign work.	New legislation implemented that requires major changes to land-use or closure criteria, requiring major changes to rehabilitation design or processes, as well as impacting on closure costs.	
	Response to above Triggers			
	No actions required except to continue to review any legislation changes that may affect rehabilitation methodology. If best practice is implemented in rehabilitation works, then the risk of legislation changes impacting on planned or implemented rehabilitation will be reduced.	Rehabilitation Plan and closure criteria are to be updated in accordance with updated legislation. Impact on closure costing to be determined. Rehabilitation designs are to be updated as required.	Closure criteria and final land use options are to be reviewed and the rehabilitation processes developed to achieve the required changes, specialist advice may be required. Closure costing and rehabilitation plans, and manuals are to be updated.	Triggers for legislation changes will include new approval conditions, updates of mining lease conditions, RMP amendments, changes to mine closure plan.
Overburden Emplacement footprint within design specifications	Outside toe of the dump is well within designated footprint	Toe of the dump is <5 m from the designated dump footprint, or permanent infrastructure is to be placed within the dump footprint.	Toe of dump has extended past the designated dump footprint, or permanent infrastructure has been placed within the dump's footprint.	Identified during Annual Review process and annual rehabilitation monitoring inspection. Toe dump constraints can be visually inspected if toe markers have been put in place. Survey plans and or aerial photography can be used to

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
				compare planned design with actual.
	Response to above Triggers			
	Confirm with mine planning that no additional extension on the dump has been planned.	Discuss situation with mine planning and put procedures in place to prevent toe of dump extending beyond the design criteria. Design criteria can be reviewed and amended if the dump rehabilitation design is feasible within the amended toe constraints.	Dumping should be put on hold until the situation has been reviewed and a workable rehabilitation plan implemented for the change in dumping strategy. If no alternative plan is feasible then all dumping that would impact on the toe of the dump is to cease. An investigation into the cause of the overburden exceeding the toe constraints is to be investigated with corrective actions taken.	
Overburden Emplacement outside the design criteria (shape, height, and volume)	Dump is in accordance with design criteria.	Dump area has reached the design capacity.	Dumping has extended beyond the design criteria (shape, height, and volume).	Identified during Annual Review process, annual rehabilitation monitoring inspection, routine visual inspections, mining and survey reports. Toe dump constraints can be visually inspected if toe markers have been put in place. Survey plans and or aerial photography can be used to compare planned design with actual.

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
	Response to above Triggers			
	No action to be taken.	Discuss situation with mine planning and put procedures in place to prevent toe of dump extending beyond the design criteria. Design criteria can be reviewed and amended if the dump rehabilitation design is feasible within the amended toe constraints.	Dumping should be put on hold until the situation has been reviewed and a workable rehabilitation plan implemented for the change in dumping strategy. If no alternative design plan is feasible then all dumping should be halted. An investigation into the cause of the change of the dumping plan is to be investigated with corrective actions taken.	
Slope Gradient	Slope gradient $\leq 1\%$	Slope gradient $\geq 2\%$ of design gradient	Slope gradient $\geq 4\%$ of design gradient	Survey is undertaken as part of the waste dump inspection and internal sign-off process prior to the placement of subsoil and topsoil.
	Response to above Triggers			
	Do nothing, progress rehabilitation works.	Review waste dump ITP's. Instigate investigation into cause of the non-conformance. Regrade slopes and survey.	Review waste dump ITP's. Instigate investigation into cause of the non-conformance. Determine and implement methodology to return the slope to design gradients.	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Topsoil	Suitable topsoil quality and quantity for planned rehabilitation.	Insufficient topsoil for planned rehabilitation.	Insufficient suitable growing media for planned rehabilitation.	Identified during topsoil placement inspections undertaken following topsoil placement and during soil testing undertaken during the annual rehabilitation monitoring program.
	Response to above Triggers			
	Proceed with seeding and/or planting.	Apply ameliorated subsoil.	Test mine spoil for agronomic and erosion parameters. Amend mine spoil for rehabilitation purposes. Undertake an investigation to understand why topsoil and subsoil resources were insufficient.	
Plant Species Establishment	>75% of target species diversity present 3 years following seeding.	<75% and >40% of target species diversity present 1 year following seeding.	<40% of target species diversity present 1 year following seeding.	Identified during annual rehabilitation inspection. Measured as number of grass seedlings that have emerged ± 2 weeks after expected germination. Establishment rate is determined by counting the number of seedlings in a few (1-3) square metre plots with comparison to species diversity sown.
	Response to above Triggers			
	No action to be taken other than continued monitoring.	Visual investigation for potential causes of low establishment rate, including (soil moisture &	Investigation into cause of low seed establishment. Investigations may include: a soil sampling	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
		temperature, ground conditions). Record any findings. Follow up seeding to improve plant densities is to be considered. Undertake spot topsoil and subsoil samples to determine if soil parameters fall within specified ranges.	program including soil moisture levels, analysis of meteorological conditions, follow seed germination testing with original seed used, germination trials in seed trays using field growth medium.	
Germination testing	>80% of seeds germinate	65% - 80% of seeds germinate	<40% of seeds germinate	
	Response to above Triggers			
	No action to be taken and germination rate is to be used to determine seeding rate.	Cause of poor germination rate is to be investigated. Investigation is to include growth vigor, as vigor may also be affected. Actions to improve germination using various seed preparation methodologies may be required and the germination trials redone. Seeding rate in kg/ha is to be adjusted to compensate for poor germination. An alternate option is to include other seed which has a higher germination rate if available.	Investigation of flow germination rate to be undertaken. Actions to improve germination using various seed preparation methodologies may be required and the germination trials. Seeding rate in kg/ha is to be adjusted to compensate for poor germination. Other seed may need to be sourced.	Identified during seed germination trials prior to annual rehabilitation planting. Measured as number of grass seedlings that have emerged ± 2 weeks after expected germination. Establishment rate is determined by counting the number of seedlings in a few (1-3) square metre plots with comparison to species diversity sown.
Weeds and invader species within the seed mix	No identified weeds	Suspect weed and/or invader species.	Weeds and/or invader species identified in seed mix.	Weeds and invader species will be identified during germination trials. Identification can also be done by visual inspection of the seed mix prior to use. History and

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
				sourcing of the seeds acts as a prompt to investigate the seed mix.
	Response to above Triggers			
	No action to be taken.	Seed mix to be visually screened and additional testing undertaken to confirm if free of weeds.	Seed mix is not to be used on any mine rehabilitation areas.	
Rehabilitation Monitoring				
Geotechnical instability	No identified signs of instability or mass movement.	Signs of minor settlement (drop in elevation), appearance of tension cracks.	Signs of significant movement: Elongation and widening of tension cracks, visible vertical or horizontal movement, soil bulging downslope of settlement	Ground movement will be identified as part of infield rehabilitation monitoring (ecological or annual walk around, remote sensing initiative to identify erosion would also assist in the identification of ground movement).
	Response to above Triggers			
	No action to be taken.	Depth and extent of cracking to be recorded and routine monitoring to be undertaken. Survey stations for movement may be required. Minor settlement can be infilled with topsoil and reseeded if required.	Geotechnical investigation of the ground movement is to be undertaken together with an assessment of damage to rehabilitation landform or drainage structure.	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Erosion and loss of topsoil/growth medium	No rill erosion evident	Rills and inter rill erosion present	Gullies and tunnels present	Visual assessment for rill, inter rill, gully and tunnel erosion inlet and outlet points. Identified during annual rehabilitation monitoring or routine site inspections (e.g. monthly environmental inspections).
	Response to above Triggers			
	No action is to be taken other than continued monitoring following rainfall.	Undertake contour scarification to increase roughness and remove rills. Increase surface cover via soil polymers, rock and timber debris or cover crops.	Gypsum treatment of dispersive soils. Regrade landform to promote sheet flow. Maintenance of drainage structures to reduce ponding. Removal of diversion banks once 70% soil surface cover is achieved.	
Vegetation predation or animal burrowing	Minimal amount of vegetation predation by browsers and grazers (kangaroos, rabbits, insects), no effect on plant growth.	Signs of plant stress due to grazing, plants able to cope but show stunted growth.	Significant plant dieback due to animal or insect predation.	Identified as part of annual rehabilitation monitoring.
	Response to above Triggers			
	No action to be taken other than continued monitoring.	Main culprits causing predation are to be identified. Animal numbers are to be monitored and culled where required.	Measures to be taken to protect young plants and animal control to be undertaken.	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Ecological Vegetation communities have unsatisfactory progress towards achieving the set closure criteria, or there is degradation in the ecological community function.				
	Response to above Triggers			
Destructive environmental event (fire, drought, flood, insect plague)	Minimal effect/damage to vegetation and landform including drainage structures, vegetation able to fully recover without intervention.	Minor damage to ecological plant structures and or landform and stability structures. Minimal remediation required e.g. reseeding or fertiliser application.	Significant damage to ecological plant structures and or landform and stability structures requiring remediation and redesign.	Identified as part of post event inspection and monitoring by rehabilitation specialist as required.
	Response to above Triggers			
	No action to be taken other than continued monitoring.	Remediation action plan to be implemented by site personnel.	Detailed assessment to be undertaken by rehabilitation specialist and remedial action plan developed. Preventative measure to be investigated and any recommendations are to be implemented and the rehabilitation manual updated as required.	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Diversion Banks	Diversion banks show no signs of erosion.	Diversion banks show signs of greater than expected sediment deposition, erosion or water ponding.	Diversion bank has significant sediment deposition, signs of water overtopping or substantial erosion (undercutting, tunnel erosion, riling or gully along bank).	Monitoring is undertaken during routine inspections (walk around) and formal annual rehabilitation monitoring. Site incident reporting and environmental observations may also identify issues.
	Response to above Triggers			
	Continued monitoring. Remove diversion bank and re-establish sheet flow conditions when 70% soil surface (vegetation) cover exists below diversion bank.	Monitoring frequency is to be increased, and observations undertaken during rainfall events that cause runoff. Local repair work is to be undertaken as needed. Remove diversion bank and re-establish sheet flow conditions when 70% soil surface (vegetation) cover exists below diversion bank.	Investigation into the cause of the diversion bank failure is to be initiated, and the design parameters reviewed, with learning fed back into the rehabilitation processes. Investigation initiated by erosion specialist if ground movement (slumping, settlement) is suspected. Grade survey of the diversion bank may be required if drainage is an issue. After initial causes have been identified a remediation plan is to be implemented. Remove diversion bank and re-establish sheet flow conditions when 70% soil surface (vegetation) cover exists below diversion bank.	

Trigger Action Response Plan (TARP)				
Response to Undesired Changes to Rehabilitation affecting Outcome Criteria, or Operational Activities that may affect Rehabilitation Outcomes				
Rehabilitation or Operational Activity	Green	Amber	Red	Monitoring/ Measuring Method
Slope Drains & Drop structures	Slope drains show no signs of erosion and any geofabrics/membranes or rock lining are in place as constructed. No signs of water overtopping or undercutting of drain structure.	Slope drains starting to show signs of channel bed erosion, minor undercutting of drain inlets, erosion riling of drain sidewalls, drain outlets show signs of erosion. Topsoil/growth medium shows signs of accelerated erosion and degradation of any vegetation covering.	Severe channel erosion, damage to any geofabric linings or stone lining, overtopping of drain sidewalls, loss of topsoil/growth medium, tunnel erosion under or beside the structure.	Monitoring is undertaken during routine inspections (walk around) and formal annual rehabilitation monitoring. Site incident reporting and environmental observations may also identify issues.
	Response to above Triggers			
	No action to be taken other than continued monitoring.	Monitoring frequency is to be increased, and observations undertaken during rainfall events causing runoff. Local repair work is to be undertaken as needed. Remove diversion bank and re-establish sheet flow conditions when 70% soil surface (vegetation) cover exists below diversion bank.	Investigation into the cause of the failure is to be initiated, and the design parameters reviewed, with learning fed back into the rehabilitation design. Erosion specialist investigation initiated if tunnel erosion is suspected. Grade survey of the diversion bank may be required if drainage is an issue. After initial causes have been identified a remediation plan is to be implemented. Remove diversion bank and re-establish sheet flow conditions when 70% soil surface (vegetation) cover exists below diversion bank.	

11 REVIEW, REVISION AND IMPLEMENTATION

Review of the RMP

Review of this RMP may be triggered by any of the following

- Changes to construction methodologies, mining operations, equipment or design;
- A hazard, near miss, or incident;
- Outcomes of an internal or external audit;
- Changes to legislation or guidelines;
- Modifications to the MP 09_0182, mining leases, EPL or other relevant approvals; and
- Impending expiration of the RMP term.

The RMP will be revised in accordance with requirements of Clause 11 of Schedule 8A to the *Mining Regulation 2016* including:

- As a consequence of an amendment made to the rehabilitation objectives, rehabilitation completion criteria or final landform and rehabilitation plan;
- To reflect any changes to the risk control measures in the RMP that are identified in a rehabilitation risk assessment; and
- Whenever directed in writing to do so by the Secretary.

Environment Incident Reports

All environment incidents will be managed in accordance with BCOPL's Incident Management Procedure. Reporting of environment incidents by the contractor(s) to the BCOPL Environment Superintendent shall be undertaken as soon as practically possible, but not later than 24 hours following the incident. In accordance with the MP 09_0182, the EPL and Mining Lease conditions, BCOPL is required to provide verbal and written notification to the appropriate regulatory authorities of any incident that has caused, or threatens to cause, material harm to the environment. Relevant contractors will also be notified immediately of any non-compliant activities that present a risk of causing material environmental harm in the area that they are working.

Following an incident, corrective actions will be identified and agreed on with relevant personnel (and regulators if required) prior to implementation. Corrective actions may include a review of any relevant plans and procedures following identification of a non-conformance. Where the non-conformance issue is associated with an inspection, audit or monitoring event, the actions will be linked to the record of the event. Incident reports will be reviewed on a regular basis to ensure actions are progressed appropriately.

Independent Audit

An internal audit will be commissioned by the BCOPL Environment Superintendent (or delegate) to ensure the implementation of the RMP. Non-conformance issues and corrective action requests will be identified and formally documented in the audit process.

Abbreviations

Abbreviation	Definition
A	Authorisation
ARI	Average Recurrence Interval
ASCF	Aboriginal Stakeholder Consultation Forum
BC Act	<i>Biodiversity Conservation Act 2016</i>
BCM	Boggabri Coal Mine
BCOPL	Boggabri Coal Operations Pty Ltd
BCSD	Department of Planning and Environment – Biodiversity Conservation and Science Division
BMP	Biodiversity Management Plan
BNCCA ACT	<i>Brigalow and Nandewar Community Conservation Area Act 2005</i>
BOA	Biodiversity Offset Areas
BTM Complex	Boggabri, Tarrawonga, Maules Creek Complex
CBIMP	Common Boundary Integration Management Plan
CBIMP	Common Boundary Integrated Management Plan
CCC	Community Consultative Committee
CEC	Cation Exchange Capacity
CFMP	Clearing and Fauna Management Protocol
CHMP	Cultural Heritage Management Plan
CHPP	Coal Handling and Preparation Plant, including By-pass crusher
CL	Coal Lease
CMA	Catchment Management Authority
CSIRO	Commonwealth Scientific and Industrial Research Organisation
DA	Development Application
DCCEEW	Commonwealth Department of Climate Change, Energy, the Environment and Water
DECC	Former Department of Environment and Climate Change
DECCW	Former Department of Environment, Climate Change and Water
DPE	Former Department of Planning and Environment
DPHI	Department of Planning Housing and Infrastructure (former DPE)
DPI	NSW Department of Primary Industries
DRE	Former NSW Department of Trade and Investment - Division of Resources and Energy

Abbreviation	Definition
DRG	Former Department of Planning and Environment – Division of Resources and Geoscience
EA	Environment Assessment
EC	Electrical Conductivity
EP&A Act	<i>Environmental Planning and Assessment Act, 1979</i>
EPBC Act	<i>Environmental Protection and Biodiversity Conservation Act, 1999</i>
EPL	Environmental Protection Licence
ESP	Exchangeable Sodium Percentage
GMP	Groundwater Management Plan
GSC	Gunnedah Shire Council
IA	Idemitsu Australia Pty Ltd
IBC	Idemitsu Boggabri Coal Pty Limited
IKC	Idemitsu Kosan Co. Ltd
Km	Kilometre
LOM	Life of Mine
ML	Mining Lease
MNES	Matters of National Environmental Significance
MOP	Mining Operations Plan
Mt	Million Tonnes
Mtpa	Million Tonnes Per Annum
NAF	Non-acid forming
NSC	Narrabri Shire Council
NSW	New South Wales
NSW DCCEEW	NSW Department of Climate Change, Energy, the Environment and Water
OC	Organic Compound
OEA	Overburden Emplacement Area
OEH	Former NSW Office of Environment and Heritage
PAC	Former NSW Planning and Assessment Commission
PAF	Potentially Acid Forming
POEO Act	<i>Protection of the Environment (Operations) Act, 1997</i>

Abbreviation	Definition
RL	Relative Level
RMP	Rehabilitation Management Plan
RMS	NSW Roads and Maritime Services
ROM	Run of Mine
RR	Department of Primary Industries and Regional Development, NSW Resources, Resources Regulator
SMP	Soil Management Protocol
SWB	Site Water Balance
SWMP	Surface Water Management Plan
TARP	Trigger Action Response Plan
TCPL	Tarrawonga Coal Pty Limited
WEPP	Water Erosion Prediction Project
WMP	Water Management Plan
WMS	Water Management Strategy

A.1 Approved Rehabilitation Objectives Statement



**NSW
Resources
Regulator**

ROBJ0001211

APPROVED REHABILITATION OBJECTIVES STATEMENT

Boggabri Coal

FRIDAY 13 OCTOBER 2023

Contents

Summary..... 3

Important note..... 3

Rehabilitation Objectives..... 4

Summary

DETAIL	APPROVAL
Reference	ROBJ0001211
Date of approval	Friday 13 October 2023
Mine	Boggabri Coal
Contact	Ben Hiatt

Important note

The Regulator may make the information in your application and any supporting information(including this approval) available for inspection by members of the public, including by publication on its website or by displaying the information at any of its offices. If you consider any part of your application to be confidential, please communicate this to the Regulator via the message function on this application within the Portal.

Rehabilitation Objectives

The following rehabilitation objectives have been approved.

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Bushfire	A1	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A1	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A1	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	A1	Final Landform is safe for future use
Ecological rehabilitation	A1	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.
Ecological rehabilitation	A1	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A1	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A1	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.
Ecological rehabilitation	A1	Levels of ecosystem function have been established that demonstrate the rehabilitation is

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		self-sustainable
Ecological rehabilitation	A1	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A1	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A1	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A1	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A1	Final Landform is safe for future use
Ecological rehabilitation	A1	Final Landform is safe for future use
Ecological rehabilitation	A1	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A1	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A1	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Groundwater	A1	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Groundwater	A1	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A1	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A1	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A1	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A1	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Land contamination	A1	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A1	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A1	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	A1	Safe, stable and non-polluting.
Landform stability	A1	Safe, stable and non-polluting.
Landform stability	A1	Landform generally blends in with the surrounding landscape.
Landform stability	A1	Safe, stable and non-polluting.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Landform stability	A1	Landform generally blends in with the surrounding landscape.
Landform stability	A1	Landform generally blends in with the surrounding landscape.
Removal of infrastructure	A1	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A1	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A1	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A1	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A1	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A1	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Surface water	A1	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A1	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A1	Constructed landforms drain to the natural environment.
Surface water	A1	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A1	Constructed landforms drain to the natural environment.
Surface water	A1	Constructed landforms drain to the natural environment.
Surface water	A1	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A1	Water quality non-polluting and appropriate for conservation end land use.
Water approvals	A1	Structures that take or divert water such as final voids, dams, levees etc. are appropriately

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take.
Water approvals	A1	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take.
Water approvals	A1	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take.
Bushfire	A3	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A3	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A3	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	A3	Final Landform is safe for future use
Ecological rehabilitation	A3	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A3	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.
Ecological rehabilitation	A3	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Ecological rehabilitation	A3	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A3	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181
Ecological rehabilitation	A3	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A3	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A3	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A3	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A3	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A3	Final Landform is safe for future use
Ecological rehabilitation	A3	Final Landform is safe for future use
Ecological rehabilitation	A3	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Groundwater	A3	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		environmental harm.
Groundwater	A3	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A3	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A3	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A3	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A3	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Land contamination	A3	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A3	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A3	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	A3	Landform generally blends in with the surrounding landscape.
Landform stability	A3	Landform generally blends in with the surrounding landscape.
Landform stability	A3	Safe, stable and non-polluting.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Landform stability	A3	Safe, stable and non-polluting.
Landform stability	A3	Landform generally blends in with the surrounding landscape.
Landform stability	A3	Safe, stable and non-polluting.
Removal of infrastructure	A3	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A3	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A3	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A3	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A3	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A3	All open cut mining infrastructure decommissioned and removed.
Surface water	A3	Constructed landforms drain to the natural environment.
Surface water	A3	Constructed landforms drain to the natural environment.
Surface water	A3	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A3	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A3	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A3	Constructed landforms drain to the natural environment.
Water approvals	A3	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Water approvals	A3	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Water approvals	A3	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Bushfire	A4	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A4	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A4	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	A4	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A4	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A4	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181
Ecological rehabilitation	A4	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A4	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A4	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A4	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A4	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181
Ecological rehabilitation	A4	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A4	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A4	Final Landform is safe for future use
Ecological rehabilitation	A4	Final Landform is safe for future use
Groundwater	A4	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A4	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A4	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Groundwater	A4	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A4	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A4	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Land contamination	A4	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A4	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A4	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	A4	Safe, stable and non-polluting.
Landform stability	A4	Safe, stable and non-polluting.
Landform stability	A4	Landform generally blends in with the surrounding landscape.
Landform stability	A4	Landform generally blends in with the surrounding landscape.
Landform stability	A4	Landform generally blends in with the surrounding landscape.
Landform stability	A4	Safe, stable and non-polluting.
Removal of infrastructure	A4	All open cut mining infrastructure decommissioned and removed.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Removal of infrastructure	A4	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A4	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A4	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A4	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A4	All open cut mining infrastructure decommissioned and removed.
Surface water	A4	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A4	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A4	Constructed landforms drain to the natural environment.
Surface water	A4	Constructed landforms drain to the natural environment.
Surface water	A4	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A4	Constructed landforms drain to the natural environment.
Water approvals	A4	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Water approvals	A4	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Water approvals	A4	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Bushfire	A7	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	A7	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	A7	Final Landform is safe for future use
Ecological rehabilitation	A7	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A7	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.
Ecological rehabilitation	A7	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A7	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	A7	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A7	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	A7	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities, including PCT78/NA193, PCT84/NA191 and/or PCT102/NA181.
Ecological rehabilitation	A7	The vegetation composition of the rehabilitation is recognisable as the target vegetation

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	A7	Final Landform is safe for future use
Groundwater	A7	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A7	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	A7	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	A7	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Land contamination	A7	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Land contamination	A7	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	A7	Landform generally blends in with the surrounding landscape.
Landform stability	A7	Landform generally blends in with the surrounding landscape.
Landform stability	A7	Safe, stable and non-polluting.
Landform stability	A7	Stable, safe and non-polluting.
Removal of infrastructure	A7	All open cut mining infrastructure decommissioned and removed.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Removal of infrastructure	A7	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	A7	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A7	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Surface water	A7	Constructed landforms drain to the natural environment.
Surface water	A7	Constructed landforms drain to the natural environment.
Surface water	A7	Water quality non-polluting and appropriate for conservation end land use.
Surface water	A7	Water quality non-polluting and appropriate for conservation end land use.
Water approvals	A7	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Water approvals	A7	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Bushfire	A8	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	A8	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	A8	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Ecological rehabilitation	A8	Final Landform is safe for future use
Ecological rehabilitation	A8	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Landform stability	A8	Safe, stable and non-polluting.
Landform stability	A8	Landform generally blends in with the surrounding landscape.
Removal of infrastructure	A8	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	A8	All open cut mining infrastructure decommissioned and removed.
Surface water	A8	Constructed landforms drain to the natural environment.
Surface water	A8	Water quality non-polluting and appropriate for conservation end land use.
Agricultural revegetation	B1	Revegetation is sustainable for the long-term and only requires maintenance that is consistent with the intended final land use.
Agricultural revegetation	B1	Land capable of sustaining low intensity grazing land use.
Agricultural revegetation	B1	Final Landform is safe for future use
Bushfire	B1	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Groundwater	B1	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	B1	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Land contamination	B1	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	B1	Safe, stable and non-polluting.
Landform stability	B1	Landform generally blends in with the surrounding landscape.
Removal of infrastructure	B1	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	B1	All open cut mining infrastructure decommissioned and removed.
Surface water	B1	Water quality non-polluting and appropriate for agricultural end land use.
Surface water	B1	Constructed landforms drain to the natural environment.
Water approvals	B1	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Agricultural revegetation	B3	Final Landform is safe for future use
Agricultural revegetation	B3	Revegetation is sustainable for the long-term and only requires maintenance that is consistent with the intended final land use
Agricultural revegetation	B3	Land capable of sustaining low intensity grazing land use.
Bushfire	B3	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Groundwater	B3	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Groundwater	B3	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Land contamination	B3	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	B3	Landform generally blends in with the surrounding landscape.
Landform stability	B3	Safe, stable and non-polluting.
Removal of infrastructure	B3	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Removal of infrastructure	B3	All open cut mining infrastructure decommissioned and removed.
Surface water	B3	Water quality non-polluting and appropriate for intended final land use.
Surface water	B3	Constructed landforms drain to the natural environment.
Water approvals	B3	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Agricultural revegetation	B7	Land capable of sustaining low intensity grazing land use.
Agricultural revegetation	B7	Revegetation is sustainable for the long-term and only requires maintenance that is consistent with the intended final land use
Agricultural revegetation	B7	Final Landform is safe for future use
Bushfire	B7	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Groundwater	B7	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	B7	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Land contamination	B7	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	B7	Safe, stable and non-polluting.
Landform stability	B7	Landform generally blends in with the surrounding landscape.
Removal of infrastructure	B7	All open cut mining infrastructure decommissioned and removed.
Removal of infrastructure	B7	Exploration drill holes / groundwater piezometers decommissioned and sealed.
Surface water	B7	Water quality non-polluting and appropriate for intended final land use.
Surface water	B7	Constructed landforms drain to the natural environment.
Water approvals	B7	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Bushfire	G3	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Land contamination	G3	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	G3	Safe, stable and non-polluting.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Removal of infrastructure	G3	All open cut mining infrastructure decommissioned and removed.
Retention of infrastructure	G3	Any infrastructure that is to be retained as part of the final landuse (subject to agreement with the Resources Regulator) must be safe and not pose any hazards to the community.
Surface water	G3	Runoff water quality from mine site does not present a risk of environmental harm
Water approvals	G3	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Bushfire	J4	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Bushfire	J4	The risk of bushfire and impacts to the community, environment and infrastructure has been addressed as part of rehabilitation
Ecological rehabilitation	J4	The vegetation composition of the rehabilitation is recognisable as the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	J4	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the target vegetation communities including PCT1329/NA237, PCT1383/NA226, PCT 1313/NA228, PCT88/NA179 and/or PCT27/NA219.
Ecological rehabilitation	J4	The vegetation composition of the rehabilitation is recognisable as, or is trending towards the target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	J4	Final Landform is safe for future use
Ecological rehabilitation	J4	The vegetation structure of the rehabilitation is recognisable as, or is trending towards the

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
		target vegetation communities, including PCT78/NA193, PCT1313/NA228, PCT1381/NA165, PCT1307/NA224, PCT1380/NA163 and/or PCT610/NA245.
Ecological rehabilitation	J4	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Ecological rehabilitation	J4	Final Landform is safe for future use
Ecological rehabilitation	J4	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	J4	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Ecological rehabilitation	J4	Levels of ecosystem health have been established that demonstrate rehabilitation ecosystem health is consistent with reference sites in neighbouring Leard State Forest
Groundwater	J4	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	J4	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Groundwater	J4	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	J4	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Land contamination	J4	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

REHABILITATION OBJECTIVE CATEGORY	SPATIAL REFERENCE	REHABILITATION OBJECTIVES
Land contamination	J4	There is no residual soil contamination onsite that is incompatible with the final land use or that poses a threat to the environment.
Landform stability	J4	Safe, stable and non-polluting.
Landform stability	J4	Landform generally blends in with the surrounding landscape.
Landform stability	J4	Safe, stable and non-polluting.
Landform stability	J4	Landform generally blends in with the surrounding landscape.
Water approvals	J4	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Water approvals	J4	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take
Ecological rehabilitation	J5	Levels of ecosystem function have been established that demonstrate the rehabilitation is self-sustainable.
Groundwater	J5	Impacts to the groundwater regime are generally within range predicted within the Project environmental assessment documentation
Groundwater	J5	Groundwater quality meets the requirements of SSD 09_0182 and does not present a risk of environmental harm.
Water approvals	J5	Structures that take or divert water such as final voids, dams, levees etc. are appropriately licensed (e.g. under the Water Management Act 2000) and where required ensure sufficient licence shares are held in the water source(s) to account for water take

APPROVED REHABILITATION OBJECTIVES STATEMENT

ROBJ0001211 | Boggabri Coal

